



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 361 Const Calendar Day: 372 Date: 11-Jun-2013 Tuesday
 Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 am 05:00 pm Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 55 - 60 12 PM 4PM 60 - 66
 Precipitation Condition Partly cloudy

Working Day If no, explain:

Diary:

Dispute

Work description.

06/11/2013
 Diary Tuesday June 11, 2013

Cable Work:

The ABF crew stopped the removal and disassembling of the W-line suspender bracket platforms, which has been started from the West end.

Painters are continuing the paint work on the split collars and suspender brackets of the W-line after necessary washing and applying the anti rust paint at the damaged spots before application of the final paint. The painting is being completed from the West toward the East. The Paint of the split collars and the suspender brackets from WPP58 to WPP74 are being completed, in that case the painting of the suspender cables, Split collars, and suspender brackets of the W-line is completed.

Other non- related cable work:

The ABF subcontractor is continuing the sand blasting of the deck. The sand blast of the whole deck is being continued from the West end of the E-line toward the East, the prime paint is applied immediately after sand blasting. The deck sand blasting and the prime paint is completed up to the EPP108 and the deck cleaning is done up to the end of SAS.

The painters started cleaning of the SAS deck starting from the West end of the W-line.

The ABF crew continues working on the North side barrier of the E-line at Pier W2 and setting up the sliding steel barrier at Hinge K. The concrete at the light pole position and other barriers are not poured yet. The ABF subcontractor involved in putting the polyester concrete overlay is continuing the trimming of the previous work.

The ABF crew are mainly involved in installing the SAS pipe barriers (Posts) either at the cross beams or remaining of the deck pipe barriers (Posts) at the South East end of the W-line. The tensioning of the post bolts is being supervised by Caltrans.

The final cables of the SAS deck pipe barriers (Posts) are being put in place, a cable with white the plastic cover.

The work on retrofitting the Pier E2 shear keys is being continued.

Prepared by: Abbas Iranmanesh

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 361

Date: 11-Jun-2013 **Tuesday**

Attachment

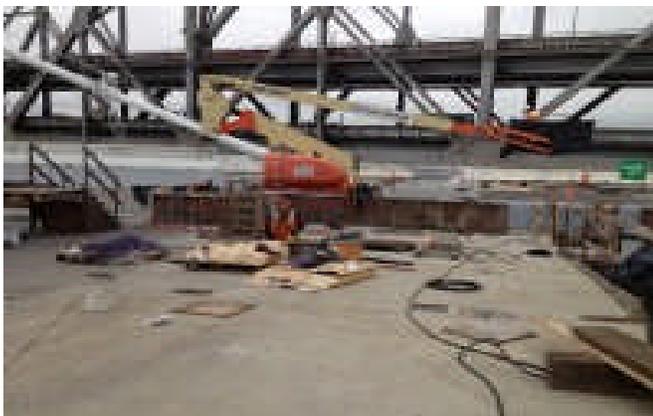

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 361

Date: 11-Jun-2013

Tuesday

