



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 047 Const Calendar Day: 387 Date: 26-Jun-2013 Wednesday
 Inspector Name: Gagnier, Pamela Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 AM 07:30 PM Break: Over Time:
 Federal ID:
 Location:
 Reviewer: Jefferson, Paul Approved Date: 11-Apr-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM
 Precipitation Condition

Working Day If no, explain:

Diary: Dispute

E2 Shear Key Modifications

CCO 325 - Conco - Don McDowell (Carpenter FM - 8 hours), J.D. Freeman, Ralph Gomez, Robert Garcia, Ricky Valenzuela, Danny McDowell all Carpenters. Everyone worked 8 regular hours unless otherwise noted.

Today Conco continues drilling #25 dowels. They also continue drilling holes for vertical soffit dowels at E2E south side and north side.

CCO 327 - ABF - See M. Bruce and B. Wolcott for ABF Labor, Equipment and Remarks.

CCO 314 - ABF - See B. Brignano's diary for ABF Labor, Equipment and Remarks.

CCO 319 - In Place Machining (NPM) - 3 workers - T. Rouse (Tech), D. Odee (Tech), S. Mentovay (Tech) - 8 Reg Hrs and 4 OT Hrs. Today IPM is mounting the drilling template and start drilling holes on the north side of E2E and setting up to start machining the west face of E2E.

Inspectors Remarks:

DJV - requested pictures of vertical PT layout measurements to cored holes at E2E west face. I took photos and provided to DJV. See attached photos.

CCO-314 Bid Item: 001 0-RRR-EFA.314 E2 Remove, Replace & Test Rods
 AMERICAN BRIDGE/FLUOR, A JV

Labor								Dispute
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	BYRON SMITH	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOHN DUSKIN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	RONNY CHAMBERLAIN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	CHRISTOPHER BISKNER	0.00	0.00	0.00	0.00		<input type="checkbox"/>

CCO-327 Bid Item: 001 0-FIS-ELS.327 Pier E2 Falsework/Install Saddle
 AMERICAN BRIDGE/FLUOR, A JV

--	--	--	--	--	--	--	--	--

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 047

Date: 26-Jun-2013

Wednesday


Attachment



E2E West 3rd from Bottom TCT - Vert Tendon



E2E West Bottom TCT - Vert Tendon

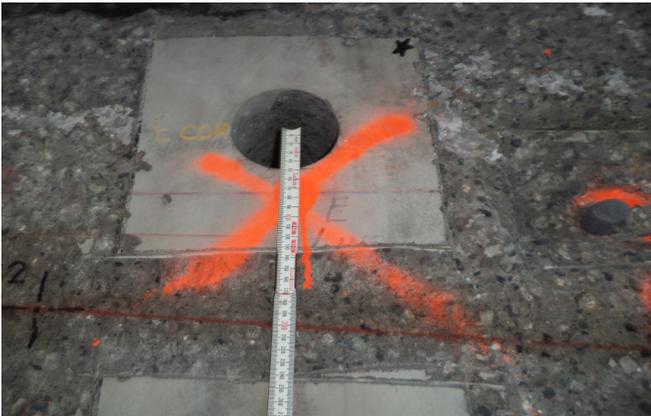

E2E West 5th from Bottom TCT - Top Draped



E2E West 2nd from Bottom TCT - Vert Tendon



E2E West 4th from Bottom TCT - Vert Tendon



E2E Bottom Hole

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 047

Date: 26-Jun-2013

Wednesday

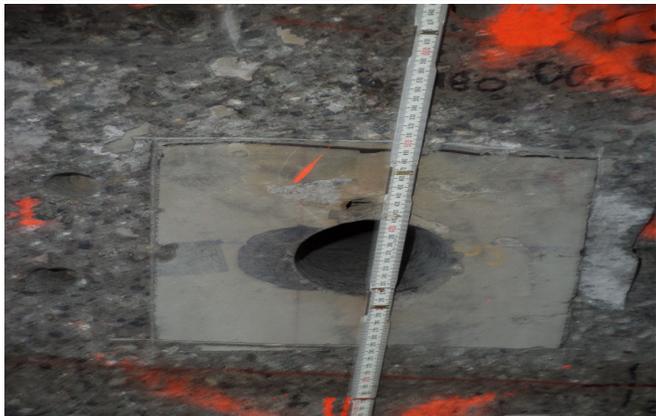

E2E West 4th from Bottom TCT - Between Draped



E2E West 3rd from Bottom TCT - Below Bottom Draped



E2E West 5th from Bottom TCT - Vert Tendon
