



### SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 10:19 AM

## Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 129 Const Calendar Day: 507 Date: 24-Oct-2013 Thursday

Inspector Name: Gagnier, Pamela Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: Over Time:

Federal ID:

Location:

Reviewer: Jefferson, Paul Approved Date: 23-May-14 Status: Approved

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

### Weather

Temperature 7 AM 12 PM 4PM  
Precipitation Condition

Working Day  If no, explain:

### Diary:

Dispute

#### E2 Shear Key Modifications

CCO 328 - HARRIS SALINAS

E2W East -

Today HS finished back wall, middle wall upper horizontals and all vertical mid layer. They also installed Layer A PT ducts and inner draped DL2 and DL3. Also they installed all north and south end U rebars. Also top longitudinal and through cap tendon spirals.

CCO 329 - CONCO

Today Conco continues to erect form panels for E2W West  
Also Conco formed E2E north east lower saddle (1st lift) for Monday grouting.

CCO 327 - ABF

E2W - Today Adam Reeve injected Simpson epoxy between upper saddle and shear key base at SK1 SE, NW and NE locations. SW was previously completed.

I worked 2 hours overtime covering field activities.

CCO-328 Bid Item: 001 0-BRS-ELS.328 Pier E2 Bar Reinforcing Steel

HARRIS SALINAS REBAR

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: HARRIS SALINAS REBAR								
Ironworker	JNM	ALFREDO CORPUS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	VILLASENOR GUELLERMO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	ZAVALA ALONZO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER GODOY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DOUG WALLACH	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	JUAN ROBLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DANIAL MONTES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JAIME MONTES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DANIAL GUDINO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	HECTOR LEON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	SIMON MARTINEZ	8.00	2.00	1.00	11.00		<input type="checkbox"/>

## Daily Diary Report by Bid Item

Job Name: 04-0120F4    Inspector Name: Gagnier, Pamela    Diary #: 129    Date: 24-Oct-2013    Thursday

CCO-329    Bid Item: 001    0-PCC-ELS.329    Pier E2 Place Concrete

CONCO PUMPING

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> CONCO PUMPING								
Semi-Skilled Laborer	JNM	ARTURO SEGURA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	WENDELL STEPHENS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Carpenter	JNM	MIKE ABARRA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Carpenter	JNM	SALVADOR MARROQUIN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Carpenter	JNM	ABRAHAM RUELAS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Carpenter	FOR	JAMES CROTTY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Carpenter	GEN	MARK WOZNICKI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RALPH GOMEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>

**Attachment**



E2W - Injection of Simpson Epoxy at SK 1



E2W West - Installed Grout Vents thru forms for Draped and Through Cap Tendons



E2W - Injection of Simpson Epoxy at SK 1



E2W East - Through Cap Tendon Pipe

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 129

Date: 24-Oct-2013

Thursday



E2W East - Layer A Vertical Ducts




E2W East - Rebar being installed



E2W West - Conco Installing Form Panels



E2W West - Installed Grout Vents for Draped and Through Cap Tendons

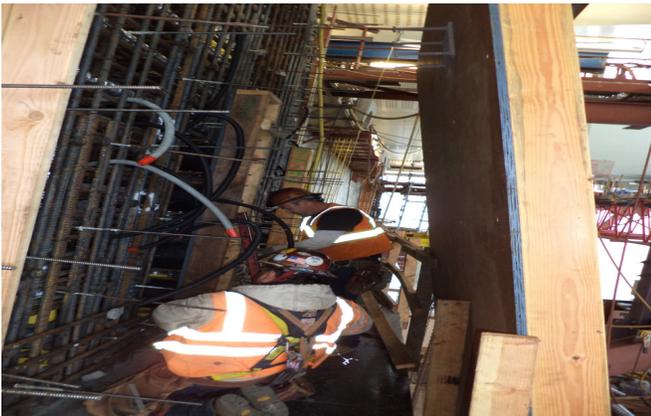

E2W West - Conco Installing Form Panels



E2W East - Layer A Vertical Ducts at Transition Coupler
