



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 221 Const Calendar Day: 582 Date: 07-Jan-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 04:30 PM 02:30 AM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 18-Jan-14 Status: Approved

Weather

Temperature 7 AM 12 PM 4PM 50 - 60
 Precipitation 0 Condition Partly Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activites

01-07-14, Tuesday, Night Shift: 4:30 PM – 2:30 AM, Partly Cloudy, 61/43 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

* Arrived at Burma SAS office around 04:30 PM. Saw Bob, Robert & Brain. Prepared paper work & called Ed (METS) to find the field status. Talked to Laraine as well, she told me she will send me the spreadsheet to fill out the work status on night shift.

* Talked to Ed Leach (METS) at connex, he told me welder Donald will be in day shift & new weld's name is Brendon Chapman. Took boat (By Justin) to tower with Ed (METS) and went inside the base V-T-L-M area.

* Welder, Mike Jimenez (Forman), continued welding at location J / Face B.

* At location N/ Face A exaction /grinding done by Chris at y = 520-730 & y = 290-390. QC (JR) & QA (James) performed MT at this location (ok).

* New welder Brendon worked on grinding at location V / Face B. QC (JR) & QA (James) performed MT. later on, QA (Jesse) and QA (Ed) performed UT on location V / Face A & B and results were OK.

* Welder Ma performed grinding at location T / Face A.

* MT/UT were OK at location E (Y = 6000 - 9730), face A by QA/QC.

* QC, Jesse & Bonifacio worked 10 hours in this shift, respectively.

* Shift ended at 02:30 AM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor							Dispute	
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	BRENDON CHAPMAN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 221 **Date:** 07-Jan-2014 **Tuesday**

Equipment	Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00			<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00			<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00			<input type="checkbox"/>
Contractor: AMERICAN BRIDGE/FLUOR, A JV									
	*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
	*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
	*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
	2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
	2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>

Attachment




Ma performed grinding on location T / Face A area



QA Jesse & QA Ed performed UT at location V / Face A



Welding done on location V / Face A

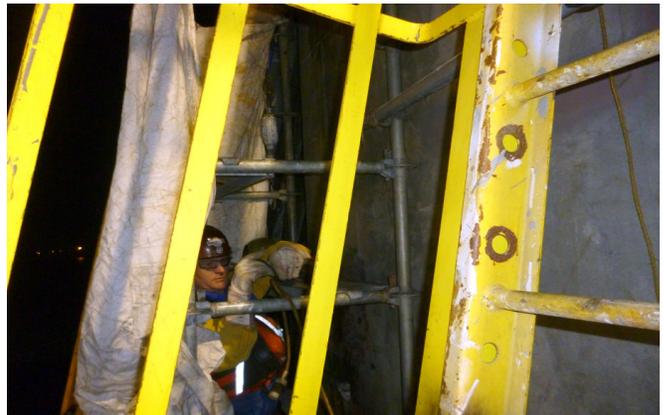

New welder Brendom performed grinding on location V / Face B area
