



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 230 Const Calendar Day: 593 Date: 18-Jan-2014 Saturday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 02:00 PM 10:30 PM Break: 00:30 Over Time: 08:00

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

**Weather**

Temperature 7 AM 12 PM 4PM 60 - 70  
 Precipitation Condition Mostly Clear

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activites**

01-18-14, Friday, Night Shift: 4:30 PM – 2:30 AM, Mostly Clear, 62/50 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

\* Arrived at Burma SAS office around 04:30 PM. Saw Bob & Mohammad at office, later on Jason Wilcox visited office. Mohammad told me, W2 area will be closed next week, no more driving parking area available, only way to Tower base is take boat from pier 7 to Tower. Prepared paper work and went to field.

\* At field, saw ABF safety officer Greg and boat operator Justin. At the field office, talked to QA-Ed Leach & James (METS) to find out the field status.

\* QC (SE), Salvador Merino and Patrick Swain were on duty tonight.

\* Welder Mike Jimenez (Forman) was running around for assigning work to the staff.

\* Welder Chris Bowles completed welding work on W / Face A area. He also completed welding work on location K / Face B, and performed grinding on W / Face A area through the shift.

\* Brendon Chapman does not work this shift.

\* Jose Torres continued & completed last night excavating work on N/Face A & B and grind on P/Face B work. He performed grinding and welding on location N / Face B area tonight.

\* Reggie Humphrey completed welding work on F / Face B area. He continued welding on location B / Face A area. QA (Ed) & QC (Patrick) performed VT on this welds.

\* Welder Man Chun Ma performed grinding on location K / Face B through the whole shift.

\* QA (Ed) performed UT on P / Face B area with QC Salvador (from last night work).

\* QA James Doe came in at 10:30 AM & left field at 7:00 PM today - 8 hours work.

\* See QA's reports (Ed Leach and James Doe) for welder's detailed activities.

\* QC Salvador Merino and Patrick Swain worked 8 hours tonight.

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 230

Date: 18-Jan-2014 Saturday

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Safety Coordinator	OTH	GREG ANDERSON	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	8.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	8.00	0.00	8.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	8.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	8.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	8.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	8.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	8.00	0.00	0.00			

**Attachment**



Entrance to K / Face B area, Ma was grinding at this area



Tower Base at the time around 6:45 PM

## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 230

Date: 18-Jan-2014

Saturday

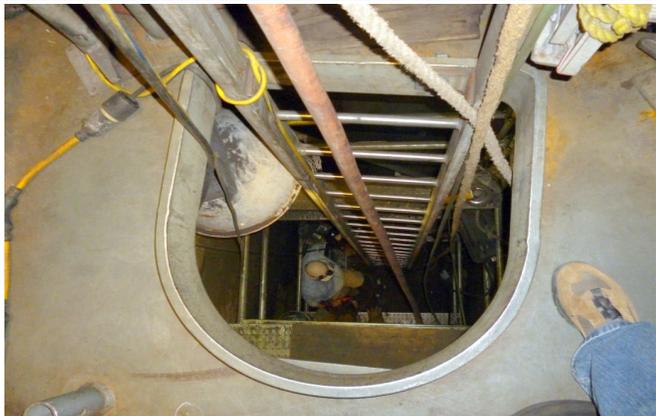

QC (Patrick) also performed VT at B / Face A area



QA (Ed) performed VT at B / Face A welding
