



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 232 Const Calendar Day: 596 Date: 21-Jan-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 04:30 PM 02:30 AM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

Weather

Temperature 7 AM 12 PM 4PM 60 - 70
 Precipitation Condition Mostly Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activites

01-21-14, Tuesday, Night Shift: 4:30 PM – 2:30 AM, Mostly Cloudy, 64/42 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

- * Arrived at Burma SAS office around 04:30 PM. Saw Bob & Robert at office, prepared paper work and went to field.
- * At field, saw ABF safety officer Greg and boat operator Justin. At the field office, talked to QA-Ed Leach & James (METS) to find out the field status.
- * QC (SE), Salvador Merino and Patrick Swain were on duty tonight.
- * Welder Mike Jimenez (Forman) did not perform any welding yet, he was in different places helping other welders work. Later on he performed grinding on S4 – S6 area tonight.
- * Welder Chris Bowles performed welding work on N / Face B area through the whole night.
- * Brendon Chapman performed welding on R5, at Y = 3800 - 4050 location.
- * Jose Torres performed excavation on location K area tonight.
- * Reggie Humphrey performed excavation on multiple locations. He also performed welding on location F and H tonight.
- * Welder Man Chun Ma performed grinding on location J / Face B area through the whole shift.
- * QC (Patrick) and QA (Ed) performed UT on weld W / Face A, at Y = 320 – 1900 area today. Ed also did UT on N2 area. Later on, QA (Ed) performed UT on W / Face B area.
- * QA (James) work schedule went back to the normal time 4:30 PM to 2:30 AM tonight.
- * See QA's reports (Ed Leach and James Doe) for welder's detailed activities.
- * QC Salvador Merino and Patrick Swain worked 10 hours tonight.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 232

Date: 21-Jan-2014

Tuesday

Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Safety Coordinator	OTH	GREG ANDERSON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Equipment							Rental Company	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>	
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>	
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>	
2292	WELDER, 600 AMP					No	<input type="checkbox"/>	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>	
2293	WELDER, 600 AMP					No	<input type="checkbox"/>	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>	

Attachment



Reggie performed welding at F area



Brendon performed welding on R5 area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 232

Date: 21-Jan-2014


Tuesday



Ma performed grinding on J / Face A area



Mike performed grind on S4-S6 area, Brendon performed welding with QA (Ed)

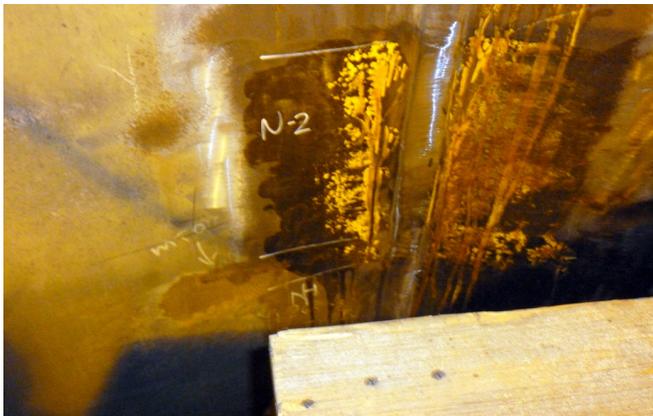

QA (Ed) performed UT on N2 area



QA (Ed) performed UT on W / Face A area



QA (Ed) performed UT on W / Face B



QA (Ed) performed UT on W / Face B
