



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 240 Const Calendar Day: 605 Date: 30-Jan-2014 Thursday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

Weather

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60
 Precipitation Condition Mostly Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower activites

01-30-14, Thursday, Day Shift: 07:00 AM – 05:30 PM, Mostly Cloudy, 60/54 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications.

* Arrived at Burma SAS office around 07:00 AM. Attended safety meeting and respirator fit test class this morning. Went to field afternoon.

* Talked to QA - Simion Ramirez (METS) & Joe Adame to find out the field status. Saw Semi at field office.

* QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. JR worked on E2 instead of Tower Base today, QA Simiom also worked in E2 with JR today.

* Welder Richard Garcia (Forman) performed Forman's duty this morning, and excavating on H / Face A, Y = 9200 - 9300 area. Later on, he performed excavating on D / Face A at Y = 6200 - 6500 area through the shift.

* Welder Donald Plumb was work on E2 instead of Tower Base area, but he came back to tower after 3:30 PM for two hours work on ESW repair work, Same as QC JR.

* Zachariah Macdonald performed grinding on D / Face A, Y = 1000 - 5800 area, at 1:45 PM the light was off on this area, Paul & Richard were helping Zach to obtain the light back.

* Paul Fambrini performed misc. works just like yesterday.

* Guowu Chen performed grinding on D / Face B at Y = 1000 - 5800 area, back to back to Zach working location. QC Bernie & QA Joe performed UT on this area. QC - Bernie also performed UT on N / Face B at Y = 300 -6000 area.

* Welder Randy Clayborn was sick and not here today.

* Welder Ernest Connors performed excavating on F / Face A (Y = 4055 - 5050) area this morning. He left from field around 12:30 today.

* See QA's reports (Joe Adame) for welder's detailed activities.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 240

Date: 30-Jan-2014 Thursday

* QC Bonifacio Daquinag (JR) worked 2 hours, and Bernie Docena worked 10 hours in ESW repair work today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	ERNEST CONNER	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	2.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>


Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Rental Company	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>

Attachment



Fender system on Tower Base

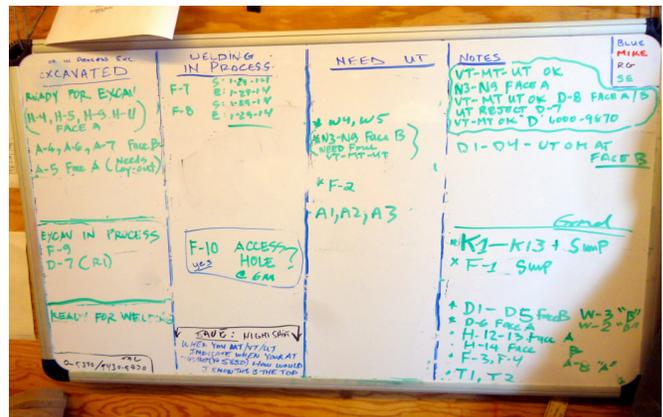

Work status for ESW repair works

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 240

Date: 30-Jan-2014

Thursday

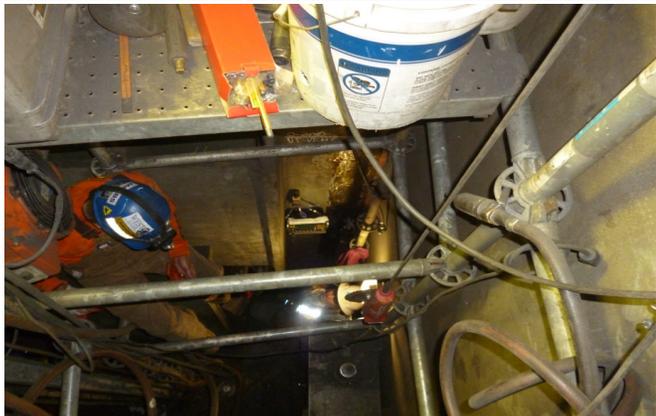


QA (Joe) & QC (Bernie performed UT testing on F / Face A area



Guowu and QC (Bernie) on D / Face B area



Welding on F9 / Face A area

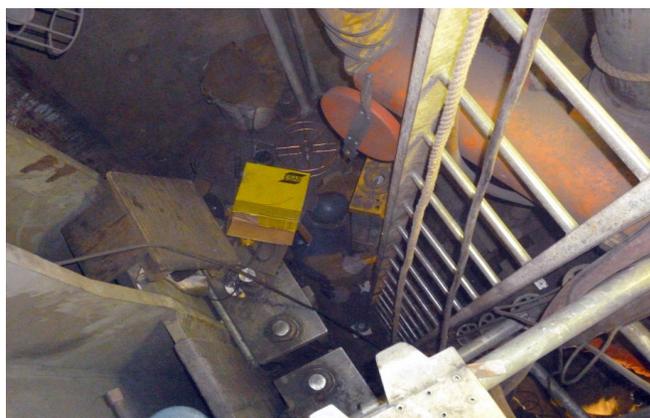

Zac performed grinding on D / Face A area
