



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 241 Const Calendar Day: 606 Date: 31-Jan-2014 Friday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60
 Precipitation Condition Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activitie

01-31-14, Friday, Day Shift: 07:00 AM – 05:30 PM, Mostly Cloudy, 60/54 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications.

- * Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,
- * Talked to QA - Simion Ramirez (METS) & Joe Adame to find out the field status. Saw Semi at field office.
- * QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. JR worked on E2 instead of Tower Base today, QA Simiom also worked in E2 with JR today - same as last few days. QC - Bernie performed VT / UT on N / Face B area with QA Joe.
- * Welder Richard Garcia (Forman) performed Forman's duty today.
- * New welder Kyle Clowley performed grinding on T / Face A & B preparing for MT / UT later on.
- * Welder Donald Plumb was work on E2 instead of Tower Base area, but he came back to tower after 3:30 PM for two hours work on ESW repair work, Same as QC JR.
- * Zachariah Macdonald performed grinding on H14 / Face B preparing for repair.
- * Paul Fambrini performed misc. works (such as preheat pad installation) just like yesterday.
- * Guowu Chen performed grinding on F9 / Face A at Y = 5700 area and H14 / H16 locations as well.
- * Welder Randy Clayborn was not in tower base today.
- * Welder Ernest Connors performed excavating on H / Face A (around Y = 9200) area. He also performed excavating on A6 & 7 / L1-L3 area today.
- * Welder Eric Sparks performed ESW Test Sample preparation work on pier 7 for 8 hours today
- * See QA's reports (Joe Adame) for welder's detailed activities.
- * QC Bonifacio Daquinag (JR) worked 2 hours, and Bernie Docena worked 10 hours in ESW repair work

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 241

Date: 31-Jan-2014 Friday

today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV


Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	2.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			

Attachment

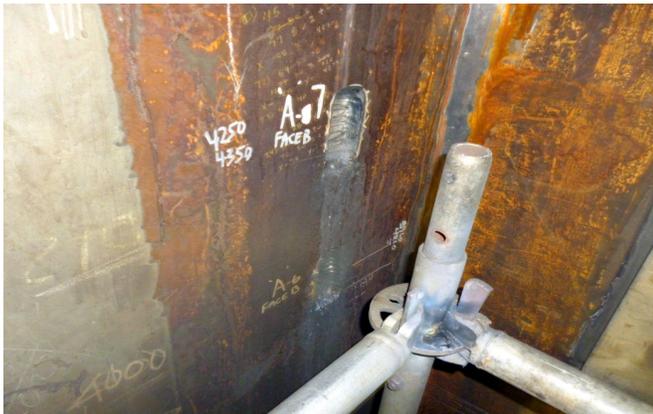

Excavating / grinding on A7 / Face B area



Pro-heat pad on F6 - F9 area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 241

Date: 31-Jan-2014


Friday



Welding on D7 / Face B area



Excavating / grinding on H14 / Face B area

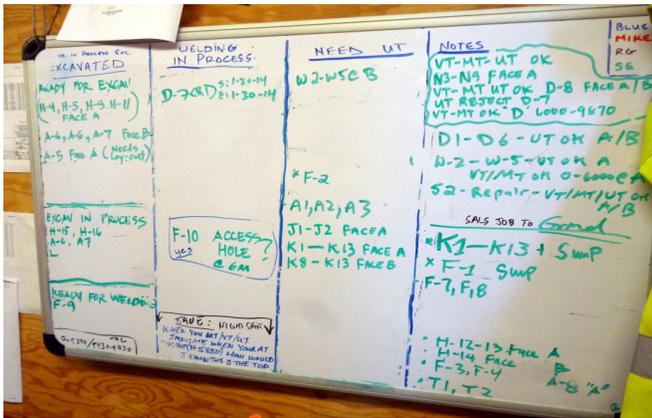

Work progress on the board



Excavating on L5 area
