



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 243 Const Calendar Day: 610 Date: 04-Feb-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

Weather

Temperature 7 AM 40 - 50 12 PM 40 - 50 4PM 50 - 60
 Precipitation Condition Partly Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activites

02-04-14, Tuesday, Day Shift: 07:00 AM – 05:30 PM, Mostly Cloudy, 60/54 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications.

- * Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,
- * Talked to QA - Joe Adame (METS) to find out the field status.
- * QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. JR worked on E2 instead of Tower Base today, QA Simiom have different shift time schedule - from 12:00 PM to 10:30 PM today. Saw ABF QC - Chris Chew today.
- * Welder Richard Garcia (Forman) was not in tower base today, Eric Sparks was here rplacing Richard's forman duty.
- * Welder Kyle Clowley was not here today.
- * Welder Donald Plumb performed excavating on G / Face A area, and welding later on.
- * Zachariah Macdonald performed grinding welds on B / Face B area for UT testing later on.
- * Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing) as usual.
- * Guowu Chen performed grinding on F / Face A area and A / Face B area as well.
- * Welder Randy Clayborn was not in tower base today (at E2).
- * Welder Ernest Connors excavating on L / Face A area.
- * Welder Eric Sparks spent 5 hours installed cutting equipment on V / Face B area (CCO 366) today.
- * Bernie performed MT on G / Face A location today.
- * See QA's reports (Joe Adame) for welder's detailed activities.
- * QC Bonifacio Daquinag (JR) worked 0 hours, and Bernie Docena worked 10 hours in ESW repair work

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 243

Date: 04-Feb-2014 Tuesday

today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	3.00	2.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 243


Date: 04-Feb-2014

Tuesday

Donald performed excavating and welding on G / Face A area



Pro-heat pad on L / B location

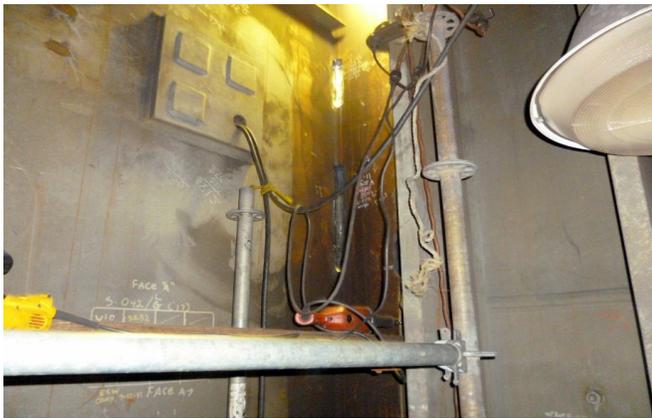


Ray performed excavating on L / Face A area



Chen performed grinding on F / Face A area



Pro-heat pad on A / Face A area

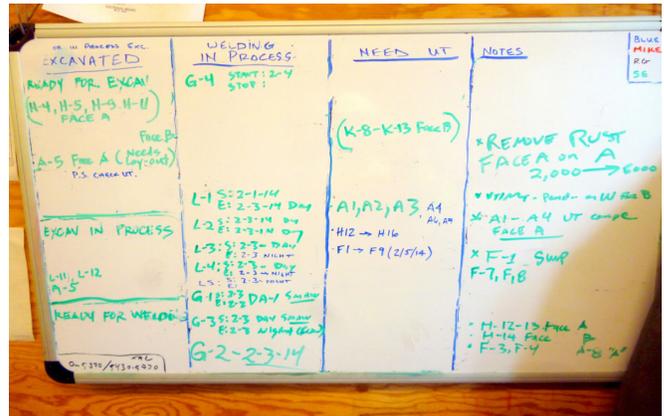

Work progress on the board
