



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 244 Const Calendar Day: 611 Date: 05-Feb-2014 Wednesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 40 - 50 4PM 40 - 50
 Precipitation Condition Partly Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activities

02-05-14, Tuesday, Day Shift: 07:00 AM – 05:30 PM, Mostly Cloudy, 56/45 F

- *** Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications ***
- * Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,
- * Talked to QA - Joe Adame (METS) to find out the field status.
- * QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. JR was back to Tower Base work today, QA Simiom have different shift time schedule - from 12:00 PM to 10:30 PM today, he worked on ESW TI repair work today. Saw ABF QC - Chris Chew at barge.
- * Welder Kyle Clowley performed excavating on M / Face B area today.
- * Welder Donald Plumb performed excavating on A / Face A area (4 hrs and 6 hrs on CCO 366 work),
- * Zachariah Macdonald performed grinding welds on B / Face B area for UT testing later on.
- * Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing - 4 hrs and 6 hrs on CCO 366 works).
- * Guowu Chen performed grinding on F / Face A area as well.
- * Welder Randy Clayborn performed welding on L / Face A area.
- * Welder Ernest Connors excavating on H / Face B area.
- * Bernie performed MT on A & K / Face B locations, and JR on A and L locations. QA (Joe) worked MT on K / Face B area.
- * See QA's reports (Joe Adame) for welder's detailed activities.
- * QC Bonifacio Daquinag (JR) worked 10 hours, and Bernie Docena worked 10 hours in ESW repair work today.
- *** CCO 366 - ESW Test Sample ***

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 244

Date: 05-Feb-2014

Wednesday

* Richard Garcia (Forman) and Eric Sparks started setting up the cutting machin on V / Face B area this morning for ESW Test Sample.

* Kent Aaron, Ethan and Julient were helping Richard to set-up the equipment V (Face A) to make sure the cutting was aligned with plan.

Richard and Eric worked 10 hrs on CCO work, and
Aaron Kent worked 2 hours
Ethan Kent & Julient Paulk worked 4 hours on this CCO work.

Two side lines of test sample have been cut today (see Pictures), top and bottom radius lines were not cut yet. ABF still try figure how to cut the curve through the cutting machin.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JULIENT POULK	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	ETHAN KENT	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 244

Date: 05-Feb-2014

Wednesday

Attachment




Randy performed welding on L / Face A area



Four holes have been drilled on test sample



QA (Joe) performed MT on K / Face B with Chen

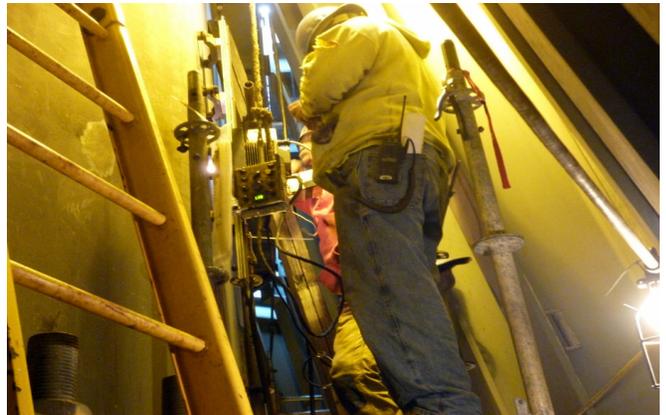

Richard & Eric performed cutting ESW Test Sample V / Face B area



Randy performed grinding on L / Face A area



Test Sample back on V / Face A area
