



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 246 Const Calendar Day: 613 Date: 07-Feb-2014 Friday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time: 00:00  
 Federal ID:  
 Location:  
 Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60  
 Precipitation Condition Cloudy to rain

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activitie**

02-07-14, Friday, Day Shift: 07:00 AM – 03:30 PM, Cloudy to Rain, 55/51 F

- \*\*\* Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications \*\*\*
- \* Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,
- \* Talked to QA - Simion Ramirez (METS) to find out the field status.
- \* QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. QA (Joe) was not here today. Saw ABF QC - Chris Chew at barge.
- \* Welder Kyle Clowley performed grinding / excavating on L / Face A area today.
- \* Welder Donald Plumb assisted Paul to mobilize the equipment around the welding area.
- \* Zachariah Macdonald performed grinding welds on G / Face B area.
- \* Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing - 4 hrs and 6 hrs on CCO 366 works).
- \* Guowu Chen performed grinding on K / Face A area as well.
- \* Welder Randy Clayborn performed welding on L / Face A area.
- \* Welder Ernest Connors excavating on M / Face A area.
- \* Bernie performed UT on K / Face A & B locations, and JR performed MT on H2 (for Excavation) locations.
- \* See QA's reports (Simion Ramirez) for welder's detailed activities.
- \* QC Bonifacio Daquinag (JR) worked 8 hours, and Bernie Docena worked 8 hours in ESW repair work today. Tower Base was out of power on 2:00 Pm, Rain was getting havier that time, crew left field at 3:00 Pm, worked 8 hours today.
- \*\*\* CCO 366 - ESW Test Sample \*\*\*

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4

**Inspector Name:** Liu, Tai-Lin

**Diary #:** 246

**Date:** 07-Feb-2014 **Friday**

\* Richard Garcia (Forman) and Eric Sparks continued cutting the test sample on V / Face B area this morning. Used manual torch to cut top & bottom radius lines (see pictures) up to around 10:00 am. Julient Paulk helped Richard & Eric to remove the sample from the wall until 10:30 AM, Jonathon Biskner was on the back of the sample (V / Face A area) to make sure the cuts were aligned with the plan and help to detach the sample from wall. Then the sample was uploaded to the skirt area and download it to the outside tower base around 11:00 AM. Crew were cleaning the area and removing equipment from the area V / Face B. At 2:00 PM, the tower base area was out of power and sample was sent to pier 7. Crew were left from site at 3:00 PM, worked 8 hours today.

\* Richard and Eric worked 8 hrs on CCO work.

\* Julient and Jonathon worked 8 hrs on CCO work today.

\* Helper Kent Aaron & Keller Jeffrey (boat operator) worked 4 hours on this CCO works.

\*\* Back to office around 3:30 Pm, wrote the diary and loaded pictures (and video for cutting the test sample), and left office around 4:30 PM.

**04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	JNM	JEFFREY KELLER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	JULIENT POULK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	JONATHON BISKNER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 246

Date: 07-Feb-2014

Friday

2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00		

## Attachment




Richard & Eric performed hand torch cutting the radius lines



QA (Simion) watched Test Sample cutting operation



Julient helped Richard & Eric to remove sample from wall

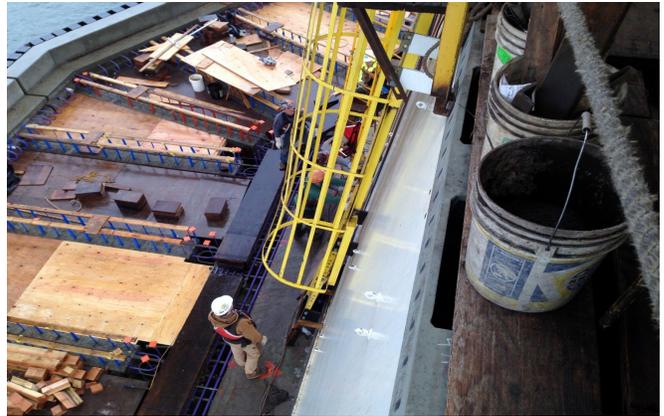

Unload sample plate from skirt area to bottom of Tower Base



Three welders performed cutting test sample on V / Face B area
