



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 253 Const Calendar Day: 624 Date: 18-Feb-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

Weather

Temperature 7 AM 50 - 60 12 PM 60 - 70 4PM 60 - 70
 Precipitation Condition Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activities

02-18-14, Tuesday, Day Shift: 07:00 AM – 05:30 PM, Cloudy, 63/50 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

- * Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,
- * Talked to QA - Simion Ramirez (METS) to find out the field status. QA - Joe Adam was not here today, Simon told me that Joe will come back tomorrow.
- * QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today.
- * Kyle Clowley and Randy Clayborn were working on Skirt Welding work instead of ESW weld repair work.
- * Welder Donald Plumb performed excavating on H / Face B area this morning and excavating on G / Face A this afternoon - took over from Eric..
- * Zachariah Macdonald was helping Paul to mobilize the equipment and helped Plumb for excavating on H / Face B area..
- * Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing).
- * Guowu Chen performed grinding / excavating on M / Face B area.
- * Eric performed excavating / welding on G / Face A area this morning and left field after lunch..
- * Welder Ernest Connors performed excavating on V / Face B below test sample hole,
- * Richard was not in today.
- * JR was watching welds G & H, and Bernie was watching welds V & M today. No MT and UT performed on this shift.
- * See QA's reports (Simion Ramirez) for welder's detailed activities.
- * QC Bonifacio Daquinag (JR) and Bernie Docena worked 10 hours today.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 253

Date: 18-Feb-2014 Tuesday

(2). CCO 366 - ESW Test Sample ***

* NO work for this CCO work today.

(3). Tower Fender System Cast-in-place concrete work

* Stanley asked me to check the stay form cleaning work starting or not. At field, nobody worked on that work yet. Sami was back on this work today. He will cover the work from now on.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>

Attachment

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 253

Date: 18-Feb-2014

Tuesday



Chen performed grinding on M / Face B area




Kyle & Randy performed skit welding work



Eric performed excavating on G / Face A area with Paul



Installed pro-heat pad on top of weld area

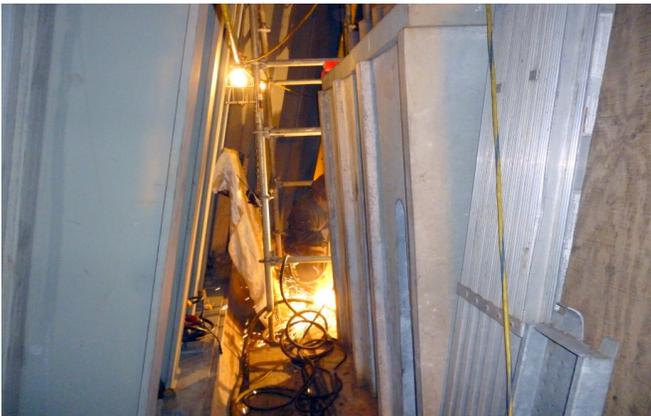

Conners performed excavating on V / Face B area



Plumb took over excavating work from Eric on G / Face A area
