



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 256 Const Calendar Day: 627 Date: 21-Feb-2014 Friday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM 60 - 70
 Precipitation Condition Partly loudy

Working Day If no, explain:

Diary:

Dispute

Tower Activities

02-21-14, Friday, Day Shift: 07:00 AM – 05:30 PM, Partly Cloudy, 64/54 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

- * Arrived at Burma SAS office around 07:00 AM. Prepared paper (CCO366 work order) work & went to field,
- * Talked to QA - Joe Adame & QC - JR & Bernie. QA Simion Ramirez (METS) was not here this morning, he showed up this afternoon. Saw Sami at job site.
- * QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today.
- * Welder Donald Plumb performed welding / griinding on K / Face A area today.
- * Zachariah Macdonald performed grinding on G / Face A area today.
- * Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing). Paul left site around 3:00 PM, worked 8 hours today.
- * Guowu Chen performed grinding on F / Face B, and G / Face A area today.
- * Eric performed helping to other welder today, he also started removing stair & scaffolding from inside tower base to barge with Richard.
- * Welder Ernest Connors performed welding / excavating on V / Face B area (See picture),
- * Richard performed welding on K / Face A area, and demo. Scaffolding with Eric.
- * QC Bernie performed UT on F / Face A & B welds, at 3 to 9 meters area,
- * See QA's reports (Simion Ramirez & Joe Adame) for welder's detailed activities.
- * QC Bonifacio Daquinag (JR) worked 10 hours today, and Bernie Docena also worked 10 hours today.

(2). CCO 366 - ESW Test Sample ***



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 256

Date: 21-Feb-2014

Friday

* NO work for this CCO work today.

Crew will work tomorrow (Saturday), Sami will cover the work.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 256

Date: 21-Feb-2014

Friday

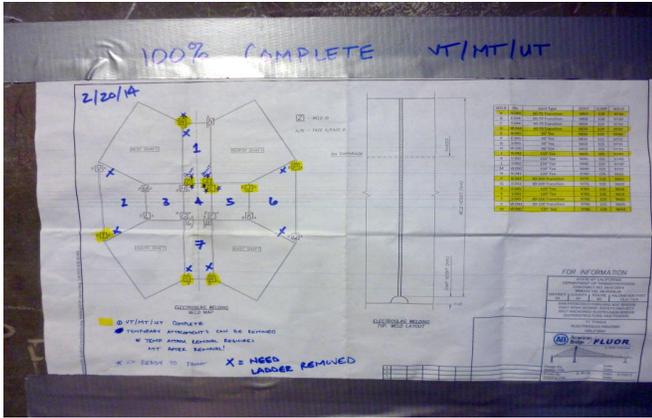


Wall attachment for ESW work progress

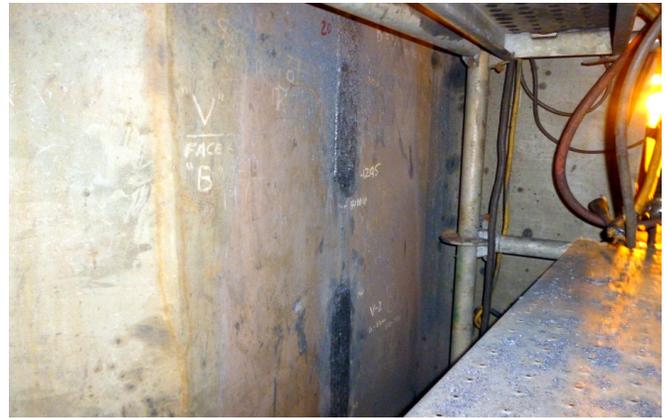


Bottom V / Face B area of welding




Excavating & welding on V / Face B area by Connors

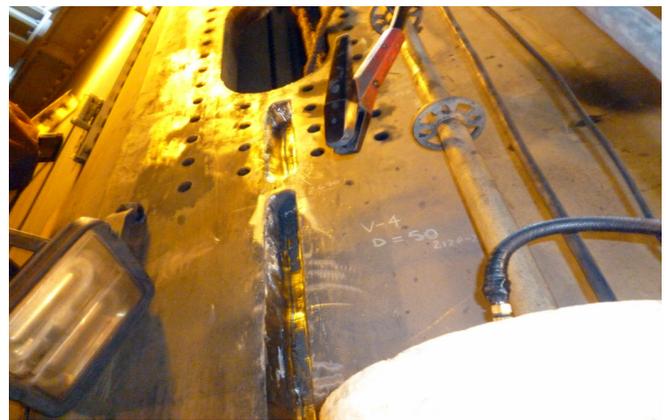

Connors performed excavating on V / Face B right below cut sample

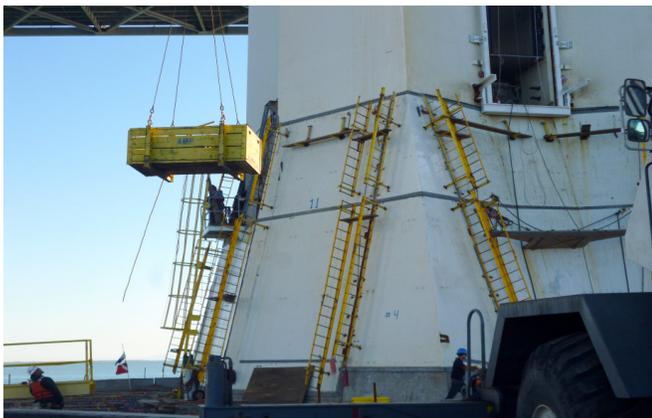

Eric performed scaffolding removal

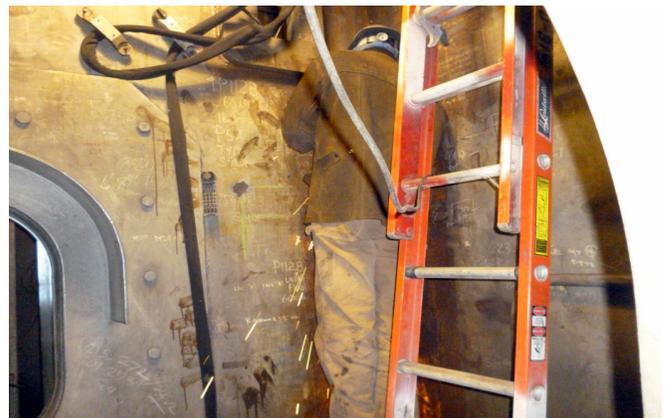

Welder performed grinding on F / Face B area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 256

Date: 21-Feb-2014

Friday



Two empty container transferred from pier7 to T1 by boat

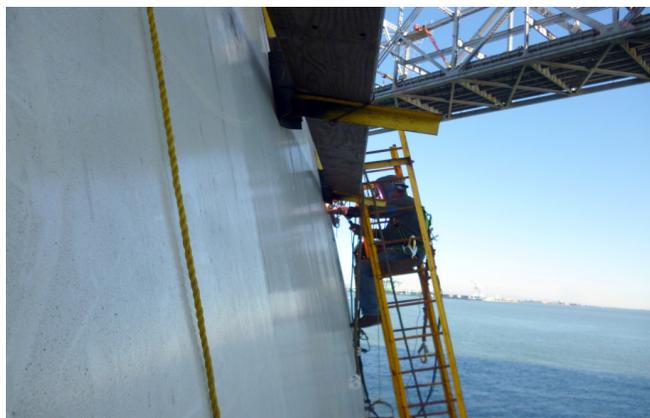

Tower skirt welding at West area
