



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 258 Const Calendar Day: 631 Date: 25-Feb-2014 Tuesday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00  
 Federal ID:  
 Location:  
 Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 60 - 70 4PM 60 - 70  
 Precipitation Condition Partly loudy

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activities**

02-25-14, Tuesday, Day Shift: 07:00 AM – 05:30 PM, Partly Cloudy, 72/58 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

- \* Arrived at Burma SAS office around 07:00 AM. Prepared paper work (CCO#366) & went to field,
- \* Talked to QA - Simion Ramirez (METS) and Joe Adame to find out field status. Talked to Sami regarding CCO 366 work order sheets in day 2/11 & 2/12 (He covered field work for me (I were attending Winter Training that two days)).
- \* QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today.
- \* Welder Donald Plumb performed grinding & repairing the welds on L / Face B & F / Face B area today.
- \* Zachariah Macdonald performed grinding on G / Face B & H / Face B area today.
- \* Paul Fambrini was not in today. .
- \* Guowu Chen performed grinding on H / Face B & F / Face A & B area today.
- \* Welder Ernest Connors continued welding / excavating on V / Face B area, he also performed grinding on bottom edge of cut out sample area (Might be CCO 366 work),
- \* QA Joe performed MT on L & G area, Simon did MT on Skirt area. QC Bernie performed UT on H / Face B area. QC (JR) performed MT on F / Face B area (see pictures).
- \* See QA's reports (Simion Ramirez & Joe Adame) for welder's detailed activities.
- \* QC Bonifacio Daquinag (JR) worked 10 hours today, and Bernie Docena also worked 10 hours today.

(2). CCO 366 - ESW Test Sample \*\*\*

- \* Connors performed grinding on bottom of cut out edge today.
- \* At Pier7, two painters (Richard Salcido & Rafael Ventura) performed blasting & prime the cut out test sample for two hours & one gel (Interzinc 22 HS) and 4 sacks (Abrasive) used.

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 258

Date: 25-Feb-2014 Tuesday

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

| Trade  | Class | Name               | RT Hrs | OT Hrs | DT Hrs | Total | Remarks | Dispute                  |
|--|-------|--------------------|--------|--------|--------|-------|---------|--------------------------|
| <b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV |       |                    |        |        |        |       |         |                          |
| Ironworker                                     | JNM   | Zach MacDonald     | 8.00   | 2.00   | 0.00   | 10.00 |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | DONALD PLUMB       | 8.00   | 2.00   | 0.00   | 10.00 |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | CHRISTOPHER BOWLES | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | APP   | JOSE TORRES        | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | MAN CHUN MA        | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | BRENDON CHAPMAN    | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Welder   | APP   | Reggie Humphry     | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Operator                                       | JNM   | JUSTIN GARRETT     | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | MICHAEL JIMENEZ    | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | FOR   | RICHARD GARCIA     | 8.00   | 2.00   | 0.00   | 10.00 |         | <input type="checkbox"/> |
| Painter  |       | RICHARD SALCIDO    | 2.00   | 0.00   | 0.00   | 2.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | PAUL FAMBRINI      | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | GUOWU CHEN         | 8.00   | 2.00   | 0.00   | 10.00 |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | RANDY CLAYBORN     | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | JNM   | ERNEST CONNER      | 8.00   | 2.00   | 0.00   | 10.00 |         | <input type="checkbox"/> |
| Ironworker                                     | APP   | KYLE CROWLEY       | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Ironworker                                     | FOR   | ERIC SPARKS        | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |
| Painter  |       | RAFAEL VENTURA     | 2.00   | 0.00   | 0.00   | 2.00  |         | <input type="checkbox"/> |
| Safety Coordinator                             | OTH   | GREG ANDERSON      | 0.00   | 0.00   | 0.00   | 0.00  |         | <input type="checkbox"/> |

**Equipment**

| Equipment ID                                   | Description       | RT Hrs | OT Hrs | ST Hrs | IT Hrs | Rental Company | Remarks | Dispute                  |
|--|-------------------|--------|--------|--------|--------|----------------|---------|--------------------------|
| <b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV |                   |        |        |        |        |                |         |                          |
| *E0020562                                      | WELDING EQUIPMENT | 8.00   | 2.00   | 0.00   | 0.00   |                | No      | <input type="checkbox"/> |
| *E0030562                                      | WELDING EQUIPMENT | 8.00   | 2.00   | 0.00   | 0.00   |                | No      | <input type="checkbox"/> |
| *E0010562                                      | WELDING EQUIPMENT | 8.00   | 2.00   | 0.00   | 0.00   |                | No      | <input type="checkbox"/> |
| 2292   | WELDER, 600 AMP   | 8.00   | 2.00   | 0.00   | 0.00   |                | No      | <input type="checkbox"/> |
| 2293   | WELDER, 600 AMP   | 8.00   | 2.00   | 0.00   | 0.00   |                | No      | <input type="checkbox"/> |

**Attachment**



# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 258

Date: 25-Feb-2014

Tuesday

Grinding on M / Face B area




QA Simon performed MT on Tower Skirt area



Tower fender crew (Conco) laid rebar on east side of fender system



Grinding on F / Face B area

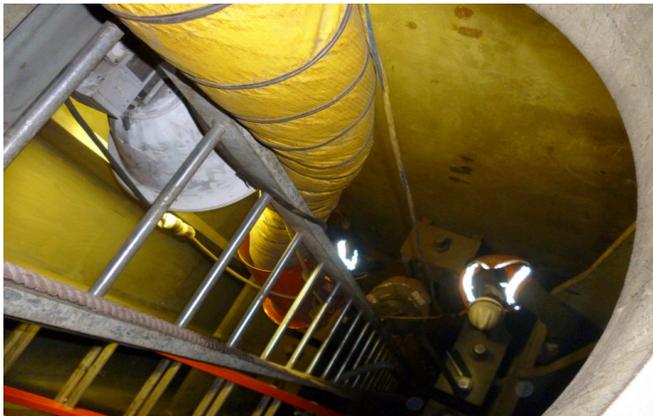

Labor performed cleaning on bottom of tower base



QC (JR) performed MT on F / face B area

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 258

Date: 25-Feb-2014

Tuesday



Ray performed grinding on V / Face B area



Grinding & welding on V / Face B area



Welder Chen performed heating up the weld area for NDT test



Grinding performed by Plume on G / Face A area



QC (JR) & Plumb checked weld on F / Face B area



Connors performed grinding on underneath of cut out area (V / Face B)
