



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 263 Const Calendar Day: 637 Date: 03-Mar-2014 Monday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

Weather

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60
 Precipitation Condition Cloudy

Working Day If no, explain:

Diary:

Dispute

Tower Activitie

03-03-14, Monday, Day Shift: 07:00 AM – 05:30 PM, Cloudy Morning & Rain afternoon, 61/53 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

* Arrived at Burma SAS office around 07:00 AM. Attended staff meeting. Prepared paper work (CCO 366 work order sheet) & went to field.

* Talked to QA - Simion Ramirez (METS) and Joe Adame to find out field status. Simion was busy for skirt work, Joe was taking care of ESW repair work

* QC (SE), Patrick Swain performed VT / MT on M / Face A area and Bernie Docena performed VT / MT & UT on skirt area, JR with Joe were in cell #4 & 5 performing MT in that area (see picture),

* Welder Mike performed grinding on cell 5 area.

* Welder Randy performed excavating & welding on M / Face A area today (see picture).

* Welder Chen performed grinding on mid - cell (#4) & N / Face A area (see picture) today.

* Paul & Jose performed pro-heat pad installation & removal, Paul also performed grinding wall on cell 4 between E & J area today.

* Welder Richard, Plume, Connors, Ma & Zack worked in other area not in ESW repair work today..

* See QA's reports (Simion Ramirez & Joe Adame) for welder's detailed activities.

* QC Patrick Swain, JR & Bernie worked 10 hours today.

(2). CCO 366 - ESW Test Sample ***

* no work on this item today.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV			

Labor							Dispute	
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 263 **Date:** 03-Mar-2014 **Monday**

Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs		Remarks
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>

Attachment



QC (JR) & QA (Joe) performed MT on cell # 4 area



Welding machine relocated to outside of tower base area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 263

Date: 03-Mar-2014


Monday



E2 temporary tower removal




Chen performed grinding on N / Face A area

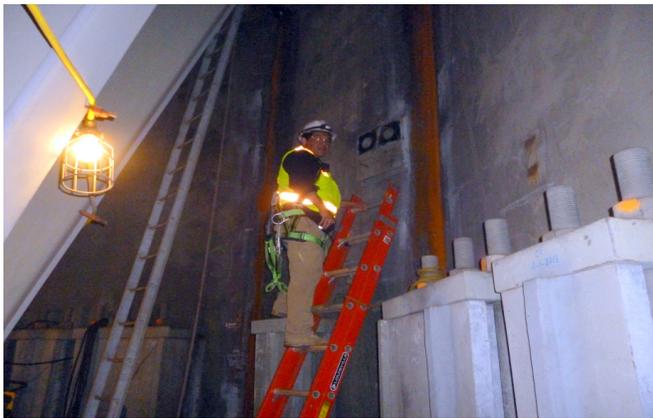

QC Simion checked grinding on bottom of tower base



View from V / Face B - test sample cut out area

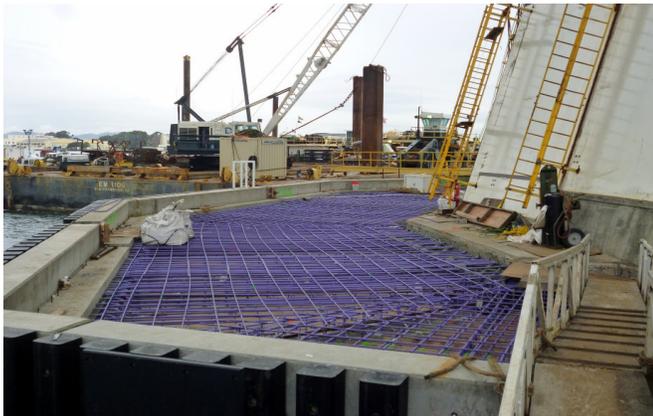

Conco performed rebar installation on west side of fender system



Randy performed grinding on M / Face A area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 263

Date: 03-Mar-2014

Monday



Paul performed grinding on cell #5 between E & J area



IRWs performed walking scaffolding & temporary tower removal on E2 area
