



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 265 Const Calendar Day: 639 Date: 05-Mar-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 60 - 70 4PM 60 - 70

Precipitation Condition Cloudy

Working Day  If no, explain:

**Diary:**

Dispute

**tower Activites**

03-05-14, Wednesday, Day Shift: 07:00 AM – 05:30 PM, Cloudy, 65/54 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

\* Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field.

\* Talked to QA - Simion Ramirez (METS) and Joe Adame to find out field status.  
 Simion watched skirt welding work same as James Dore,  
 Joe was taking care of ESW repair work

\* QC (SE), Patrick Swain performed MT on serval cells grinding area. Final repaired welds on M / Face A by Randy will be ready for Patrick UT check on tomorrow.  
 Bernie Docena performed UT on skirt area & Plumb was fixing the welds.  
 JR worked in W2 area today,

\* Welder Mike, Randy, Richard, Chen, Plumb & Paul worked in skirt area & seal plate welding work (see pictures).

\* Chen also performed grinding on top of the cut out section on V / Face B area.

\* Welder Ma & Zack were not in tower today.

\* QA (Joe) performed MT on skirt area.

\* See QA's reports (Simion Ramirez & Joe Adame) for welder's detailed activities.

\* QC (Patrick) will UT on last repaired welds on M / Face A area tomorrow.

\* QC Patrick Swain, JR & Bernie worked 10 hours today.

\* See Sami's diary for crew working hours on skirt & seal plate installation work.

(2). CCO 366 - ESW Test Sample \*\*\*

\* Certified Coating Company (CCC) performed painting on cutout setion (V / Face A & B area this afternoon (See pictures).

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 265

Date: 05-Mar-2014

Wednesday

\* Two labors: Francisco Castro & Tony Katrones worked 3 hours today..

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

**Attachment**



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 265

Date: 05-Mar-2014

Wednesday

Randy, Richard & Mike left from seal plate welding operation to take break



Crew sent in scaffolding into tower base, Conco performed rebar tie-up at below



Grinding on V / Face B area (Test Sample cut out area)



Painted area on V /Face A cut out area - CCO work



Installed paint pumping line on inside of skirt area



Seal plate welding

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 265

Date: 05-Mar-2014


Wednesday



Temporary tower removal on E2 area



Grinding welds inside the cell

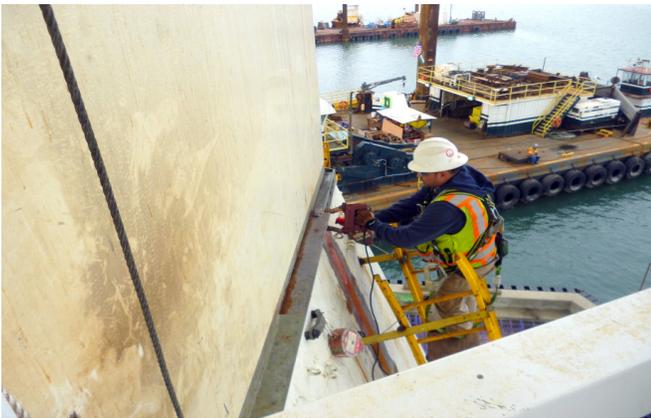

QA (Joe) performed MT on skirt area



Mike performed welding on seal plate to floor



Welders & QC worked on skirt area



Certified Coating performed painting on cut out setion (V / Face B) - CCO

---

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 265

Date: 05-Mar-2014

Wednesday

---



Guwoo Chen performed grinding on skirt area
