



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 277 Const Calendar Day: 681 Date: 16-Apr-2014 Wednesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:00 PM Break: 00:30 Over Time: 01:30

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 07-Jun-14 Status: Approved

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

04-16-14, Wednesday, Day Shift: 07:00 AM - 05:00 PM, Clear

Mohammad asked me to cover Tower base operation this afternoon dut to Tom has Doctor's appointment this afternoon.

After lunch, took boat to T1.

At tower fender slab, saw three IRWs (Regie, Richard & Paul) working on tower skirt on East side of tower. Talked to Forman Richard regarding the skirt installation operation. Total 3 IRWs worked today for 8 hours. QC Bernie was on site. He did MT testing on skirt today. QA Simion was not in site this afternoon.

Saw CCC Supervisor Jean on site. Talked to QA Joe Ullrich (METS) and CCC forman Tony Katrones. Paint crew were working on Cell 2, South Shaft, Cell 7 & and East Shaft today. Crew's name were Jorge Flores Ramero, Tony Katrones, Ron Pubb, Ricardo Passila, Marco Ordon, Edilberto Leon, Bill Greenwood and Andrews Madina. CCC left site around 04:35 PM.

I went back to Pier 7, download my pictures and left offic around 5:00 PM.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV			

Labor								Dispute
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	Zach MacDonald	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 277 **Date:** 16-Apr-2014 **Wednesday**

Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	Tony Miranda	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	STANLEY DALIE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Dispute
Equipment ID	Description					Remarks	
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		


Attachment



View in South Tower area



Tower Elevator Installation

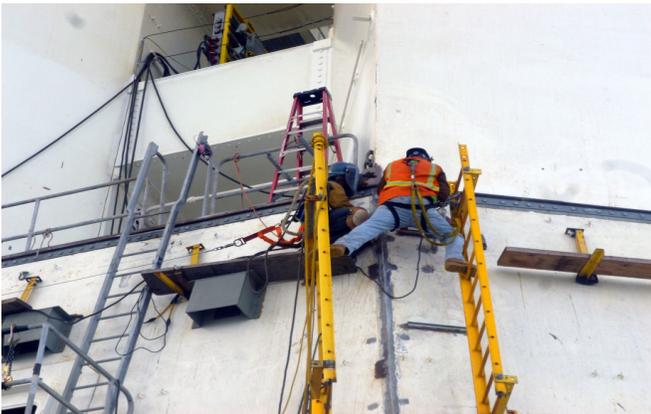

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 277

Date: 16-Apr-2014

Wednesday

Regie & Paul worked on tower skirt on west entrance area



CCC Forman Tony watched spary operation at west entrance area
