



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 313 Const Calendar Day: 749 Date: 23-Jun-2014 Monday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

- * Attended stuff meeting from 8:00 to 9:15 AM.
- * Went to T1 - Tower Base Area by boat around 9:45 AM, saw Tony (CCC), Joe (METS) and ABF paint inspector Ray Shutley as well - talked to them about the work status.
- * There was still no Tower (beyond 53 m) cleaning / painting work due to accident happended on the ladder.
- Six ABF's labors: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz, and James Sturgeon (ABF's Forman) were in tower (below 53 m) performed cleaning, and installed safety features today.
- * Paint Crew: Billy Gatewood, Joege Fiones, Mark Sterward, Recavdo Pasalla (paint forman), Marco Ornuo, Javier Alvag, Edilberto Leon, & Tony Katrones (Superintendent). Performed paint spary on west side of tower base (exterior of tower skirt 3 - 13 meter, two coatings).
- * Back to office, performed paper work including RFI/Submittal PMIV works until 3:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							

Daily Diary Report by Bid Item


Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 313 **Date:** 23-Jun-2014 **Monday**

*E0020562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
2292	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
2293	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE CERTIFIED COATINGS COMPANY							
04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE CERTIFIED COATINGS COMPANY							
04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE CERTIFIED COATINGS COMPANY							
CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist AMERICAN BRIDGE/FLUOR, A JV							

Attachment



Joe (METS) & Tony (CCC) talked about work status

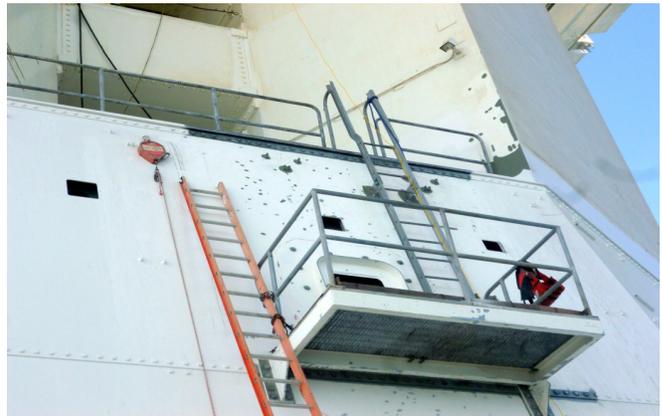

CCC performed paint repair by hand on east side of opening area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 313

Date: 23-Jun-2014

Monday



Tower East side painting were complete, CCC worked on West Side - with Containment



Final primer coating was on in west side of tower skirt (Exterior)



West side of panel, the blasting was done and primer coating was on
