



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 316 Const Calendar Day: 752 Date: 26-Jun-2014 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Tctivites

- * Checked e-mail & performed paper work early morning. Attended safety meeting until 9:10 AM.
- * Went to T1 - Tower Base Area by boat around 9:30 AM with Robert in the same boat,
- * ABF crew performed prep work ready for Tower (beyond 53 m) cleaning / painting work today, they might start tomorrow or next week.

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz, James Sturgeon (ABF's Forman) performed prep & cleaning (below 53 meter) today. Crew might perform grout chipping & patching on bottom of tower skirt tomorrow.

- * For CCC painters' works:
 - Continued removed scaffolding on west side of tower base (see pictures). Total 10 people worked in field today. Crew moved scaffolding members on north side of tower ready for crane to move to barge tomorrow.

Paint Crew: Billy Gatewood, Recavdo Pasalla (paint forman), Marco Ornuo, Javier Alvag, Edilberto Leon, Ron Shaves, Jose Ayala, Felipe Jr. Sunloz, Jauier Alcala, Felipe Martinez & Tony Katrones (Superintendent).

- * Three personnel were installing pump at bottom of tower base and connecting pipe to outside the tower (FS W) .
- * Three labores were working on Dehumidifier duct welding to panel on cell 6 area.
- * Went down to Tower base to check caulk sealing between base plates (Cell #5), but did not see any one working down there.

* Back to office, performed paper work including RFI/Submittal PMIV works until 3:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 316 **Date:** 26-Jun-2014 **Thursday**

Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	8.00	0.00	0.00	8.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks
Contractor: AMERICAN BRIDGE/FLUOR, A JV						
*E0020562	WELDING EQUIPMENT					No
		0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No
		0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No
		0.00	0.00	0.00	0.00	<input type="checkbox"/>
2292	WELDER, 600 AMP					No
		0.00	0.00	0.00	0.00	<input type="checkbox"/>
2293	WELDER, 600 AMP					No
		0.00	0.00	0.00	0.00	<input type="checkbox"/>

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 316

Date: 26-Jun-2014

Thursday




Two FSW workers performed dehumidifier duct welding on east side of opening area



New & Old east span bay bridge




Ten panthers removed scaffolding on west side of tower

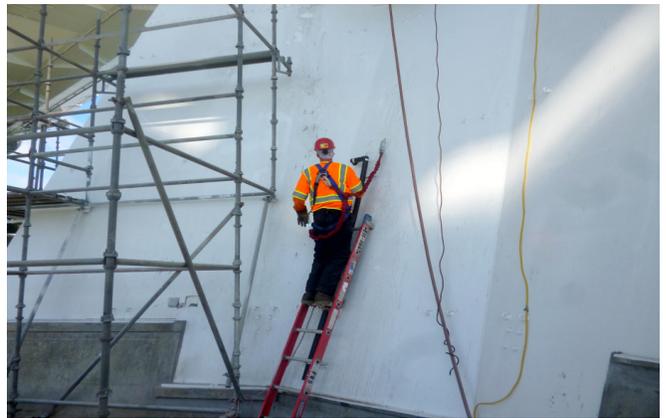

FSW fitting crew installed pump & connecting pipe



Dehumidifier and surrounding piping & duct at Cell 6 area

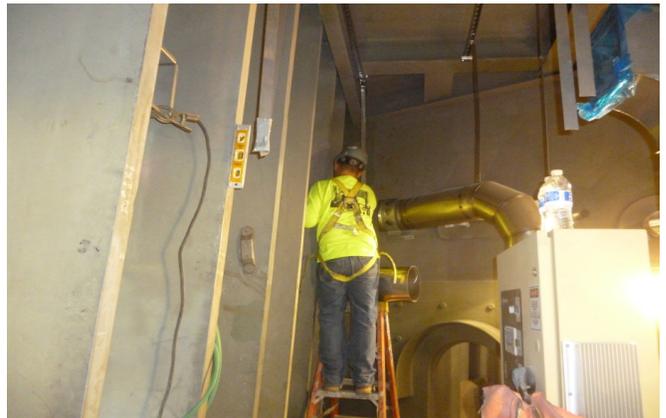

FSW crew installed duct fitting to dehumidifier at cell 6 area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 316


Date: 26-Jun-2014 Thursday



CCC crew put the scaffolding members together ready to move to barge



Inside of tower base at cell #5 - checking caulk sealing on tower base plates

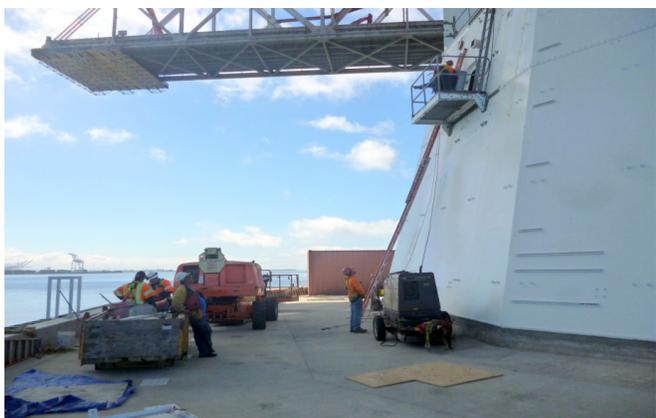

CCC Tony & ABF paint inspector watched operation in east side of tower opening area
