



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:25 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 330 Const Calendar Day: 779 Date: 23-Jul-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day  If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (Below 53 m area) (7/23/14, Wednesday - Clear):



\* Performed paper work including PMIV RFI/Submittal process work this morning.

\* CCC painting works:

- CCC crew continued performing prep & painting work on tower facad area (El. 43 meter) and Tower base cell area touch - up paint repair work.

- Two painters: Billy, Marco continued working in tower base cell area for touch-up paint repair work.

- CCC crew completed working on El. 43 meter façade painting work.

Paint Crew: Billy Gatewood, Joege Flores, Javier Alvag, Recardo Pasalla, Marco Ornuño, E Leon and Tony Katrones.

\*\*\* \*\* Noted that E Leon and Billy Gatewood worked 8 hours on CCO # 314 works today.

\* ABF cleaning work (below 53 m area):

- ABF labores continued performing tower shaft exterior cleaning works (see pictures).

- Crew started cleaning area at shaft S face C at El. 53 m today.

- CCC crew started paint repair on shaft W face B, shaft N face B and shaft E face C & D today.

- Forman Victor and Jose were set up scaffolding on shaft S face C area.

- ABF's crew: Victor Hernandez, Jose Jr. Avila, Fabian Rodriguez, Aurelio Rodriguez, Juan Gutiores, Guillermo Limon,

- CCC crew: See Larain's diary.

\* Other works:



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 330    **Date:** 23-Jul-2014    **Wednesday**

- Saw 3 electricians worked on installing PVC pipe for electric lines around exterior of skirt area (see pic).
- Crane operator Neil Caldwell & helper Justin at barge stand by for any lifting work needed.
- Saw Mahmoud performed inspection on tower elevator installation with 4 workers.
- ABF IRWs Paul & Plumb were in tower as well.

**04-0120F4    Bid Item: 053    T-L01-DSE.053    Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

**04-0120F4    Bid Item: 078    T-L01-ENE.078    Tower Lift 01 External Paint Tower NE**

CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-L05-ENE.078    Tower Lift 05 External Paint Tower NE**

CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-HEA-ENE.078    Tower Head External Paint Tower NE**

CERTIFIED COATINGS COMPANY

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 330

Date: 23-Jul-2014

Wednesday

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist  
AMERICAN BRIDGE/FLUOR, A JV


### Attachment



Safety office Grady walked around T1 Tower today with me



ABF labores started cleaning on tower shaft S face C area

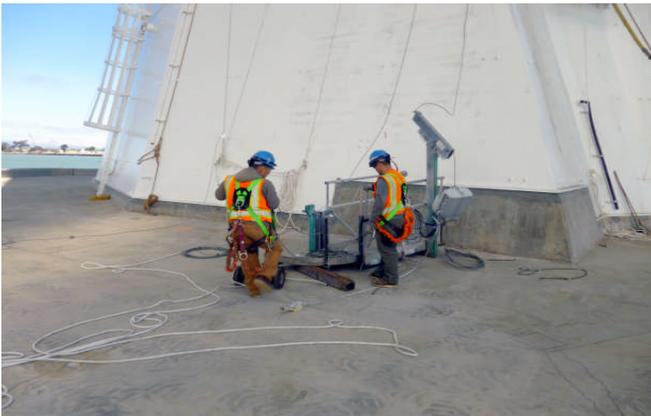


ABF labores Victor & Jose prepared the scaffolding for cleaning on shagt S face C



Old bridgr demolition - from tower base view



CCC painters performed paint repair on tower shaft W face B exterior

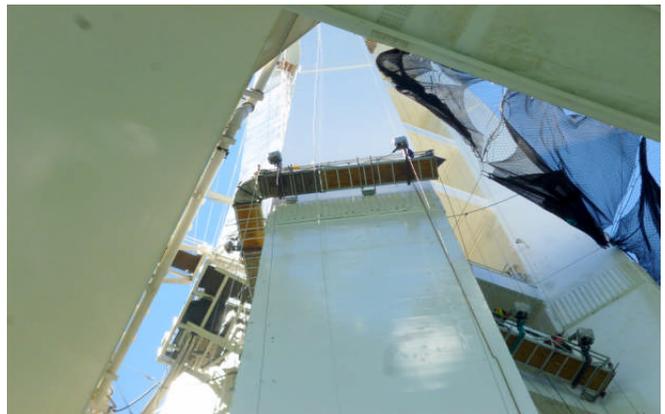

CCC painters started paint repair on exterior shaft E face B and shaft



---

**Daily Diary Report by Bid Item**

**Job Name:** 04-0120F4

**Inspector Name** Liu, Tai-Lin

**Diary #:** 330

**Date:** 23-Jul-2014

**Wednesday**

---

E face C & D

