



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:23 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 332 Const Calendar Day: 781 Date: 25-Jul-2014 Friday
Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
Inspection Type: Continuous
Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
Precipitation Condition Clear

Working Day [checked] If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (Below 53 m area) (7/25/14, Friday - Clear):



- \* Performed paper work, and RFI/Submittal PMIV process and went to field with Grady.
\* At job site, talked to CCC Tony he mentioned that his work almost finished waiting for METS SMR and paint inspector to check facade area on 43m, 47.6m and 53m - 3 layers and inside tower base touch-up works. Today, CCC have two painters at tower base skirt area and two at facade area.
- CCC container on the tower base concrete slab was removed from site.
Paint Crew: Billy Gatewood, Joege Flores, Recardo Pasalla, Javier Alcala, Edllbert Leon and Tony Katrones.
\*\*\* Noted that E Leon, Billy Gatewood, J Flores and J Alcala worked 8 hours on CCO # 314 works today.
\* ABF cleaning work, and CCC paint repair work (below 53 m area):
- Saw 6 ABF's labores at tower base slab area installing scaffolding (L shape) on shaft S face C & D area including ABF painter inspector Ray (see pictures). ABF started performing cleaning on above faces today(below El. 43 area).
- Labor Ignacio Garcia also performed tower base slab cleaning at south side of concrete slab.
- ABF's crew: Jose Jr. Avila, Fabian Rodriguez, Juan Gutiores, Guillermo Limon, Julio Hernandec Mag Juleno and Ignacio Garcia.
\* CCC crew continued performing paint repair on shaft S face B, shaft N face B and shaft E face C & D today (see pictures).
- CCC crew: Francisco Serano, Rafael Serano, Daniel Rosales, Cory Reese and Cory Robinson.
\* Other works:
- Saw 1 electrician worked on installing PVC pipe for electric lines around exterior of skirt area.

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 332    **Date:** 25-Jul-2014    **Friday**

- Did not see crane operator Neil Caldwell & helper Justin at barge today.
  - Saw Mahmoud performed inspection on tower elevator installation with 2 workers (US Hoist).
  - ABF IRWs Paul & Plumb were in tower as well.
- Performed paper work and RFI/Submittal PMIV process work at office.

**04-0120F4    Bid Item: 053    T-L01-DSE.053    Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**  
 AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

**04-0120F4    Bid Item: 078    T-L01-ENE.078    Tower Lift 01 External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-L05-ENE.078    Tower Lift 05 External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-HEA-ENE.078    Tower Head External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 332

Date: 25-Jul-2014

Friday

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist  
AMERICAN BRIDGE/FLUOR, A JV

### Attachment



CCC performed paint repair on shaft S face B area




CCC Tony at site and container was removed from that area




US Hoist performed elevator installation work



CCC crew performed paint repair on shaft N face B, and shaft E face C & D

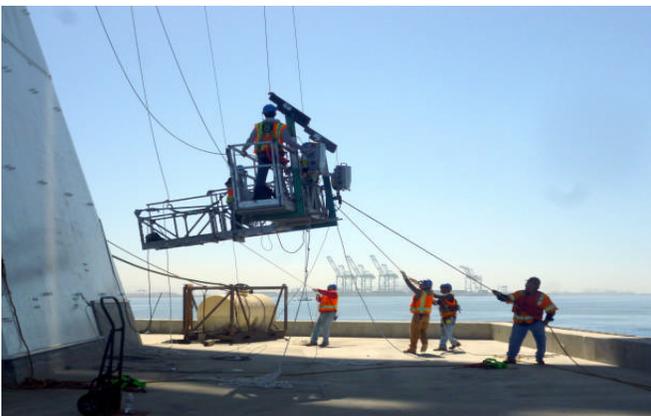

Picture for ABF labores installing L shape cleaning car at shaft S area

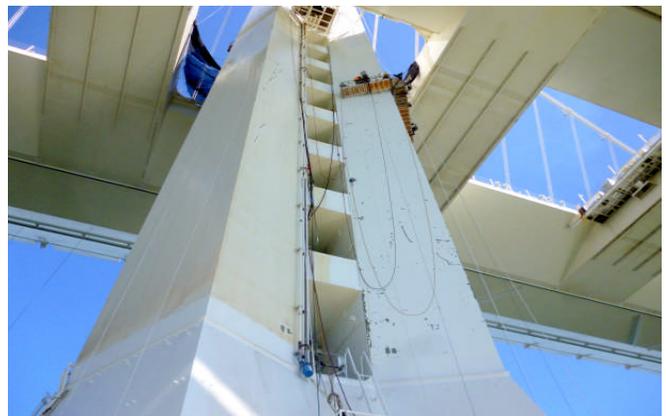

CCC worked paint repair on shaft E face C area

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 332

Date: 25-Jul-2014

Friday



ABF labores installed scaffolding (L shape) on shaft S face C & D for tower cleaning work



Picture showed different crew working on tower area
