



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 349 Const Calendar Day: 806 Date: 19-Aug-2014 Tuesday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 06:00 AM 04:30 PM Break: 00:30 Over Time: 02:00  
 Federal ID:  
 Location:  
 Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80  
 Precipitation Condition Clear

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activites**

CCO # 382 - Tower Painting and Cleaning works (8/19/14, Tuesday - Clear):

- \* Performed paper work, and checked e-mail. Went to job site (T1 base by boat) around 09:25 AM.
- \* At tower base (footing & El.13m)
  - Did not see any labor on the footing area.
  - Saw CCC 6 painters performed paint repair on W/N shafts D/C faces at El. 28m & 45m area.
  - From footing wiewed upward to top top, the safety net surrounding El. 53 m area already been removed (see pictures).
  - Air was wet this morning, painting might not have condition this morning.
- \* After lunch, drove to W2 and walked to Tower entance El. 53m.
  - Saw two L-shape swing stages with 6 painters continued performing paint repair on N/W shafts, D/C faces at El. Close to 53m (below 53m).
  - At tower El. 53m, saw ABF forman James he told me there were no labor work in tower today.
  - Saw METS paint inspectors Justing and QC Sage at El. 53m as well.
  - Saw three painters performed cleaning & painting on N shaft E/A faces. Few more painters were in higher elevation performed paint repair.
  - Sage told that total 12 painters worked today from (6:00 AM to 4:30 PM - 10 hours shaft today)
- \* METS Justing told me that this morning the wether did not have paint condition due to wet air, afternoon Sage said temperature has condition to perform painting, Justing will verfiy the condition. Justing also mentioned the paint repair on top chinrry (inside south shaft) ready for him to check, he plan to go there checking the work.
- \* Paint Crew: Sage Ray, Armado Avitia, Manuel Ramirez, Cory Reese, Alberto Serrano, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Edilberto Leno, Daniel Rosales, Abraham Ventura. Crew worked from 6AM to 4:30PM, 10 hours shift.
- \* No labor except James Sturgeon worked in tower today.
- \* Performed paper work at office and talked to Awal the field status - I will not be office for the next three working days.,

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 349    **Date:** 19-Aug-2014    **Tuesday**

| AMERICAN BRIDGE/FLUOR, A JV                    |                      |                      |  |        |        |                |         |                          |
|--|----------------------|----------------------|--|--------|--------|----------------|---------|--------------------------|
| <b>Labor</b>                                   |                      |                      |  |        |        |                |         |                          |
| Trade  | Class                | Name                 | RT Hrs                                       | OT Hrs | DT Hrs | Total          | Remarks | Dispute                  |
| <b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV |                      |                      |  |        |        |                |         |                          |
| Ironworker                                     | JNM                  | DONALD PLUMB         | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Ironworker                                     | JNM                  | PAUL FAMBRINI        | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | JNM                  | FERMIN MEDINA        | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Ironworker                                     | GEN                  | AARON KENT           | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | JNM                  | LUIS Jimenez         | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | JNM                  | DANNY SCHWARTZ       | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | APP                  | JAVIER MEDINA        | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | FOR                  | GUILLERMO LIMON      | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | APP                  | ROGELIO RODRIGUEZ    | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | JNM                  | CARLOS MONTEJANO     | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | APP                  | JOSE AVILA           | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Semi-Skilled Laborer                           | JNM                  | VICTOR HERNANDEZ     | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| Ironworker                                     | FOR                  | JAMES STURGEON       | 0.00   | 0.00   | 0.00   | 0.00           |         | <input type="checkbox"/> |
| <b>Equipment</b>                               |                      |                      |  |        |        |                |         |                          |
| Equipment ID                                   | Description          | RT Hrs               | OT Hrs                                       | ST Hrs | IT Hrs | Rental Company | Remarks | Dispute                  |
| <b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV |                      |                      |  |        |        |                |         |                          |
| *E0020562                                      | WELDING EQUIPMENT    |                      |  |        |        |                | No      | <input type="checkbox"/> |
|  |                      | 0.00                 | 0.00   | 0.00   | 0.00   |                |         |                          |
| *E0030562                                      | WELDING EQUIPMENT    |                      |  |        |        |                | No      | <input type="checkbox"/> |
|  |                      | 0.00                 | 0.00   | 0.00   | 0.00   |                |         |                          |
| *E0010562                                      | WELDING EQUIPMENT    |                      |  |        |        |                | No      | <input type="checkbox"/> |
|  |                      | 0.00                 | 0.00   | 0.00   | 0.00   |                |         |                          |
| 2292   | WELDER, 600 AMP      |                      |  |        |        |                | No      | <input type="checkbox"/> |
|  |                      | 0.00                 | 0.00   | 0.00   | 0.00   |                |         |                          |
| 2293   | WELDER, 600 AMP      |                      |  |        |        |                | No      | <input type="checkbox"/> |
|  |                      | 0.00                 | 0.00   | 0.00   | 0.00   |                |         |                          |
| <b>04-0120F4</b>                               | <b>Bid Item: 078</b> | <b>T-L01-ENE.078</b> | <b>Tower Lift 01 External Paint Tower NE</b> |        |        |                |         |                          |
| CERTIFIED COATINGS COMPANY                     |                      |                      |  |        |        |                |         |                          |
|  |                      |                      |  |        |        |                |         |                          |
| <b>04-0120F4</b>                               | <b>Bid Item: 078</b> | <b>T-L05-ENE.078</b> | <b>Tower Lift 05 External Paint Tower NE</b> |        |        |                |         |                          |
| CERTIFIED COATINGS COMPANY                     |                      |                      |  |        |        |                |         |                          |
|  |                      |                      |  |        |        |                |         |                          |
| <b>04-0120F4</b>                               | <b>Bid Item: 078</b> | <b>T-HEA-ENE.078</b> | <b>Tower Head External Paint Tower NE</b>    |        |        |                |         |                          |
| CERTIFIED COATINGS COMPANY                     |                      |                      |  |        |        |                |         |                          |
|  |                      |                      |  |        |        |                |         |                          |
| <b>CCO-355</b>                                 | <b>Bid Item: 001</b> | <b>0-CIC-EFA.355</b> | <b>CIC - Elevator Impacts - USA Hoist</b>    |        |        |                |         |                          |
| AMERICAN BRIDGE/FLUOR, A JV                    |                      |                      |  |        |        |                |         |                          |
|  |                      |                      |  |        |        |                |         |                          |

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 349

Date: 19-Aug-2014 Tuesday

Attachment




Painter performed paint repair on El. 53 m area



6 painters on swing stage El. 28m and two painters on El. 53m performed paint repair




At north side of tower, two swing stages 6 painters performed preparation work on N/W shafts D/C faces

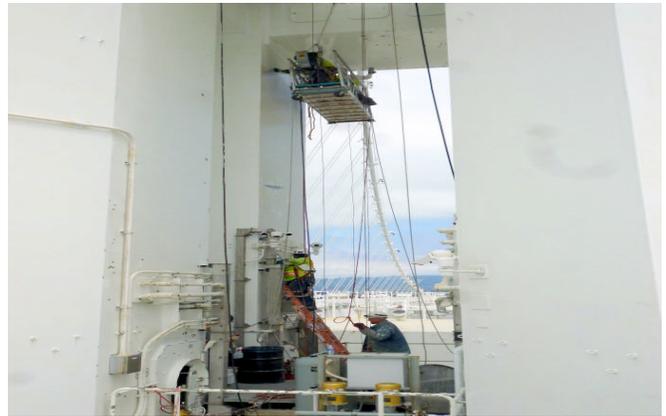

At El.53m, three painters & QC Sage performed paint repair



QC Sage & METS Justing were talking the work status

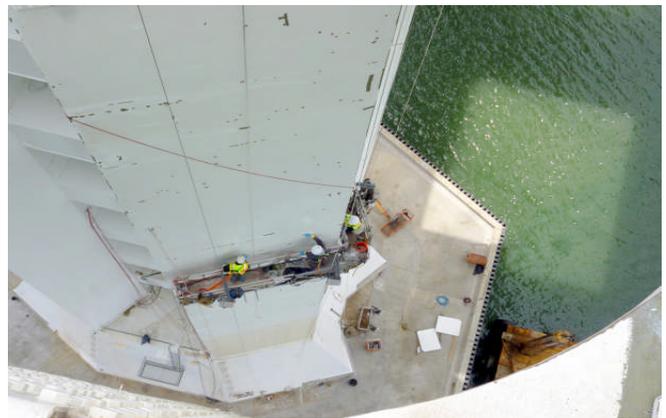

Down view from El.53m, saw 6 painters on N/W shaft D/C faces doing paint repair
