

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-001883**Date Inspected:** 03-Apr-2008**Project Name:** SAS Superstructure**OSM Arrival Time:** 1730**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 800**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China

CWI Name:	N/A	CWI Present:	Yes	No
Inspected CWI report:	Yes No N/A	Rod Oven in Use:	Yes No N/A	
Electrode to specification:	Yes No N/A	Weld Procedures Followed:	Yes No N/A	
Qualified Welders:	Yes No N/A	Verified Joint Fit-up:	Yes No N/A	
Approved Drawings:	Yes No N/A	Approved WPS:	Yes No N/A	
		Delayed / Cancelled:	Yes No N/A	
Bridge No:	34-0006	Component:	OBG Deck Panels	


Summary of Items Observed:

CALTRANS Quality Assurance (QA) Inspector, Erik Prue was present for the fabrication scheduled for this project at the ZPMC facility in Shanghai, China for the San Francisco Oakland Bay Self Anchored Suspension Bridge.

QA inspector performed ultrasonic testing (UT) verification after ZPMC Quality Control (QC) UT inspections on partial penetration joints of the deck panel DP-299-001 to the U-Rib weld joints #1 thru #6 and DP 110-002 U-rib weld joints #5 thru #8. QC UT inspected 15% of the total weld length of each weld joint. ZPMC QC UT Inspectors found lack of penetration indications that results in depth of penetration less than the minimum of 9.6 mm required on weld joints for both deck panels. QA UT Inspector inspected 100% of required 15% QC UT inspection per weld joint. QA UT Inspector verified ZPMC QC UT findings. For details on UT inspections see modified TL-6027 UT Inspection reports generated on this date.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

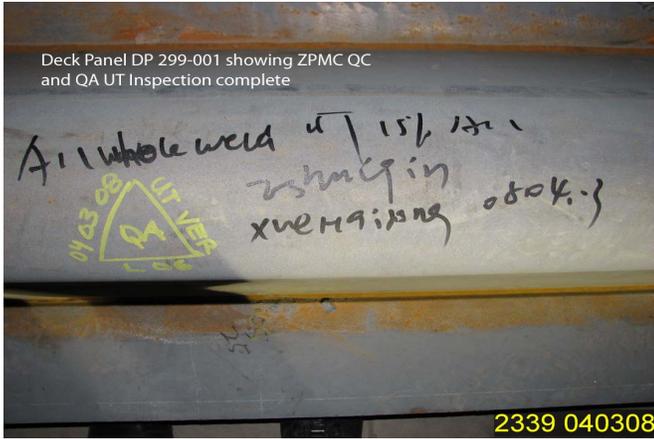

Summary of Conversations:

QA UT Inspector Mr. Paul Dawson performed UT inspection on DP 110-002 welds #1 thru #4 while I performed UT inspection on welds #5 thru #8. For complete documentation on UT inspection see modified TL-6027's UT reports dated this day for Mr. Erik Prue and Mr. Paul Dawson.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Patrick Lowery, 858 344-2712, who represents the Office of Structural Materials for your project.

Inspected By:	Prue,Erik	Quality Assurance Inspector
Reviewed By:	Hager,Craig	QA Reviewer
