

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-023853**Date Inspected:** 17-May-2011**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1900**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** An Qing Xiang**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG**Summary of Items Observed:**

On this day CALTRANS OSM Quality Assurance (QA) Inspector Umesh Gaikwad was present during the times noted above for observations relative to the fabrication of the Self-Anchored Suspension (SAS) Superstructure being performed by Zhenhua Port Machinery Company (ZPMC) at Changxing Island in Shanghai, China. QA observed and/or found the following:

Trial Assembly Yard

This QA Inspector observed the following work in progress:

OBG Seg 13AW:

This QA Inspector, along with Mr. Shailesh Wadkar; performed in process Visual Inspection of welds (Seg 13AW) at Panel Points (PP) 117.5, PP118 and PP118.35. Visual Inspection was performed on the welds between Longitudinal Diaphragm (LD) 3034A to Edge Panel (EP) 3023A (on the welds inside of the Segment). At various locations on the EP to FB welds, this QA Inspector observed cope holes that require to be profiled correctly. In addition, the following welds were observed to have toe cracks. Details are as follows:

- 1) Seg3013R-032 and 033 (fillet welds at PP117.5 – identified earlier on Dt: 05/12/11).
- 2) Seg3013P-018 and 027 (fillet welds at PP118).
- 3) Seg3013P- 028, 017, 020, 022, 026, 028 (PP118).
- 4) Seg 3013M-024, 028 (PP118.35).

WELDING INSPECTION REPORT




(Continued Page 2 of 5)

5) Seg 3013Q-007 (PP118).

This QA Inspector informed to ZPMC CWI, identified as Mr. An Qing Xiang. The weld locations were documented and forwarded to the CT Lead QA Inspector for further disposition.


See attached photo for details.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable Contract documents.

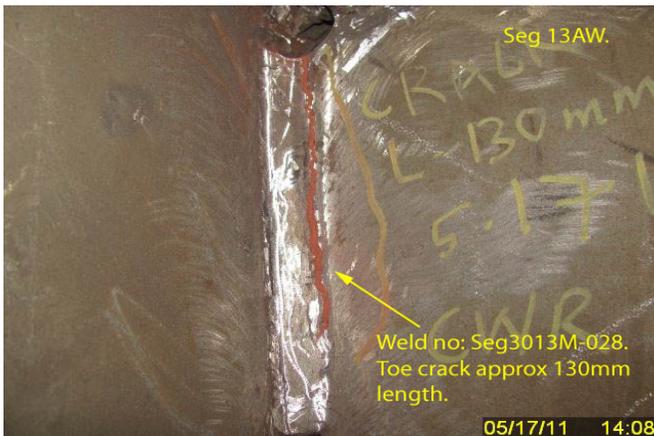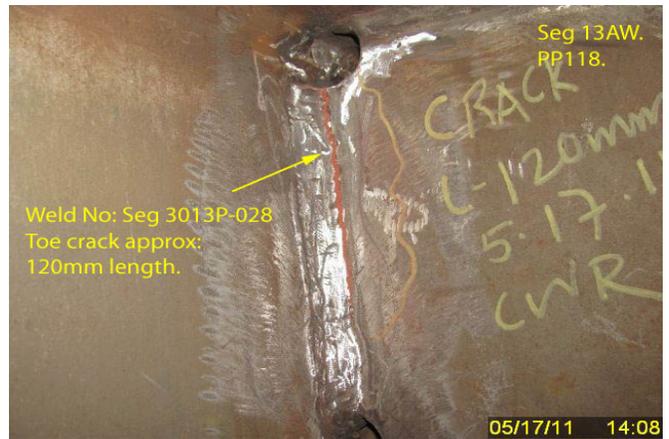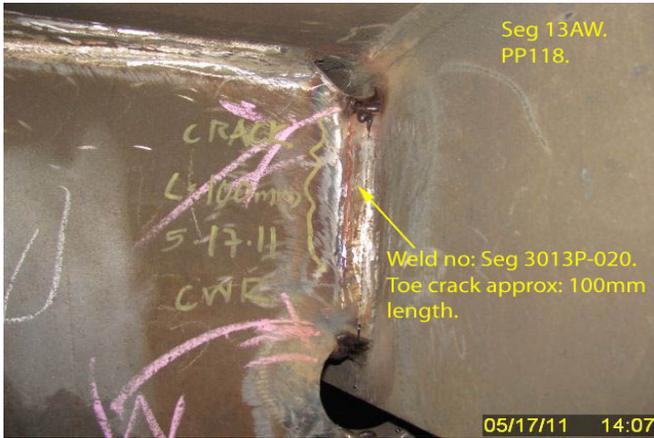



WELDING INSPECTION REPORT

(Continued Page 3 of 5)

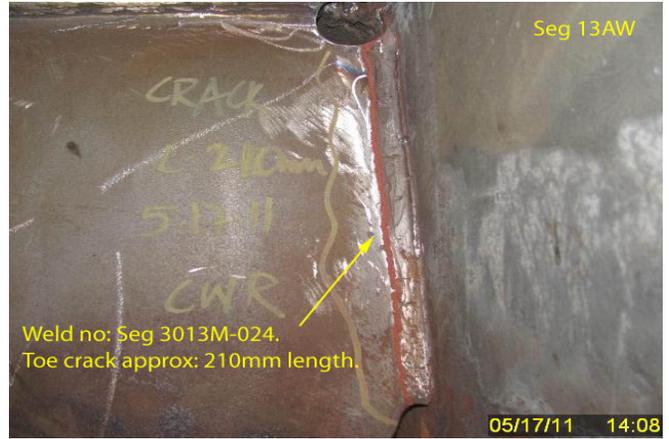


WELDING INSPECTION REPORT

(Continued Page 4 of 5)

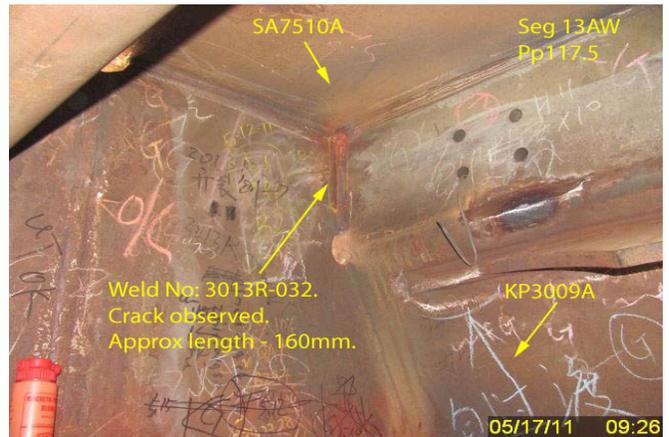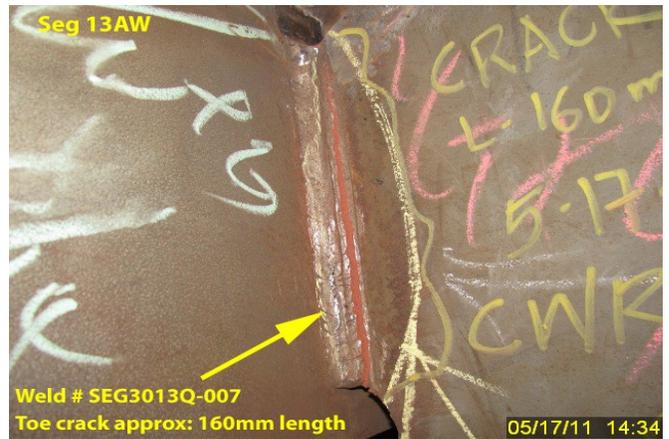

WELDING INSPECTION REPORT

(Continued Page 5 of 5)

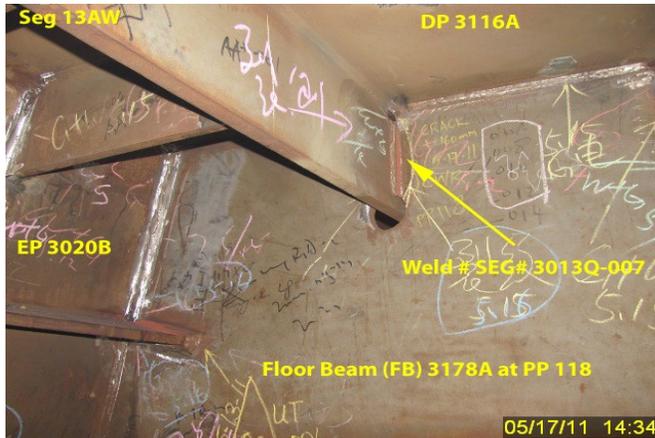

Summary of Conversations:

Only general conversation was held between QA and QC concerning this project.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Eric Tsang : 15000422372, who represents the Office of Structural Materials for your project.

Inspected By:	Gaikwad,Umesh	Quality Assurance Inspector
Reviewed By:	Peterson,Art	QA Reviewer
