

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-001437**Date Inspected:** 03-Jan-2008**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1500**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Huong Wei**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Check Test Samples & PQR #HP2007531**Summary of Items Observed:**

Caltrans Quality Assurance Inspector Gabriel Quintana (QA Inspector) arrived at the Zhenhua Port Machinery Company (ZPMC) facility at Changxing Island, in Shanghai, China to observe fabrication and Quality Control Inspectors (QC Inspectors) perform their duties and responsibilities as specified in the contract documents, approved plans, fabrications documents and Special Provisions for this project. While on site the QA Inspector observed the following:

PQR ID #HP2007531 QA Inspector observed ZPMC welder Zhu Haiping ID #066424 perform welding for Procedure Qualification Record Test (PQR) #HP2007531. Base material specification is ASTM Grade 345, Heat #7300320N and is 26mm thick. Welder is observed welding in the 3G position utilizing the SMAW process. Electrodes used for the PQR is described as the following: diameter 3.2mm and 4.0mm diameter, Classification E7018, Brand TL-508, Specification AWS A5.1. QA Inspector observed ZPMC QC Inspector Huong Wei monitor welding parameters per the preliminary WPS. QA Inspector observed interpass cleaning methods by using manual steel wire brush and manual hammer with a chisel. QA Inspector performed random verifications of the welding and parameters for a total of 6 passes. QA Inspector observed that the welding parameters taken by QC Inspector appear to be accurate and in accordance with the contract documents and AWS D1.5 (2002), Qualification Section 5.13. Craig Knops of ABF is present to observe the PQR. QA Inspector did not observe the final weld layers of the PQR and no Lot Number was assigned by the QA Inspector. See the summary of conversations below for more information.

Check Test Samples - QA Inspector observed the lay out and marked Caltrans Check Test Samples that will be removed for testing as specified in the Contract Special Provisions. QA Inspector verified that the heat numbers,

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

batch numbers, grade, thickness and identification number for batch number eight (8), thirteen (13) and nineteen (19) matched the list of material for the Caltrans Check Test Samples provided. QA Inspector observed that all samples are properly marked for removal with the long dimension transverse to the direction of rolling and 355mm wide by 460mm long. QA Inspector identified each plate and with an arrow indicating the direction of roll and assigned a Caltrans Lot Number for each plate marked for sampling. The following list shows the Caltrans Lot Numbers assigned, heat numbers thickness and grades of the materials sampled. See the photographs on the following page which shows an example of the material identification and marking applied by the QA Inspector.

List of Material for Check Test Samples (eighth Batch)

Lot Number	Heat No.	Grade	Thickness
L17-003-08	7200667N	A709M-345F2-X	14mm
L17-004-08	7200833N	A709M-345F2-Z	60mm
L17-005-08	7203550N	A709M-345F2-X	14mm
L17-006-08	07302868N0	A709M-345F2-X	12mm
L17-007-08	07303999N1	A709M-345F2-X	16mm
L17-008-08	7100535N	A709M-345T2-Z25	45mm
L17-009-08	7100982N	A709M-345T2-X	45mm
L17-010-08	7200667N	A709M-345T2-X	5mm
L17-011-08	7300121N	A709M-345T2-Z	60mm
L17-012-08	07200721N	A709M-345T2-Z	90mm
L17-013-08	07101219	A709M-345T2-Z	90mm
L17-014-08	07102602N	A709M-345T2-Z	70mm

List of Material for Check Test Samples (thirteenth Batch)

Lot Number	Heat No.	Grade	Thickness
L17-015-08	7301488N	A709M-345F2-X	16mm
L17-016-08	7301485N	A709M-345F2-X	12mm
L17-017-08	7301481N	A709M-345F2-X	22mm
L17-018-08	7301584N	A709M-345F2-X	16mm
L17-019-08	7301551N	A709M-345F2-X	18mm
L17-020-08	7301552N	A709M-345F2-X	18mm
L17-021-08	7301434N	A709M-345F2-X	28mm

List of Material for Check Test Samples (nineteenth Batch)

Lot Number	Heat No.	Grade	Thickness
L17-022-08	7301541N	A709M-345F2-X	18mm

Summary of Conversations:


QA Inspector was assigned to witness test samples prior to completing the final layers of the PQR. QA Inspector was informed by QA Task Leader Jim Cochran that welding may continue with out observation by the QA Inspector under the conditions that no discrepancies were noted during prior observation. QA Inspector informed

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

Craig Knops of ABF that QA Inspector will not be present during the welding of final layers and directed him to continue his observations during any welding .


QA Inspector informed the QC Inspector Fu Yu Hong that any markings on the edges of the Check Test Samples will be required to be removed prior to shipping the samples to the testing facility.

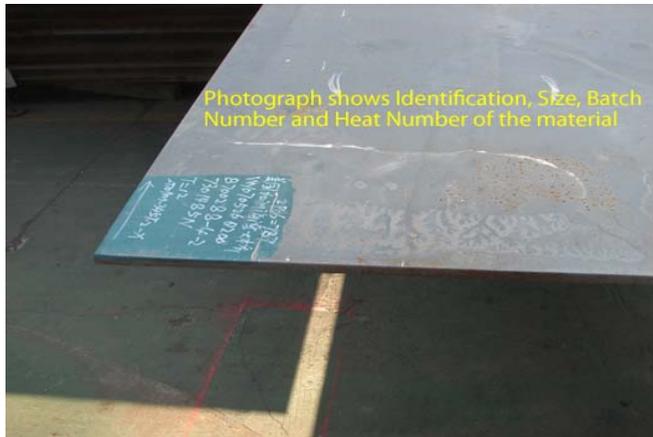

Photograph shows Identification, Size, Batch Number and Heat Number of the material



Photograph showing PQR #HP2007531 prior to welding

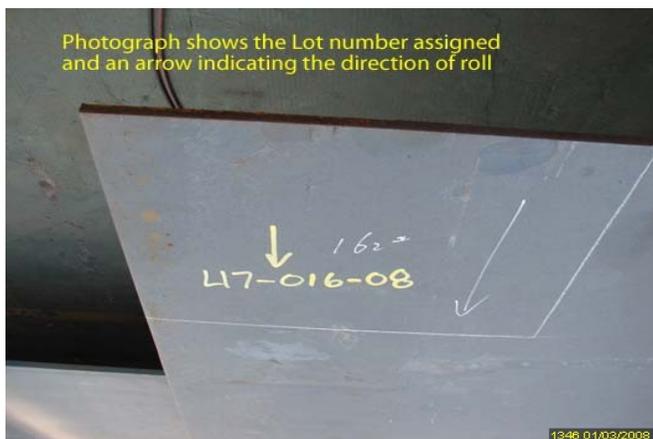

Photograph shows the Lot number assigned and an arrow indicating the direction of roll



Photograph showing ZPMC welder Zhu Haiping performing the welding of PQR #HP2007531

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Mazen Wahbeh, (818) 292-0659, who represents the Office of Structural Materials for your project.

Inspected By: Quintana, Gabriel

Quality Assurance Inspector

Reviewed By: Cochran, Jim

QA Reviewer
