

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 13.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-005571**Date Inspected:** 27-Feb-2009**Project Name:** SAS Superstructure**OSM Arrival Time:** 603**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1500**Contractor:** Oregon Iron Works Clackamas, Or.**Location:** Clackamas, Oregon**CWI Name:** See below**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Hinge K Pipe Beams**Summary of Items Observed:**

On this date, Caltrans Quality Assurance Inspector (QA) Sherri Brannon is present at the Oregon Iron Works, Inc. (OIW) jobsite in Clackamas, Oregon for the purpose of observing fabrication of the Hinge K Pipe Beams.

OIW Fabrication Shop-Bay 1:

QA Inspector Brannon randomly observed OIW personnel and 1 helper continuing in Bay 1 at the CNC mill for facing hinge k pipe beam post tension cap plate (A825M) MK#a109 in preparation for welding.

OIW Shop-Bay 1 (PQR):

QA Inspector Brannon witnessed OIW welder Mr. Craig Jacobson ID#J6 and 1 helper welding Procedure Qualification Record (PQR) number CS-065. QA Inspector Brannon observed OIW QC CWI Mr. Bill Buck monitoring the PQR test. See Caltrans Welding Witness Report, TL-6032 dated February 27, 2008 for additional information.

OIW Fabrication Shop-Bay 3 (sub-assembly):

QA Inspector Brannon randomly observed 2 OIW personnel setting up positioner in preparation for welding internal ring stiffeners (HPS 485 W) to hinge k pipe beam fuse half sections (HPS 485 W).



Material, Equipment, and Labor Tracking:

QA Inspector Brannon performed a verification of personnel at OIW. QA Inspector Brannon observed 1 Supervisor, 4 Quality Control and 6 production personnel on this date.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

The following digital photograph below illustrates observation of the activities being performed.

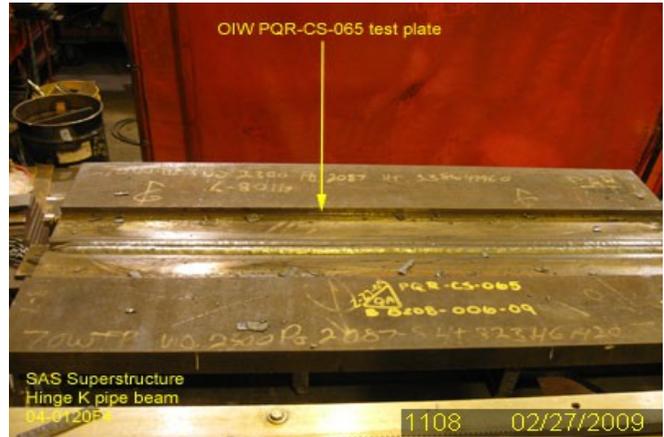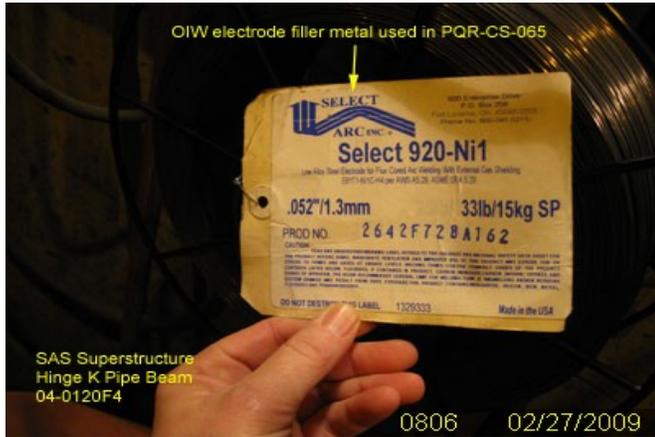

Summary of Conversations:

No relevant conversations on this date.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Mohammad Fatemi (916) 813-3677, who represents the Office of Structural Materials for your project.

Inspected By:	Brannon, Sherri	Quality Assurance Inspector
Reviewed By:	Adame, Joe	QA Reviewer
