

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 13.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-008904**Date Inspected:** 14-Sep-2009**Project Name:** SAS Superstructure**OSM Arrival Time:** 1300**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 2130**Contractor:** Oregon Iron Works Clackamas, Or.**Location:** Clackamas, OR**CWI Name:** Mike Gregson, Jose Salazar**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Hinge K Pipe Beams**Summary of Items Observed:**

The Quality Assurance Inspector Sean Vance arrived on site at Oregon Iron Works, Inc (OIW) in Clackamas, OR, to randomly observe the in process welding of the Hinge K Pipe Beam assemblies. The QA Inspector arrived on site to randomly observe the OIW Quality Control (QC) Inspectors in process and completed visual and nondestructive testing. Upon the arrival of the QA Inspector the following observations were made:

OIW Fabrication Shop-Bay 3

Hinge-K Pipe Beam Assembly 102A-1: 9/14/09

a111-1 Forging to a110-1 Base Plate

QA Inspector noticed that OIW had previously placed this forging assembly 102A-1 in position and was in-process of machining the completed stiffeners, utilizing a mechanical machining bit. QA Inspector had previously measured the stiffener heights to be approximately 662mm and noted that approximately 12mm of material (485W) was in process of being removed, to achieve a desired result of 650mm (+3mm/-10mm), which is in accordance to contract requirements. QA Inspector had previously spoken with OIW machinist and OIW explained that the mechanical machining bit was set to remove approximately 1/32" (.8mm) of material (485W), per each cutting pass. QA Inspector noted that once the machining process is complete, OIW will perform dimensional measurements utilizing a laser tracker, prior to fitting the a109 (Post Tension Cap) plates. See attached picture below.

Hinge-K Pipe Beam Assembly 102A-2: 9/14/09

a111-2 Forging to a110-2 Base Plate

QA Inspector noticed welder #O6, Mr. Tim O'Brian, was in process of performing submerged arc welding, on the

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

d107 stiffener plate to ab106 stiffener plate, designated as weld joint # W1-110, in the flat position. QA Inspector noted that this weld joint was designated as a partial joint penetration (AWS D1.5 TC-P5-S) and verified Mr. O'Brian was currently qualified for this process/position. QA Inspector noted that Mr. O'Brian was utilizing OIW approved welding procedure specification (WPS 4020) and randomly recorded pre-heat temperatures of approximately 350 degrees Fahrenheit (177 C). QA Inspector noted that QC Inspector Jose Salazar was present to monitor in-process welding parameters (amps/volts) and noted that Mr. Salazar had previously recorded in-process welding parameters of 430 amps and 30 volts, on the cover passes. QA Inspector verified in-process welding parameters of 440 amps and 30 volts, which appears to be in compliance with the applicable welding procedure specification and contract requirements. See attached picture below.

Note: QA Inspector spoke with QC Inspector Jose Salazar and Mr. Salazar explained that the following weld joints, on the radial stiffeners, were completed by Mr. O'Brian by end of shift: WJ #W1-110, W1-121 and W1-112. Mr. Salazar also explained that 100% magnetic particle testing was performed on the FCAW root passes and no rejectable indications were found, as noted in the applicable magnetic particle testing report (MT-2244-433).

Hinge-K Pipe Beam Assembly 102A-3: 9/14/09

a111-3 Forging to a110-3 Base Plate

QA Inspector witnessed QC Inspector Jose Salazar continuing to performing 100% magnetic particle testing on the base metal of forging a111-3, after previous removal of the following stiffeners: e108 (WJ #126, 127), f108 (WJ #138, 139), c107 (WJ #142, 143), e108 (WJ #146, 147) and d108 (WJ #148, 149). QA Inspector noticed Mr. Troy Smith, was in-process of grinding these previously found indications, on the base metal of forging a111-3, on the above mentioned weld joints. QA Inspector spoke with QC Inspector Jose Salazar and Mr. Salazar explained that after grinding into the base metal, to a depth of approximately 1.5mm-3mm, magnetic particle testing was being performed and no rejectable indications were found, per AWS D1.5 and contract requirements.

OIW Fabrication Shop-Bay 6 (ESW Overlay Process)

Hinge-K Pipe Beam Fuse Assembly 120A-5: 9/14/09

a124-14 Half Fuse to a124-2 Half Fuse



QA Inspector noticed that the second ESW stainless steel overlay passes were in-process, on this fuse assembly 120A-5. QA Inspector witnessed welder #F17, Mr. Igor Frolov performing electro slag welding (ESW) on the second layer welding passes, (approximately 25% complete), in the flat position, utilizing Soudokay brand Soudotape 316L stainless steel consumable strip. QA Inspector noted the first layer passes were completed utilizing the 309L consumable strip and the remaining second (in-process) & third layer passes would be completed utilizing Soudokay brand Soudotape 316L stainless steel consumable strip, per contract requirements. QA Inspector randomly noticed QC Inspector's Mike Gregson and Jose Salazar were present, to verify in-process welding parameters (amps/volts) and monitor in-process continuous pre-heat temperatures. QA Inspector spoke with QC Inspector Jose Salazar and Mr. Salazar explained that welding amps were recorded as 1200 amps/25.2 volts, travel speed at 269mm/min. and a pre-heat temperature recorded at 225 Fahrenheit (107 C). QA Inspector verified in-process welding parameters of 1200 amps/25.2 volts and recorded pre-heat temperatures of approximately 225 Fahrenheit (107 C) QA Inspector verified Mr. Igor Frolov was currently qualified for this welding process/position and randomly recorded pre-heat temperatures of approximately 225 Fahrenheit. QA Inspector noted that Mr. Igor Frolov appeared to be in compliance with the applicable approved welding procedure specification (WPS 7003). See attached picture below.

Material, Equipment, and Labor Tracking

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

QA Inspector Sean Vance performed a verification of material, personnel and equipment involved with the project. The QA Inspector observed at Oregon Iron Works: 5 OIW production personnel and 2 QC Inspectors.

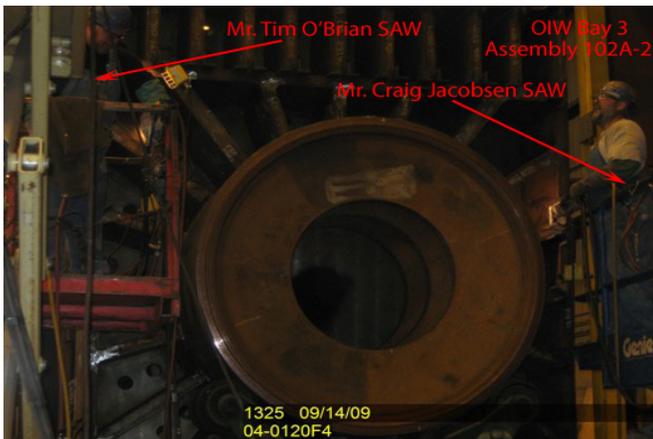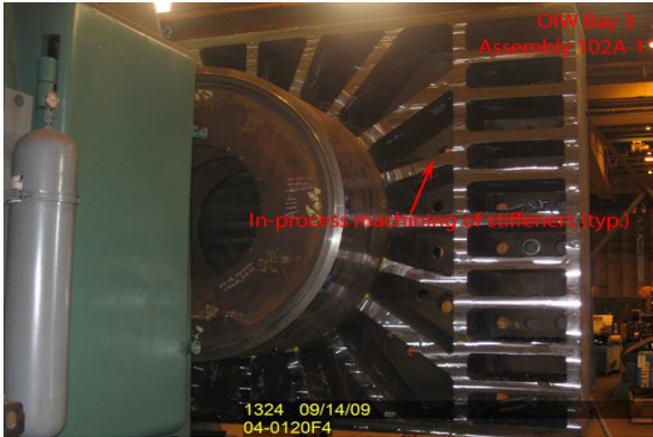

Summary of Conversations:

As noted above.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Mohammad Fatemi (916) 813-3677, who represents the Office of Structural Materials for your project.

Inspected By: Vance, Sean

Quality Assurance Inspector

Reviewed By: Adame, Joe

QA Reviewer
