

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 13.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-011361**Date Inspected:** 11-Jan-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 1000**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1830**Contractor:** Oregon Iron Works Clackamas, Or.**Location:** Clackamas, OR**CWI Name:** M. Gregson, J. Salazar**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Hinge K Pipe Beams**Summary of Items Observed:**

The Quality Assurance Inspector Sean Vance arrived on site at Oregon Iron Works, Inc (OIW) in Clackamas, OR, to randomly observe the in process welding of the Hinge K Pipe Beam assemblies. The QA Inspector arrived on site to randomly observe the OIW Quality Control (QC) Inspectors in process and completed visual and nondestructive testing. Upon the arrival of the QA Inspector the following observations were made:

AG Machining (Boring,OR)

On this date, the QA Inspector arrived at AG Machine to observe OIW perform additional informal penetrant testing and weld repairs, on the finished overlay surface, on this Fuse 120A-4. The QA Inspector met with OIW QC Inspector Jose Salazar, OIW welder (WID# C34) Mark Craig an OIW and AG Machinist. QC Inspector Salazar explained to the QA Inspector that he was continuing to perform additional informal PT on 100% of the overlay and Mr. Craig will continue to perform the GTAW weld repairs. The QA Inspector noted that the indications, currently present in the overlay, appeared after AG completed the final cut pass and finish honing. QC Inspector Salazar informed the QA Inspector that per the approved OIW Liquid Penetrant testing (PT) procedure QC-114 the piece to be examined should be at a minimum of 70 degrees Fahrenheit. For this inspection OIW are attempting to locate any discrepancy that would need to be repaired prior to final inspection. Once all repairs are complete, OIW will later perform a formal PT inspection on 100% of the Fuse overlay per the approved PT procedure. The QA Inspector witnessed QC Inspector Jose Salazar in process of cleaning "sections" on the overlay with acetone/cleaner and also later applying penetrant and developer. The QA Inspector spoke with Mr. Salazar who explained that any surface indications that were present during the informational PT testing would be marked for repairing and OIW welder Mark Craig would then grind out and perform GTAW on the repairs. QC Inspector Salazar informed the QA Inspector that multiple indications were present, during the PT testing, which appeared to

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

be small clusters of slag inclusions. The QA Inspector witnessed Mr. Craig grinding out these indications, to a depth of .5-1 mm and then later setting up to perform the GTAW.

The QA Inspector noted that Mr. Craig was currently qualified to perform these repairs and would be utilizing welding procedure specification (WPS 8022). The QA Inspector witnessed Mr. Craig performing the pre-heat required, utilizing a torch and then observed a temperature of approximately 150 degrees Fahrenheit, after the pre-heat was complete. The QA Inspector noted that 125 degrees Fahrenheit minimum was required, per WPS 8022. The QA Inspector witnessed AG Machinist rotating the fuse assembly to access the weld repair areas in the flat position. The QA Inspector then observed Mr. Mark Craig performing the GTAW on the previously excavated repair areas. The QA Inspector also observed QC Inspector Jose Salazar recording the in-process welding parameters of 123 amps and 15.5 volts. The QA Inspector also verified these welding parameters. The QA Inspector noted that after completion of these weld repair areas, the OIW Machinist performed the grinding with a buffer wheel on the completed weld repair to "flush" with the finished overlay surface. The QA Inspector observed that the Fuse was then rotated and the QC Inspector performed 100% informational PT Inspection on another section of the finished overlay. The QA Inspector also observed several more indications that would need to go through the above mentioned repair procedure. The QA Inspector observed that Mr. Salazar was present the entire time in which the GTAW welding was being performed.

The QA Inspector later spoke with QC Inspector Salazar and Mr. Salazar explained that the informational PT testing was complete and OIW will be arriving the following day on 1/12/10, to finish the weld repairs. Mr. Salazar explained that the repairs should be completed in approximately 2 hrs. (See attached pictures below)


Material, Equipment, and Labor Tracking

QA Inspector Sean Vance performed a verification of material, personnel and equipment involved with the project.

The QA Inspector observed at Oregon Iron Works: 2 OIW production personnel and 1 QC Inspector.

The QA Inspector observed at AG Machine shop: 1 AG machinist, 1 OIW welder and 1 OIW QC.

The QA Inspector noted that no work was performed at OIW Vancouver paint shop.

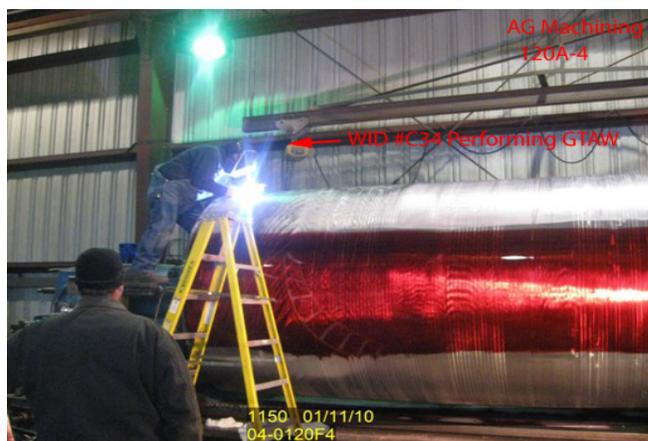

WELDING INSPECTION REPORT

(Continued Page 3 of 3)



Summary of Conversations:

As noted above.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Mohammad Fatemi (916) 813-3677, who represents the Office of Structural Materials for your project.

Inspected By: Vance,Sean

Quality Assurance Inspector

Reviewed By: Adame,Joe

QA Reviewer
