

**DEPARTMENT OF TRANSPORTATION**

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch  
690 Walnut Ave. St. 150  
Vallejo, CA 94592-1133  
(707) 649-5453  
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1x.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-014035**Date Inspected:** 17-May-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 1000**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1830**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site

<b>CWI Name:</b>	Jim Cunningham and William Sherwood			<b>CWI Present:</b>	<b>Yes</b>	<b>No</b>	
<b>Inspected CWI report:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Rod Oven in Use:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Electrode to specification:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Weld Procedures Followed:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Qualified Welders:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Verified Joint Fit-up:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Approved Drawings:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Approved WPS:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
				<b>Delayed / Cancelled:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Bridge No:</b>	34-0006			<b>Component:</b>	Orthotropic Box Girder		

**Summary of Items Observed:**

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

QA randomly observed ABF/JV qualified welders Rory Hogan (ID #3186) perform CJP groove (splice) back welding fill pass on Orthotropic Box Girder (OBG) L1W/L2W side plate 'C' outside. The welder was observed welding in the 4G (overhead) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3110-4. The welder was using a track mounted welder holder assembly that is remotely controlled. The joint being welded has the backing bar gouged using the Esab Plasma Arc machine and was ground smooth. The gouged and ground splice butt joint was also Non Destructive Testing (NDT) tested using the Magnetic Particle Testing (MT). The splice joint was preheated and maintained to greater than 150 degree Fahrenheit using Miller Proheat 35 Induction Heating System located at the other side of the plate prior/during welding. The vicinity was also properly protected from wind and other climatic changes. During welding, ABF Quality Control (QC) Jim Cunningham was noted monitoring the welding parameters of the welder.

At OBG L3E/L4E side plate 'C' outside, QA randomly observed ABF/JV qualified welder Mitch Sittinger continue perform CJP groove welding repair. The welder was observed welding in the 3G (vertical) position utilizing Shielded metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode implementing welding procedure ABF-WPS-D15-1000-Repairs. The repair excavations were preheated to more than 140 degree Fahrenheit using propane gas torch prior welding. During the shift, ABF QC William Sherwood was noted

---

---

# WELDING INSPECTION REPORT


( Continued Page 2 of 3 )

---

---

monitoring the welder. Prior welding, ABF QC William Sherwood was also observed performing Magnetic Particle Testing (MT) using Parker Contour Probe with red magnetic powder as detecting media on the repair excavation. During the shift, the welder has completed two welding repairs inside and has moved to edge plate of the same splice and fixed where bad surface profile of the back weld was noted.

At OBG L4E/L5E top deck plate 'A' outside, flush grinding using a flapper disc on the cover weld reinforcement seen completed. ABF QC Steven Mc Connell and Tom Pasqualone were noted performing Ultrasonic Testing (UT) on area A4 of the same plate.

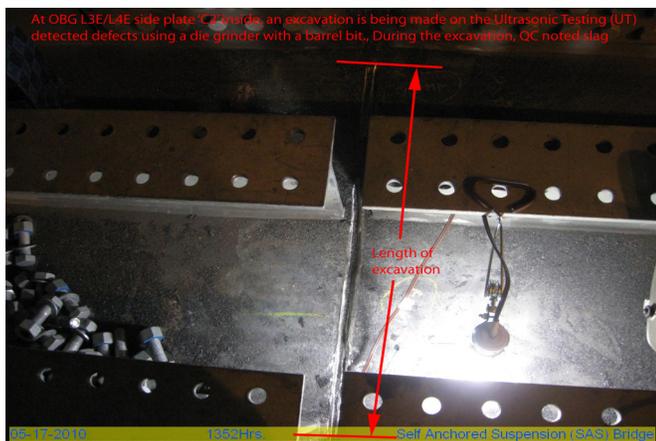

## Summary of Conversations:

As stated above.

## Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Mohammad Fatemi (916) 227-5298, who represents the Office of Structural Materials for your project.

---

Inspected By: Lizardo, Joselito

Quality Assurance Inspector

---

---

# WELDING INSPECTION REPORT

( Continued Page 3 of 3 )

---

---

**Reviewed By:**      Levell,Bill

QA Reviewer
