

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-015366**Date Inspected:** 24-Jun-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1900**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Le Zhi Jiang**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Orthotropic Box Girder (OBG)**Summary of Items Observed:**

On this date Caltrans Office of Structural Material (OSM) Quality Assurance (QA) Inspector, D.Sukanthan was present during the time noted above for observations relative to the work being performed.

OBG # CROSSBEAM CB13

This QA inspector received ZPMC Non Destructive Testing (NDT) notification 006043 to perform Magnetic particle Testing (MT) of approximately 15% of the area previously tested and accepted by ZPMC Quality Control Personnel. This QA Inspector generated a Magnetic particle Test report for this date. The member is identified as Crossbeam CB13. The weld tested is identified as follows:

(CB202G-038-045,046,147,165)

(CB202G-039-045,046,147,165)

(CB202G-040-045,046,147,165)

This QA inspector received ZPMC Non Destructive Testing (NDT) notification 006043 to perform Ultrasonic Testing (UT) of approximately 10% of the area previously tested and accepted by ZPMC Quality Control Personnel. This QA Inspector generated a Ultrasonic Test report for this date. The member is identified as Crossbeam CB13. The weld tested is identified as follows:

(FB205-037-036) Non compliant indication


(FB205-038-031) Non compliant indication

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

During the Quality Assurance Ultrasonic Testing (UT) review of welds located on Orthotropic Box Girder (OBG) Crossbeam CB 13, this Quality Assurance Inspector (QA) discovered the following issues. Three (3) longitudinal linear indication measuring approximately 35mm, 30mm and 30mm in length. The indication dbfs rating is a +1, +7 and +6. Material thickness is 12 and 14mm. The depth of the indication is approximately 8mm, 9mm and 6mm. The welds are identified as: FB205-038-031 and FB205-037-036. These welds are Complete Joint Penetration (CJP) splice weld joints. The welds are designated as Non Seismic Performance Critical Material (Non SPCM). These indications are clearly marked on or near the weld. This QA notified ZPMC QA identified as Mr. Zhang wei of this issue and that an incident report would be generated. For more information refer Ultrasonic test report for this date. See attached picture.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

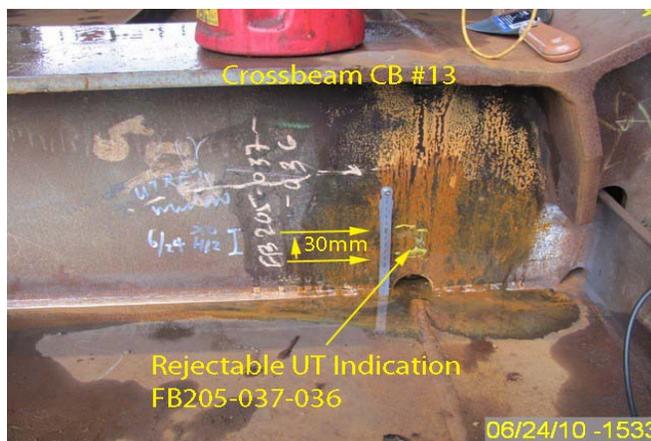

Summary of Conversations:

As mention above

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Eric Tsang 150-00422372, who represents the Office of Structural Materials for your project.

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

Inspected By:	Sukanthan,Dhanasingh	Quality Assurance Inspector
----------------------	----------------------	-----------------------------

Reviewed By:	Hall,Steven	QA Reviewer
---------------------	-------------	-------------
