

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-016300**Date Inspected:** 18-Aug-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 1000**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1500**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site

CWI Name:	William Sherwood and Jim Cunningham			CWI Present:	Yes	No	
Inspected CWI report:	Yes	No	N/A	Rod Oven in Use:	Yes	No	N/A
Electrode to specification:	Yes	No	N/A	Weld Procedures Followed:	Yes	No	N/A
Qualified Welders:	Yes	No	N/A	Verified Joint Fit-up:	Yes	No	N/A
Approved Drawings:	Yes	No	N/A	Approved WPS:	Yes	No	N/A
				Delayed / Cancelled:	Yes	No	N/A
Bridge No:	34-0006			Component:	Orthotropic Box Girder		

Summary of Items Observed:

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

At OBG 5W/6W side plate 'C' (1000mm to 3200mm) inside, QA randomly observed ABF/JV qualified welder Sungtao, Huang ID # 3794 continuing to perform CJP groove (splice) welding fill pass on the splice butt joint. The welder was observed performing automatic welding in the 3G (vertical) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3042B-1. The joint being welded had a single V-groove butt joint with backing bar. The splice joint was preheated and maintained to greater than 150 degrees Fahrenheit using Miller Proheat 35 Induction Heating System located at the opposite side of the plate prior/during welding. ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters of the welder. At the end of the shift, fill pass welding was still continuing and should remain tomorrow.

QA randomly observed ABF/JV qualified welders Rory Hogan and Jeremy Dolman continuing to perform CJP groove (splice) back welding fill pass to cover pass on Orthotropic Box Girder (OBG) 5E/6E side plate 'E1' outside. The welder was observed back welding in the 4G (overhead) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3110-4. The welder was using a track mounted welder holder assembly that was remotely controlled. The joint being welded has the backing bar gouged using the Esab Plasma Arc machine and was ground smooth. The gouged and ground splice butt joint was also Non Destructive

WELDING INSPECTION REPORT

(Continued Page 2 of 3)


Testing (NDT) tested using the Magnetic Particle Testing (MT). The splice joint was preheated and maintained to greater than 150 degrees Fahrenheit using Miller Proheat 35 Induction Heating System located on top of the plate prior welding and by moving the blanket to the side of the weld being welded during welding. The vicinity was also properly protected from wind and other climatic conditions. ABF Quality Control (QC) Jim Cunningham was noted monitoring the welding parameters of the welder. During the shift, welding of cover reinforcement at location E1 was completed and the welder has moved to E2 of the same OBG splice. Fill pass welding was still continuing at this new location and should remain tomorrow.

At OBG 4W/5W side plate 'C' outside, QA randomly observed ABF personnel Mike Maday and Bryce Howell continuing to perform plasma arc gouging on the backing bar removal of the splice butt joint. The personnel were using an Esab plasma arc gouging machine that has the nozzle holder attached to a Bug-o track. Gouging of the backing bar was not completed today and should continue tomorrow.



Summary of Conversations:

At OBG 4E/5E side plate 'C' outside, QA randomly observed ABF QC Jesse Cayabyab perform Ultrasonic Testing (UT) on the welded and flush ground cover of the splice butt joint. After the completion of his UT on the joint, QC mentioned to QA that he has completed scanning both sides of the joint (inside and outside) and that QC found numerous rejectable indications. According to QC, he marked those rejectable indications for repair.

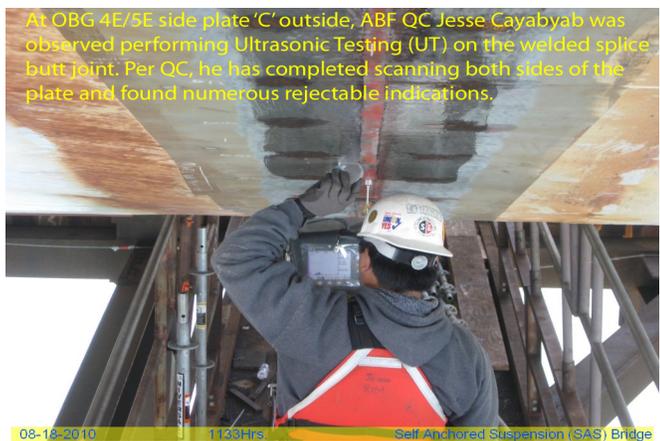

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Mohammad Fatemi (916) 227-5298, who represents the Office of Structural Materials for your project.

Inspected By:	Lizardo, Joselito	Quality Assurance Inspector
----------------------	-------------------	-----------------------------

Reviewed By:	Levell, Bill	QA Reviewer
---------------------	--------------	-------------
