

**DEPARTMENT OF TRANSPORTATION**

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch  
690 Walnut Ave. St. 150  
Vallejo, CA 94592-1133  
(707) 649-5453  
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-017522**Date Inspected:** 20-Oct-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 1000**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1830**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site

<b>CWI Name:</b>	Tom Pasqualone and William Sherwood			<b>CWI Present:</b>	<b>Yes</b>	<b>No</b>	
<b>Inspected CWI report:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Rod Oven in Use:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Electrode to specification:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Weld Procedures Followed:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Qualified Welders:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Verified Joint Fit-up:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Approved Drawings:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Approved WPS:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
				<b>Delayed / Cancelled:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>
<b>Bridge No:</b>	34-0006			<b>Component:</b>	Orthotropic Box Girder		

**Summary of Items Observed:**

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

At OBG 6W/7W side plate 'C' (7155mm to 9955mm) inside, QA randomly observed ABF/JV qualified welder Sungtao, Huang ID # 3794 continuing to perform CJP groove welding fill pass to cover pass on the splice butt joint. The welder was observed perform automatic welding in the 3G (vertical) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3042A-1. The joint being welded had a single V-groove butt joint with backing bar. The splice joint was preheated and maintained to greater than 150 degrees Fahrenheit using Miller Proheat 35 Induction Heating System heater blankets located at the opposite side of the plate prior/during welding. During welding, ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters of the welder. Before the end of the shift, cover pass welding on the splice butt joint was completed and the welder has moved to 9955mm to 10555mm and performed 3G Shielded Metal Arc Welding (SMAW) welding root pass on the splice butt joint. This new location is close to the corner of bottom plate 'D' wherein the Bug-o track mounted nozzle holder has limited access. The welder was observed welding the splice butt joint in the 3G (vertical) position utilizing a Shielded Metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1040B. Root pass welding at this new location was completed and the welder was observed putting fill pass at the end of the shift.

---

---

# WELDING INSPECTION REPORT



( Continued Page 2 of 2 )

---

---

At OBG 6W/7W top deck plate 'A1' and 'A5' outside, ABF QC Steven Mc Connell and Tom Pasqualone were observed performing Ultrasonic Testing (UT) respectively on the welded splice butt joint. QC were using General Electric USM35 ultrasonic machine. Both QC were also observed scanning from both sides of face 'A' of the joint. Steven Mc Connell was noted marking six repairs while Tom Pasqualone has only marked one so far. During the shift, ultrasonic testing on the butt joint was still continuing and should remain tomorrow.

At OBG 6E/7E side plate 'E' inside, this QA performed 10% Magnetic Particle Test (MT) verification on the welded splice butt joint. QA was using Parker Contour Probe Model DA 400 with serial number 16989 electromagnetic yoke with red magnetic powder as detecting media. QA found no significant indications during the verification. Please see TL-6028 report for more information.

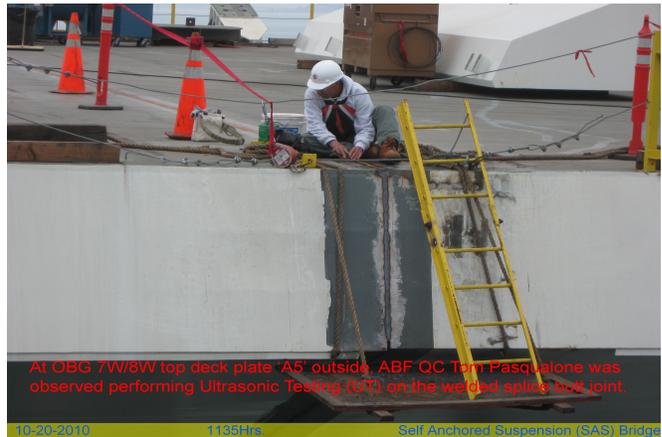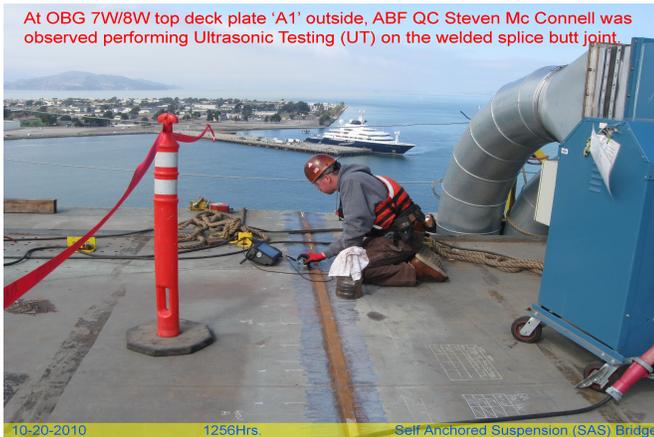

## Summary of Conversations:

No significant conversation occurred today.

## Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Mohammad Fatemi (916) 813-3677, who represents the Office of Structural Materials for your project.

---

**Inspected By:** Lizardo, Joselito

Quality Assurance Inspector

---

**Reviewed By:** Levell, Bill

QA Reviewer
