

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-018571**Date Inspected:** 08-Dec-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 630**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1500**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site**CWI Name:** See Below**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** Orthotropic Box Girders**Summary of Items Observed:**

At the start of the shift the Quality Assurance Inspector (QAI) traveled to the project site and observed the following work performed by American Bridge/Fluor Enterprises (AB/F) personnel at the locations noted below:

- A). Deck Access Hole-LS
- B). Pipe Supports
- C). QC Inspection Request

A). Deck Access Hole-LS

The welder, Xiao Jian Wan ID-9677, performed the CJP groove welding on the longitudinal stiffener at field weld identified as WN: 5E-PP29.5-E2-LS-East. The welding was performed utilizing the SMAW process as per the Welding Procedure Specification (WPS) identified as ABF-WPS-D15-1012-3, Rev.0. The WPS was also utilized by the QC inspector John Pagliero as a reference to monitor the welding and verify the welding parameters. The amperage was observed and recorded as 128 amps and the minimum preheat of 100 degrees Celsius and the maximum interpass temperature of 230 degrees Celsius was verified.

The QAI also observed the welder, Hua Qiang Hwang ID-2930, performed the CJP groove welding on the longitudinal stiffener field weld identified as WN: 6E-PP46.5-E2-LS-West. The welder utilized the SMAW process as per the Welding Procedure Specification (WPS) identified as ABF-WPS-D15-1012-3, Rev.0 and was also utilized by the QC inspector John Pagliero as a reference. The amperage was recorded as 131 amps and the minimum preheat of 100 degrees Celsius and the maximum interpass temperature of 230 degrees Celsius was

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

verified.

The welding was performed in the vertical (3G) position with the work placed in an approximately vertical plane and the groove approximately vertical. The welder utilized a slag hammer, pneumatic air gun with an attached chisel and a wire wheel attached to a 4" high cycle grinder to remove slag after deposit of each fill pass. The electrodes were stored in electrically heated, thermostatically controlled oven after removal from sealed containers.

The exposure limits of the electrodes identified as E9018-H4R and the minimum storage oven temperature of 250 degrees Celsius appeared to be in compliance with the contract documents. At the time of the observation no issues were noted by the QAI.

B). Pipe Supports

The QAI observed the continued fillet welding of the pipe supports identified as PS-11 located along the pier column embeds at W2-E1. The welding was performed by David Garcia ID-8789 utilizing a 3.2 mm electrode as per the Welding Procedure Specification (WPS) identified as Fillet Murex. The fillet welding was performed in vertical (3F) position utilizing a 3.2 mm electrode. The QC inspection was performed by Mike Johnson utilizing the WPS to monitor the welding and to verify the welding parameters.

C). QC Inspection Request

At the request of Quality Control Field Supervisor, Bonifacio Daquinag, the QAI randomly verified the visual appearance of the Complete Joint Penetration (CJP) welding of the following; edge plate splice identified as WN: 6E-7E-B1 and the longitudinal stiffener plate field splice identified as 6E-7E-A-LS1, 2 and 3 . The QAI verification was performed to verify that the welding and visual inspection performed by the QC inspector's, Jesse Cayabyab and John Pagliero, meet the requirements of the contract documents. At the conclusion of the QAI verification it appeared that the weld and the QC inspection complies with the contract documents.


QA Observation and Verification Summary

The QA inspector observed the QC activities and the welding of the field splices utilizing the WPS as noted above, which appeared to be posted at the weld station. The welding parameters and surface temperatures were verified by the QC inspector and utilizing a Fluke 337 clamp meter for the electrical welding parameters and a Fluke 63 IR Thermometer for verifying the preheat and interpass temperatures. The ESAB consumables utilized for the SMAW welding process appeared to comply with the AWS Specification and AWS Classification. The QC inspection, testing and welding performed on this shift appeared to be in general compliance with the contract documents. At random intervals, the QAI verified the QC inspection, testing, welding parameters and the surface temperatures utilizing various inspection equipment and gages which included a Fluke 337 Clamp Meter and Tempilstik Temperature indicators.

The digital photographs on page 3 of this report illustrate the work observed during this scheduled shift.

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

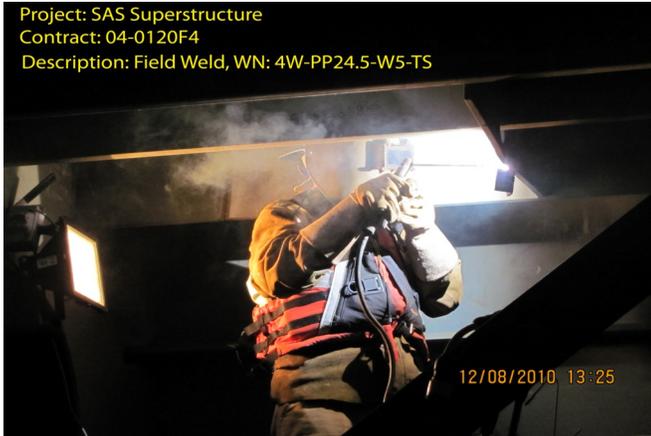

Summary of Conversations:

There were general conversations with Quality Control Inspector Bonifacio Daquinag, Jr. at the start of the shift regarding the location of American Bridge/Fluor welding, inspection and N.D.E. testing personnel scheduled for this shift.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Nina Choy 510-385-5910, who represents the Office of Structural Materials for your project.

| | | |
|----------------------|-------------|-----------------------------|
| Inspected By: | Reyes,Danny | Quality Assurance Inspector |
| Reviewed By: | Levell,Bill | QA Reviewer |
