

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-019008**Date Inspected:** 29-Dec-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1900**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Liu Hua Jie**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG COMPONENT**Summary of Items Observed:**

On this day Caltrans OSM Quality Assurance (QA) Inspector Subhasis Bera was present during the times noted above for observations relative to the fabrication of the SAS Superstructure being performed by Zhen Hua Port Machinery Company (ZPMC) at Chang Xing Island in Shanghai, China. QA Inspector observed and/or found the following:

In process Inspection

Trial Assembly

This QA Inspector observed the following work in progress:

SMAW in the 4G position for the OBG Segment 12AE to 12BE for base metal repair near splice joint of bottom plate to bottom plate, VT repair weld No. OBE12B-001. The welder is identified as #044515. ZPMC QC is identified as Mr. An Qing Xing. The welding variables recorded by QC appear to comply with WPS-345-SMAW-4G(4F)-FCM-REPAIR-1. The repair report is identified as CWR2129.

SMAW in the 1G position for the OBG Segment 12AE to 12BE for splice joint of deck plate to deck plate, UT repair weld No. OBE12-002,003. The welder is identified as #044515. ZPMC QC is identified as Mr. An Qing Xing. The welding variables recorded by QC appear to comply with WPS-345-SMAW-1G(1F)-FCM-REPAIR-1. The repair report is identified as WR19643.

SMAW in the 4G position for the OBG Segment 12AW, weld No. SP3049-001-055. The welder is identified as #041713. ZPMC QC is identified as Mr. Shi Lei. The welding variables recorded by QC appear to comply with

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

WPS-B-P-2214-B-U2-FCM-1.

SMAW in the 4G position for the OBG Segment 12AW to 12BW for splice joint of side plate to side plate at cross beam side , VT repair weld No.OBW12-004. The welder is identified as #040611. ZPMC QC is identified as Mr. Zhou Peng. The welding variables recorded by QC appear to comply with WPS-345-SMAW-4G(4F)-FCM-REPAIR-1.

SMAW in the 4G position for the OBG Segment 12AW to 12BW for near splice joint of side plate to side plate at cross beam side , VT repair weld No.OBW12D-001. The welder is identified as #040611. ZPMC QC is identified as Mr. Zhou Peng. The welding variables recorded by QC appear to comply with WPS-345-SMAW-4G(4F)-FCM-REPAIR-1.


Ultrasonic Testing (A,B,C and D-Scan)

This QA Inspector performed Ultrasonic testing (UT) verification of the area previously tested and accepted by ABF Quality control personnel. This QA inspector generated a (UT) report for this date. The member is identified as butt joint joining between side Plate to bottom Plate for OBG segment 12AW at counter weight side . The result was recorded onto a data sheet according to rejection criteria of "D" Scan procedure 001 rev.1 that Caltrans QA and ABF QA have jointly filled out on this date. The QA inspector found no rejectable indication at scanned area.

The Weld Designation is as follows

SEG3004A-015

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

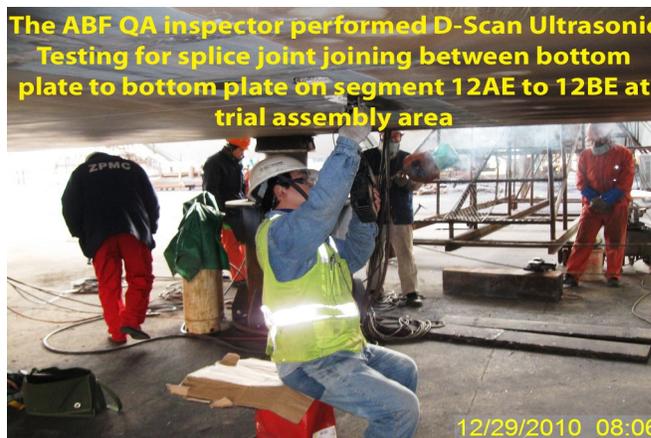

Summary of Conversations:

No relevant conversations

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Eric Tsang 150-0042-2372, who represents the Office of Structural Materials for

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

your project.

Inspected By:	Bera,Subhasis	Quality Assurance Inspector
----------------------	---------------	-----------------------------

Reviewed By:	Dsouza,Christopher	QA Reviewer
---------------------	--------------------	-------------
