

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-022497**Date Inspected:** 07-Apr-2011**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1530**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site

CWI Name:	William Sherwood and Fred Von Hoff			EWI Present:	Yes	No	
Inspected CWI report:	Yes	No	N/A	Rod Oven in Use:	Yes	No	N/A
Electrode to specification:	Yes	No	N/A	Weld Procedures Followed:	Yes	No	N/A
Qualified Welders:	Yes	No	N/A	Verified Joint Fit-up:	Yes	No	N/A
Approved Drawings:	Yes	No	N/A	Approved WPS:	Yes	No	N/A
				Delayed / Cancelled:	Yes	No	N/A
Bridge No:	34-0006			Component:	Orthotropic Box Girder		

Summary of Items Observed:

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

At OBG 10E/11E LS1 longitudinal stiffener inside, QA randomly observed ABF welder Hua Qiang Hwang continuing to perform 3G (vertical) Shielded Metal Arc Welding (SMAW) complete joint penetration (CJP) welding root pass to cover pass on the stiffener splice butt joint. The stiffener plates being welded are made of high strength plate material HPS 485W and has a thickness of 30mm. The joint has a double V joint preparation that was welded from one side and after the completion from one side, to be back gouged; Non Destructive Testing (NDT) tested using Magnetic Particle Testing (MT) and back welded to the other side. The welder was noted using E9018H4R with 1/8" diameter electrode implementing Caltrans approved welding procedure specification (WPS) ABF-WPS-D1.5-1012-3. The joint being welded was root welded using a ceramic backing. The splice joint was preheated to greater than 200 degrees Fahrenheit using Miller Proheat 35 Induction Heating System heater blanket located at the opposite side of the plate prior/during welding. The QA Inspector noted the ABF QC Fred Von Hoff was on site monitoring the in process preheats and welding parameters. During the shift, QA noted ABF QC Fred Von Hoff was closely monitoring the issuance of E9018H4R electrodes due to its limited exposure time allowed. During the shift, cover pass welding on both sides of the stiffener was completed and the welder was instructed by QC to hold the preheat of 200 ° F for three more hours after welding as required. The welder has moved to LS3 of the same OBG location and started welding root pass. Prior welding, QA performed verification on the fit up of the joint. The root gap was noted less than 3mm and the alignment was measured less than 2mm. The welder continued welding fill pass until the end of the shift.

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

QA randomly observed ABF/JV qualified welders Rory Hogan (ID #3186) and Jeremy Dolman (ID #5042) perform CJP groove (splice) back welding cover pass on Orthotropic Box Girder (OBG) 9E/10E side plate 'E1' outside. The welder was observed welding in the 4G (overhead) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3110-4. The welder was using a track mounted welder holder assembly that was remotely controlled. The joint being welded has the backing bar gouged using the Esab Plasma Arc machine and was ground smooth. The gouged and ground splice butt joint was also Non Destructive Testing (NDT) tested using the Magnetic Particle Testing (MT). The splice joint was preheated to greater than 150 degrees Fahrenheit using Miller Proheat 35 Induction Heating System located on top of the plate prior and maintained the preheat by moving the heater blankets on the side of the plate during welding. The vicinity was also properly protected from wind and other climatic changes. During welding, ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters of the welder. During the shift, cover pass welding at location mentioned above was completed and the welder has moved to side plate 'E2' of the same OBG and back welded fill pass until the end of the shift.


At OBG 10W/11W side plate 'E' (0mm to 700mm) inside, QA randomly observed ABF/JV qualified welder Jorge Lopez perform root pass cover pass welding on the Complete Joint Penetration (CJP) splice butt joint where the track mounted Bug-o welder nozzle holder has limited access. The welder was observed manually welding in the 3G (vertical) position utilizing a Shielded Metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1040B. The joint being welded has a single V-groove butt joint with steel backing bar. During welding, ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters of the welder. During the shift, cover pass SMAW welding was completed and the welder has ground flush the weld cover reinforcement which was also completed at the end of the shift.

At OBG 10W/11W edge plate 'B' inside, QA randomly observed ABF/JV qualified welder Fred Kaddu ID # 2188 perform CJP groove welding repair. The welder was observed welding in the 3G (vertical) position utilizing Shielded Metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode implementing welding procedure ABF-WPS-D15-1001-Repairs. The repair excavations were preheated to more than 140 degree Fahrenheit using propane gas torch prior welding. During the shift, ABF QC William Sherwood was noted monitoring the welder. Prior welding, ABF QC William Sherwood was also observed performing Magnetic Particle Testing (MT) on the repair excavation. There was no defect noted during the test. At the end of the shift, welding repair at the two locations was completed and visually accepted by ABF QC. QA noted parameter during welding was 135 amperes which appears in compliance to the WPS. The locations of the repairs were noted below;

Location	Y-dimension	Length	Width	Depth	Remarks
1. B (inside)	30mm	90mm	25mm	18mm	Completed (R1)
2. B (inside)	1080mm	130mm	22mm	16mm	Completed (R1)

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

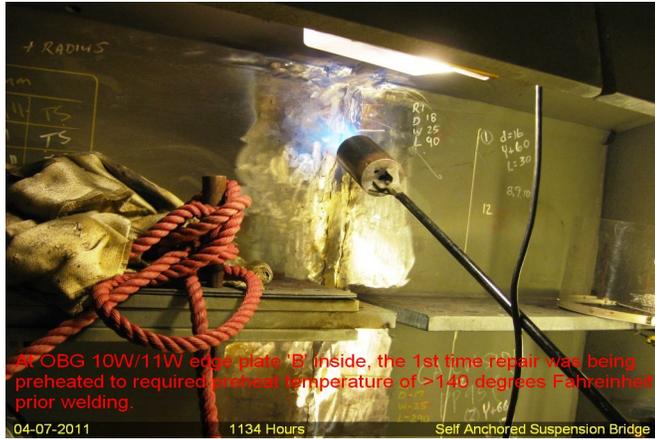

Summary of Conversations:

No significant conversation occurred today.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Nina Choy 510-385-5910, who represents the Office of Structural Materials for your project.

Inspected By: Lizardo, Joselito

Quality Assurance Inspector

Reviewed By: Levell, Bill

QA Reviewer
