

**DEPARTMENT OF TRANSPORTATION**

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch  
 690 Walnut Ave. St. 150  
 Vallejo, CA 94592-1133  
 (707) 649-5453  
 (707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Siegenthaler, Peter**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-023662**Date Inspected:** 16-May-2011**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1730**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site**CWI Name:** Steve Jensen**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** SAS Tower**Summary of Items Observed:**

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

At Tower West Shaft Splice #1 @Elevation 50.3meters:

At Northwest (C-D) corner, lower splice plate; this QA Inspector randomly observed ABF welding personnel Salvador Sandoval (#2202) continuing to perform production welding on the top half of the splice plate using the self shielded Flux Cored Arc Welding (FCAW) process. This QA Inspector observed a propylene gas torch was being used to preheat areas prior to welding. This QA Inspector observed QC Inspector Steve Jensen using an infra red temperature gauge to verify the preheat temperature of more than 300°F. This QA Inspector performed a verification of the welding parameters and observed 265 amperes and 22.0 volts with a travel speed of 95 mm per minute with equivalent heat input of 3.68 KJ per mm. The welding appeared to comply with Welding Procedure Specification (WPS) ABF-WPS-D15-F2200-3. The welder continued fill pass fillet welding on both sides of the plate until 1700hours. Before the end of the shift, the welder has stopped fillet welding and ABF personnel were noted covering the weld with heater blanket in preparation for the three hours holding of preheat temperature of more than 300°F as required. ABF personnel were using Miller Proheat 35 Induction Heating System to hold the preheat that was programmed to shut off after three hours.

At Tower West Shaft Splice #1 @Elevation 50.3meters:

---

## WELDING INSPECTION REPORT

( Continued Page 2 of 3 )

---

At West (B-C) corner, lower splice plate; This QA Inspector randomly observed ABF welding personnel Morgan Winters continuing to perform production welding on the bottom half of the lower splice plate using the self shielded Flux Cored Arc Welding (FCAW) process. This QA Inspector observed ABF personnel using a propylene gas torch on areas prior to welding. This QA Inspector observed QC Inspector Steve Jensen using a Fluke infra red temperature gauge to verify the preheat temperature of more than 300°F. This QA Inspector performed a verification of the welding parameters and observed 244 amperes and 19.8 volts with a travel speed of 95 mm per minute with equivalent heat input of 3.05 Kj per mm. The welding appeared to comply with Welding Procedure Specification (WPS) ABF-WPS-D15-F2200-3. At the end of the shift, fillet welding was still continuing and should remain tomorrow. Before the end of the shift, at around 1700hours, ABF personnel were noted covering the weld with heater blanket in preparation for the three hours holding of preheat temperature of more than 300°F as required. ABF personnel were using Miller Proheat 35 Induction Heating System to hold the preheat that was programmed to shut off after three hours.

At Tower North Shaft Splice #1 @Elevation 50.3meters:

At Northeast (B-C) corner, lower splice plate; This QA Inspector randomly observed ABF welding personnel Rick Clayborn perform production welding on the top half of the lower splice plate using the self shielded Flux Cored Arc Welding (FCAW) process. This QA Inspector observed ABF personnel using a propylene gas torch on areas prior to welding. This QA Inspector observed QC Inspector Steve Jensen using a Fluke infra red temperature gauge to verify the preheat temperature of more than 300°F. This QA Inspector performed a verification of the welding parameters and observed 270 amperes and 22.0 volts with a travel speed of 100 mm per minute with equivalent heat input of 3.56 Kj per mm. The welding appeared to comply with Welding Procedure Specification (WPS) ABF-WPS-D15-F2200-3. At the end of the shift, fillet welding was still continuing and should remain tomorrow. Before the end of the shift, at around 1700hours, ABF personnel were noted covering the weld with heater blanket in preparation for the three hours holding of preheat temperature of more than 300°F as required. ABF personnel were using Miller Proheat 35 Induction Heating System to hold the preheat that was programmed to shut off after three hours.

At Tower East Shaft Splice #1 @Elevation 50.3meters:

At Tower East Shaft, East (B-C) corner and Southeast (C-D) corner, ABF welder Richard Garcia was observed performing fit up of the lower splice plates to interior corner closure plate. The welder has tack welded various temporary attachments using SMAW to the interior corner closure plate and used wedges to hold the lower splice plates in place. The welder was also noted preheating the plates to more than 225°F prior welding. ABF QC Steve Jensen was noted at site monitoring the welder and his welding parameter. At the end of the shift, the fit up of the splice plates at location mentioned above was completed.

At the request of Quality Control Field Supervisor, Bonifacio Daquinag, QA has randomly verified the QC MT of the fillet welding of four (4) splice plates. The QA verification was performed to verify that the welding and the MT inspection performed by the QC inspector meet the requirements of the contract documents. At the conclusion of the QA verification it appeared that the weld and the QC inspection complied with the contract documents.

1. Tower South Shaft Elev. 50.3meters Southwest (B-C) corner upper splice – QA MT verified



---

# WELDING INSPECTION REPORT

( Continued Page 3 of 3 )

---

2. Tower South Shaft Elev. 50.3meters Southwest (B-C) corner lower splice – QA MT verified
3. Tower South Shaft Elev. 50.3meters South (C-D) corner upper splice – QA MT verified
4. Tower South Shaft Elev. 50.3meters South (C-D) corner lower splice – QA MT verified

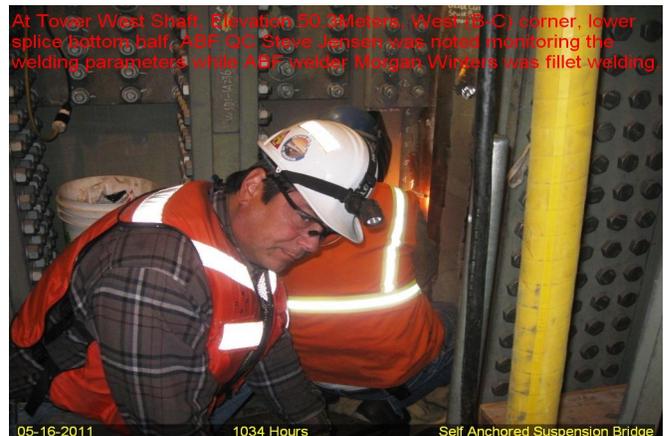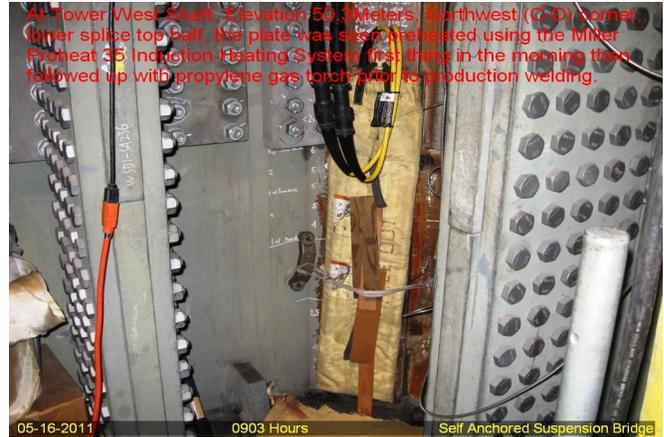

## Summary of Conversations:

No significant conversation occurred today.

## Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Nina Choy 510-385-5910, who represents the Office of Structural Materials for your project.

---

**Inspected By:** Lizardo, Joselito

Quality Assurance Inspector

---

**Reviewed By:** Levell, Bill

QA Reviewer
