

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave. St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Casey, William**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-027789**Date Inspected:** 18-Jun-2012**Project Name:** SAS Superstructure**OSM Arrival Time:** 700**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1730**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job site**CWI Name:** As Noted Below**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG/Tower**Summary of Items Observed:**

Quality Assurance Inspector (QA) Rodney Patterson was at the American Bridge/Fluor (ABF) job site at Yerba Buena Island in California between the times noted above in order to monitor Quality Control functions and the in process work being performed by ABF personnel. The following items were observed:

OBG 13E Deck Drop-in (Panel Point 122~122.5)

This QA observed ABF/JV QC inspector Salvador Merino and John Pagliero performing final visual inspection of the completed web and flange splices for the deck panel drop-in from Panel Points 122~123.5 at E2. The ABF welding personnel then performed minor grinding and weld repairs in way of the weld toe and reinforcement for the areas marked to ensure visual compliance.

OBG 13E Deck Drop-in Repairs

The QA inspector observed at random intervals, ABF/JV qualified welder Steve Davis #7889 performing Shielded Metal Arc Welding (SMAW) in the 4G position utilizing the Caltrans approved Welding Procedure Specification ABF-WPS-D1.5-1004. The welding observed was for the repair of the deck panel drop-in splice weld previously rejected by Ultrasonic Testing (UT) by ABF QC personnel. The repair surface and surrounding area was brought to temperature by the use of induction heaters from the topside of the deck as seen in the attached photograph. The preheat temperature was confirmed ABF personnel prior to welding. The Quality Control (QC) inspector Salvador Merino was observed monitoring the welding parameters at the start of welding. Weld is designated as 13E-E2.8. The weld repairs observed were performed at the following locations during the QA inspectors;

WELDING INSPECTION REPORT

(Continued Page 2 of 3)

Y=11145mm, Depth 6mm, Length=40mm

Y=10790mm, Depth 10mm, Length=100mm

Y=10600mm, Depth 6mm, Length=100mm

OBG 13E Deck Drop-in (Panel Point 123)



The QA inspector observed later in the shift, ABF/JV qualified welder Richard Garcia #5892 performing Shielded Metal Arc Welding (SMAW) in the 2G and 3G position utilizing the Caltrans approved Welding Procedure Specification ABF-WPS-D1.5-1080-R1. The weld is a Complete Joint Penetration tie bracket between the horizontal and vertical floor beam flange at panel point 123 and is designated as 13E-PP123-E2.1-BR1. The weld surface and surrounding area was brought to temperature by the use of a gas torch and the preheat temperature was confirmed ABF personnel prior to welding as seen in the attached photograph. The Quality Control (QC) inspector Salvador Merino was observed monitoring the welding parameters at the start of welding. The welding from face "A" was observed to be completed prior to the end of the QA inspectors shift and will require back gouging of the root at a later date.

This QA spent a portion of this reviewing and documenting the status and completion of various production welding tracking logs for lift 13E/14E drop-in deck work currently in-process. The QA recorded the information on the OBG tracking log.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

Summary of Conversations:

No relevant conversations.

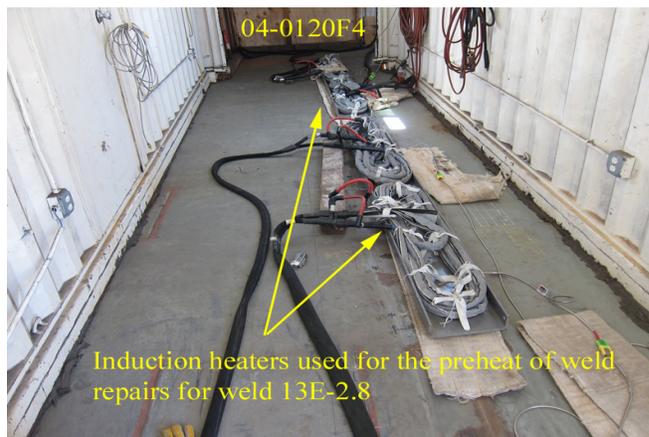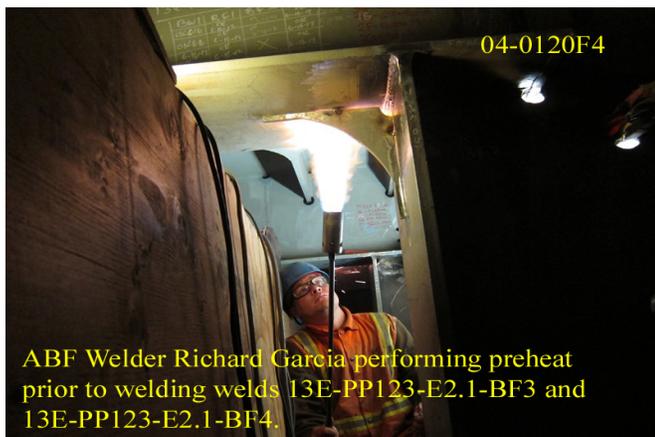

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Nina Choy 510-385-5910, who represents the Office of Structural Materials for your project.

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

Inspected By: Patterson,Rodney

Quality Assurance Inspector

Reviewed By: Levell,Bill

QA Reviewer
