

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 11:51 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 069 Const Calendar Day: 241 Date: 07-May-2010 Friday

Inspector Name: Wilcox, Jason Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 06:30 am 05:00 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Jefferson, Paul Approved Date: 13-Jan-12 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 50 - 60 4PM 50 - 60**Precipitation****Condition** Partly CloudWorking Day ☒ If no, explain:**Diary:**

Dispute

OBG Bolting & Welding**FIELD WORK:**☐**E-LINE:**

- * Observed progress on 4E/5E splice. All U-ribs are pretensioned, Step 1B status around the rest of the splice, (4 Bottom Plate stiffeners, 6 Side Plate stiffeners, and Longitudinal Diaphragms pinned and bolted with temp bolts).

- * Documented locations with bolts installed after arriving from China, (shoring locations on the Bottom Plate stiffeners).

- * Lift 6E was picked and set this morning

W-LINE:

See Thanh Le and David Chung's diaries for more details.

Splice 1:

- * Welding of the Bottom Plate

- * Back weld preparation at the North Side Panel

OFFICE WORK:

- * Met with Tai-Lin Liu and Paul Jefferson to discuss Punchlist item #1704, (Crossbeam stiffener alignment in CB3).

- * Diary review

Accrued 2 hours of overtime covering the Contractor's hours and documenting the days operations.

04-0120F4 Bid Item: 056 W-L01-OBG.056 W Line Lift 01 OBG Erect structural steel (bridge box girder)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 W-L02-ALB.056 W Line Lift 02 Align & Bolt

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Wilcox, Jason

Diary #: 069

Date: 07-May-2010 Friday

04-0120F4 Bid Item: 056 W-L02-WEL.056 W Line Lift 02 Weld
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 W-L03-ALB.056 W Line Lift 03 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 W-L03-WEL.056 W Line Lift 03 Weld
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 W-L04-ALB.056 W Line Lift 04 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 W-L04-WEL.056 W Line Lift 04 Weld
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 E-L02-ALB.056 E Line Lift 02 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 E-L02-WEL.056 E Line Lift 02 Weld
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 X-L02-CBM.056 E-W Line Cross Over Lift 02 Cross Beam
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 X-L03-CBM.056 E-W Line Cross Over Lift 03 Cross Beam
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 056 X-L04-CBM.056 E-W Line Cross Over Lift 04 Cross Beam
AMERICAN BRIDGE/FLUOR, A JV




Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Wilcox, Jason Diary #: 069 Date: 07-May-2010 Friday

| | | | |
|-----------------------------|---------------|---------------|-----------------------------|
| 04-0120F4 | Bid Item: 056 | E-L03-ALB.056 | E Line Lift 03 Align & Bolt |
| AMERICAN BRIDGE/FLUOR, A JV | | | |
| 04-0120F4 | Bid Item: 056 | E-L03-WEL.056 | E Line Lift 03 Weld |
| AMERICAN BRIDGE/FLUOR, A JV | | | |
| 04-0120F4 | Bid Item: 056 | E-L04-ALB.056 | E Line Lift 04 Align & Bolt |
| AMERICAN BRIDGE/FLUOR, A JV | | | |
| 04-0120F4 | Bid Item: 056 | E-L04-WEL.056 | E Line Lift 04 Weld |
| AMERICAN BRIDGE/FLUOR, A JV | | | |

Attachment

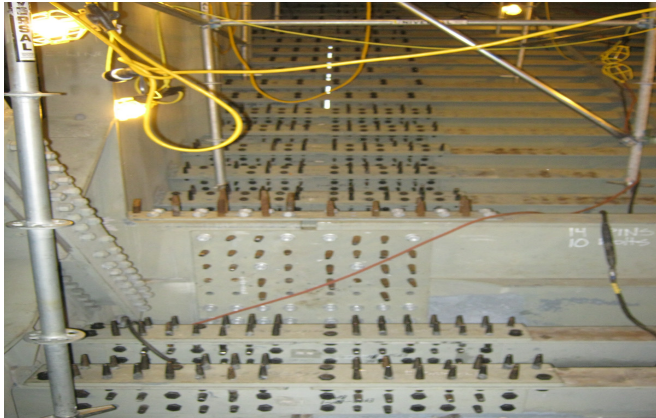

4E/5E South LD w/ Step 1 Pins and Bolts



4E/5E North LD w/ BP stiffeners Step 1



Picking and Placing Lift 6E
