



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:17 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 066 Const Calendar Day: 532 Date: 22-Feb-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☐ If no, explain:

Diary:

Dispute

Work description.

GENERAL WORK

HINGE K FRAMING

The CONCO crews completed the followings:

1. Completed the assembly of bottom frame of the West side by using nails, epoxy, and water sealant tape. The workmanship has been much better than the first time.
2. Either 2 or 3 air vents have been provided for each hinge as shown in the pictures.

Slight leakage has been observed at the East side framing as shown in the picture.


The water testing might be performed tomorrow, they prefer the epoxy and caulking is adequately dry before the test.

CONCO Crews:

- Gary Pene
- Jasmin Goranyac



Attachment

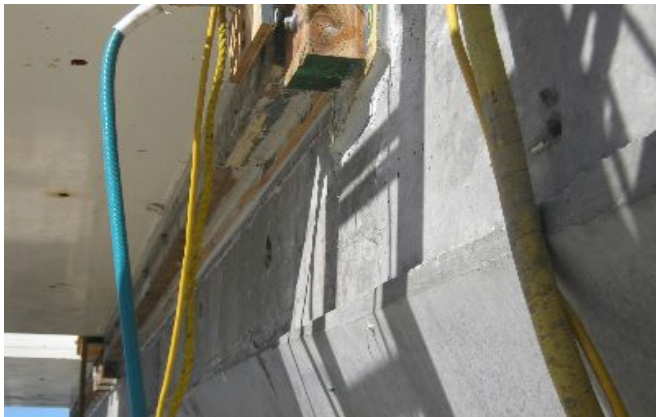

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 066

Date: 22-Feb-2011

Tuesday

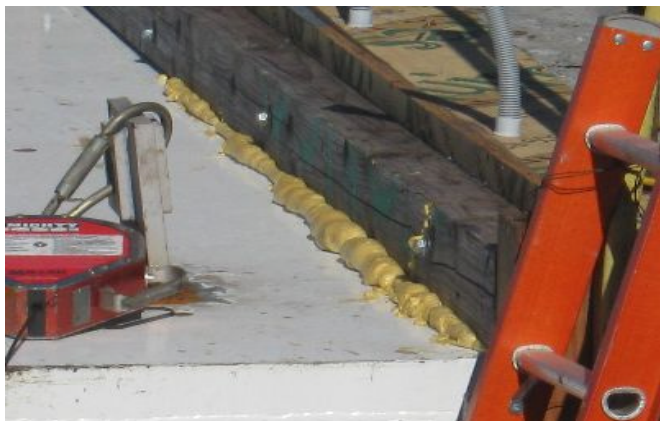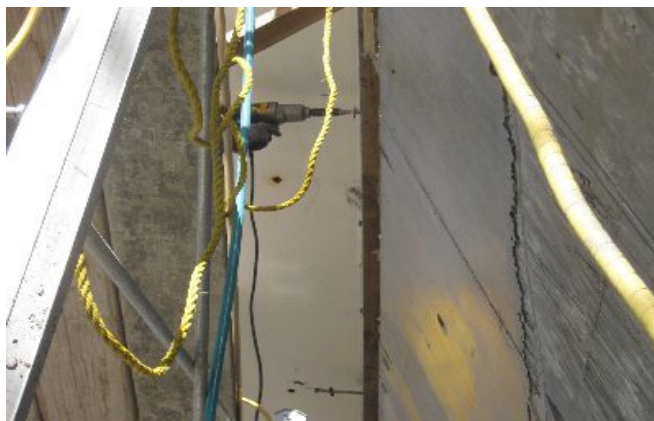

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 066

Date: 22-Feb-2011

Tuesday

