



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:16 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 069 Const Calendar Day: 535 Date: 25-Feb-2011 Friday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☐ If no, explain:

Diary:

Dispute

Work description.

GENERAL WORK

☐

The ABF crews activities:

1. The crew started setting up the facility to gather the washouts from the K- Hinge during grouting to a basin. There is a doubt if ABF can finish the work for both the West and East K-Hinges until Monday February 28,2011.
2. At 1:00 P.M. in the afternoon Bob Brignano and I checked randomly the amount of applied torque to some of the A490 bolts. Some didn't meet the requirement of 1616 lb.ft torque and consequently with the help of three ABF crews the bolts are tightened to the specified torque.
3. Bob has informed the ABF that A490 bolts don't satisfy the specification, either the shaft length is decreased or thicker washers are used. ABF has stopped installing more bolts and the West side are untouched.

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 069

Date: 25-Feb-2011

Friday

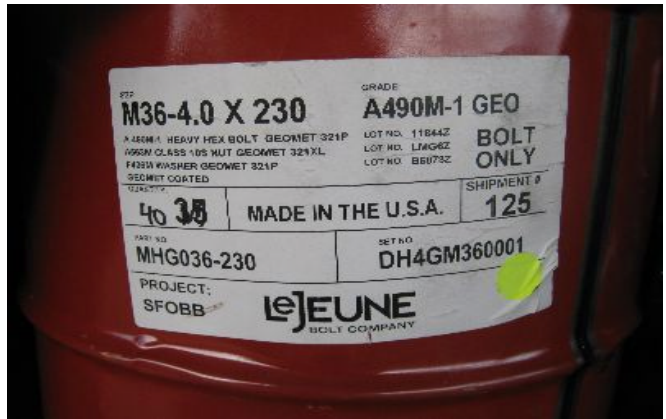

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 069

Date: 25-Feb-2011

Friday

