

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:11 AM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 079 Const Calendar Day: 553 Date: 15-Mar-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather**

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☐ If no, explain:**Diary:**

Dispute

**Work description.**

GENERAL WORK

HINGE K FRAMING REMOVAL

The CONCO crews activities:

1. The CONCO crews removed the forms of the West line hinge. As shown in the pictures there is one location under the West hinge of the West line the grout has minor issue. The cavities seem to be due to some debris remained in the formwork and settled at the bottom during 24 hours water soaking. In general, the quality of the West line grouting appears to be in a good condition, which requires minor repairs.

The ABF crews activities:

2. The ABF crews were involved in the refined adjustment of the West line deviation saddle.

CONCO Crews:

- Gary Pene
- Jasmin Goranyac

ABF Crews:

- Kubala, Jerry (IWF)
- Hernandez, walter (IWJ)
- Hernandez, Roberto (IWJ)
- Calzascia, Jonny (IWJ)
- Melgar, Felix (Laborer)
- James Allen (Surveyor)
- Bob Andres (Surveyor)

Equipment:

- Man lift

**Attachment**

ddrRptbyBidItem

## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 079

Date: 15-Mar-2011

Tuesday

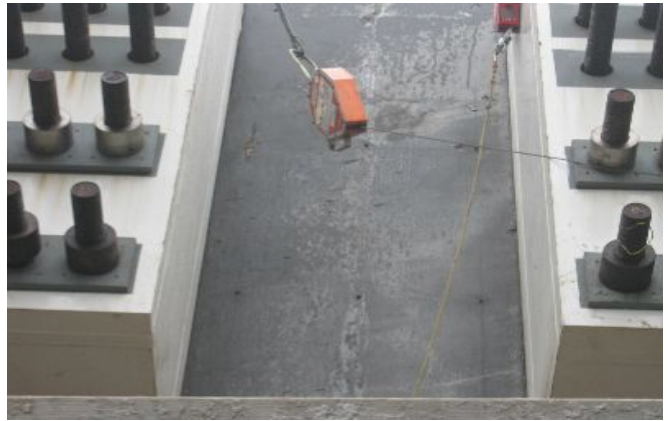



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 079

Date: 15-Mar-2011

Tuesday

