



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:10 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 080 Const Calendar Day: 554 Date: 16-Mar-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☐ If no, explain:

Diary:

Dispute

Work description.

GENERAL WORK

HINGE K- PATCHING THE GROUT CAVITIES

The CONCO crews activities:

1. The CONCO crews patched the holes in the grout at both the East and West line K hinge with 55 pounds bag of Masterflow 928 grout mix with the amount of water less than 10.5 pounds in order to be thick enough to patch the cavities.
2. The curing compound applied at the patched locations.
3. The crew also disassembled the scaffolding, which was set-up in the hinge K grouting process.
4. The crew started moving the needed material for scaffolding to the East line deviation saddle.
5. The Hydraulic jacks were in place at the West line deviation saddle, but with no activity.

CONCO Crews:

- Gary Pene
- Jasmin Goranyac

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 080

Date: 16-Mar-2011

Wednesday

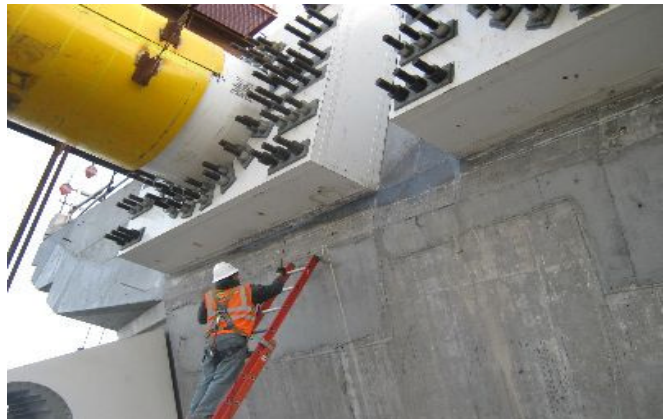

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 080

Date: 16-Mar-2011

Wednesday

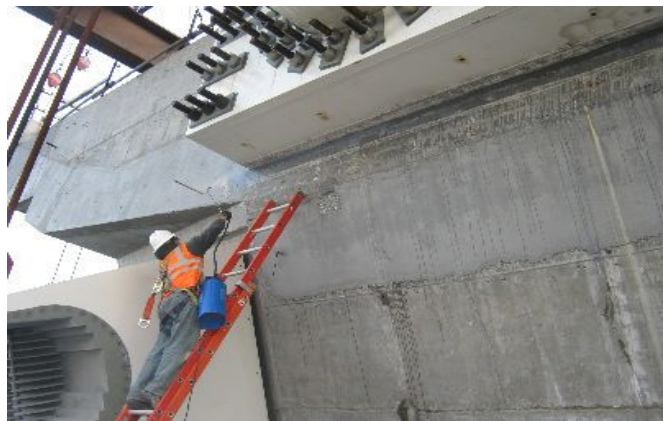

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 080

Date: 16-Mar-2011

Wednesday

