



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:07 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 090 Const Calendar Day: 568 Date: 30-Mar-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☐ If no, explain:

Diary:

Dispute

Work description.

ABF crews activities:


The ABF surveyor, James Allen, has reached to different coordinates for the specified locations on the saddles from two different benchmarks. He believes that refraction or existence of the MCM cables has caused in having two different values. All these saddle locations have been specified in the submittal ABF-SUB-1684R02.

He mentioned that is needed to repeat the surveying since it is not known which benchmark caused the error. It is not known clearly when the adjustment of the saddles is finalized.

ABF Crews:

- James Allen (Surveyor)
- Bob Andres (Surveyor)

Attachment

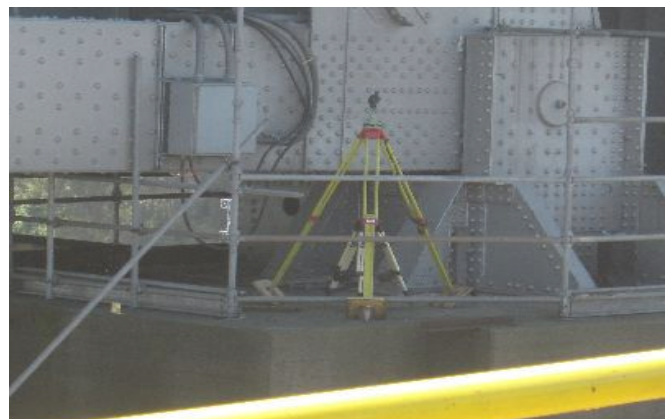

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 090

Date: 30-Mar-2011

Wednesday

