

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:57 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 107 Const Calendar Day: 591 Date: 22-Apr-2011 Friday
Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer
Inspection Type: Intermittent
Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
Federal ID:
Location:
Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70
Precipitation None Condition

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

CONCO Crews activities:

The crews started water testing of the East Line saddle form early in the morning. When the adequate water pressure was built up inside the form, the water started to leak at a high rate at different locations. That shows that the main timber of the form is not adequately sealed off to prevent the leakage. The sealing tape that has been used is about 12mm x 4 mm, which cannot adequately seals off any opening, since the concrete surface is not very smooth and straight. CONCO should have used wider and thicker sealing tape to block any water seepage. Both of the contact surfaces, between the form and the saddle, and the form and the pier W2 concrete surface are not watertight. After the test the crew started to fix the leakage locations by adding extra strip of woods with the help on nailing and caulking. There is a doubt that these repairs can solve the leakage issue. The West Line saddle form is going to be tested on Monday April 25, 2011.

CONCO Crews:

-Gary Pene
-Jasmin Gorinjac

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

CONCO PUMPING

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	CONCO PUMPING							
		Gorinjac Jasmin	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		Gary Pene	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor:	CONCO PUMPING							
*E0020406						No		<input type="checkbox"/>
		8.00	0.00	0.00	0.00			
*E0010406						No		<input type="checkbox"/>
		8.00	0.00	0.00	0.00			<input type="checkbox"/>

Attachment

ddrRptbyBidItem

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 107

Date: 22-Apr-2011

Friday

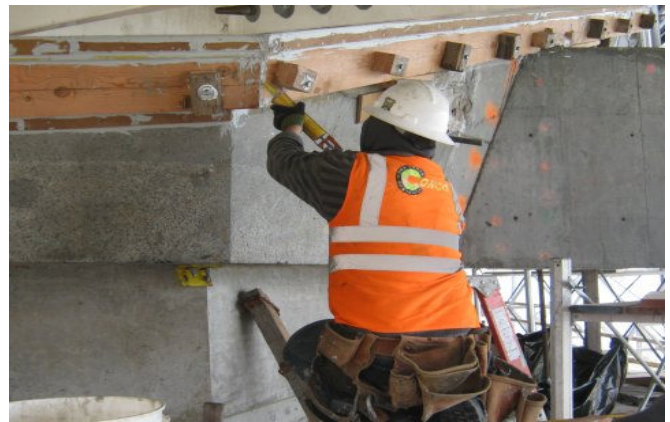

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 107

Date: 22-Apr-2011

Friday

