

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:40 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 139 Const Calendar Day: 639 Date: 09-Jun-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:45 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian

Approved Date:

10-Oct-13 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 70**Precipitation** None **Condition** SunnyWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

ABF crews are gradually completing the assembly of the "SIDE SPAN CATWALK" for the W-line connecting the bracket at the North corner of W2 pier to the saddle lower connection, based on details of the submittal ABF-SUB-2372R00. The crews put in place the side mesh in a folded condition and then connecting it to the bottom grid with helical wires. The leave the side mesh in folded position until the erection of the catwalk is completed. The crews also added the helical wires at the overlap locations of the bottom grid based on the submittal ABF-SUB-2372R00. As shown in the pictures, two types of connections are shown, one for tramway support column and the other for lateral bracing of the catwalk. The side bracing connection was observed at two locations along the length of the catwalk. The frames are secured to the bottom cables with more wires as shown in the pictures.

ABF Crews:

- Matthew Chamberlain (foreman)
- Jack Hunter
- Morris Robertson
- 6 laborers
- Total of nine crews

ABF Equipment:

-Generator ABF # 000009

04-0120F4 Bid Item: 067 C-TPW-CRB.067 Install Catwalk Ropes - Cable System Backspan

AMERICAN BRIDGE/FLUOR, A JV

Attachment

ddrRptbyBidItem

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 139

Date: 09-Jun-2011

Thursday

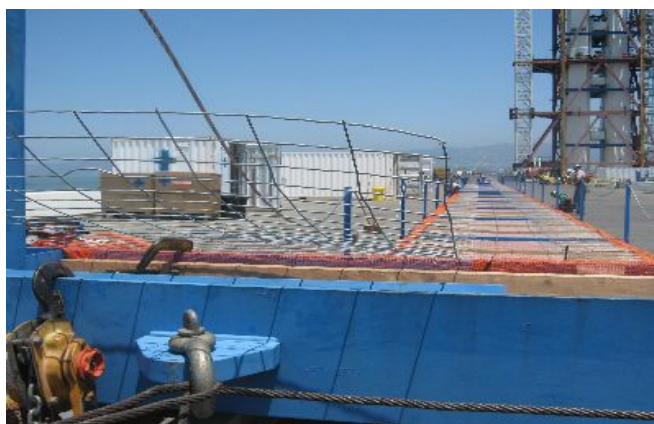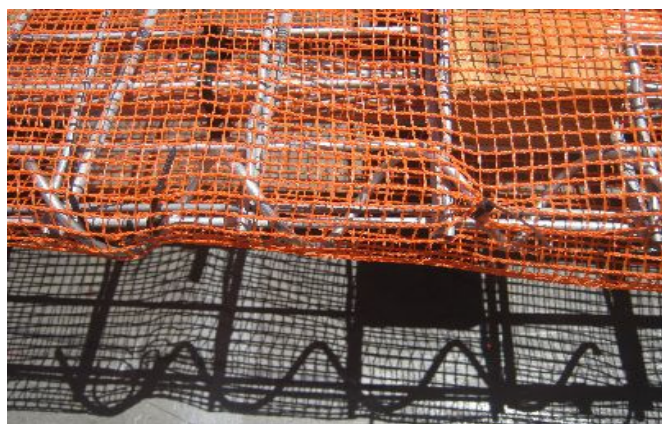

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 139

Date: 09-Jun-2011

Thursday

