



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:34 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 150 Const Calendar Day: 654 Date: 24-Jun-2011 Friday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:45 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian

Approved Date:

10-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70

Precipitation None Condition Sunny

Working Day ☒ If no, explain:

Diary:

Dispute

Work description.



ABF Crews activities:

ABF crews completed the lower catwalk lateral bracing in the morning and two laborers attached colored ribbons to the cables to prevent cutting them by moving equipments on the deck.

ABF Crews:

- Three crews (Only in the morning)
- Two laborers (Only in the afternoon)

ABF Equipments:

- Manlift (Only in the afternoon)

04-0120F4 Bid Item: 067 C-TPW-CRB.067 Install Catwalk Ropes - Cable System Backspan

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 150

Date: 24-Jun-2011

Friday

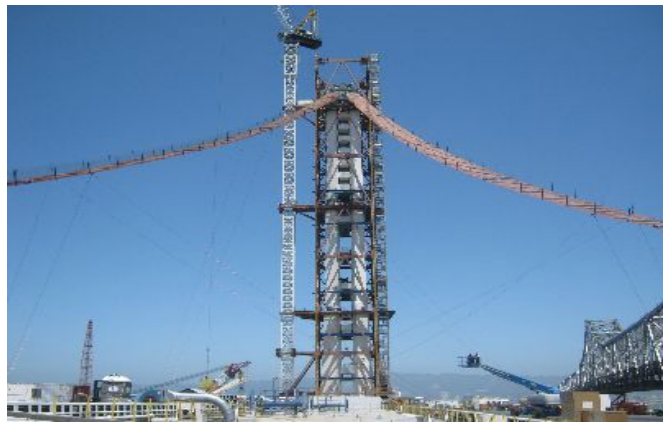

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 150

Date: 24-Jun-2011

Friday

