

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:33 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 155 Const Calendar Day: 706 Date: 15-Aug-2011 Monday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 60 - 70

Precipitation None Condition

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

☐

ABF Crews activities:

The crews continued installing the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2". Some of the frames had some deficiencies and needed welding additional pieces in order the installation become possible. As shown in the pictures, the new pieces are added. The assembled frame system does not have adequate stiffness ABF might improve this system to be adequately stiff during the operation.

ABF crews involved in the PWS secondary hauling system:

- Jerry Kubala
- Im Bandol
- Rigoverta Garcia
- Walter Hernandez
- Melgar Fleix (laborer)
- Scott Ross (crane Operator)
- Ian Murphy
- Rick Clayman

ABF Equipment:

Crane Terex RT160

Miller welding machine

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker		Rick Clayman	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		Im Bandol	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Rental Company




ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Iranmanesh, Abbas **Diary #:** 155 **Date:** 15-Aug-2011 **Monday**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0110406						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00		<input type="checkbox"/>
04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle AMERICAN BRIDGE/FLUOR, A JV							

Attachment

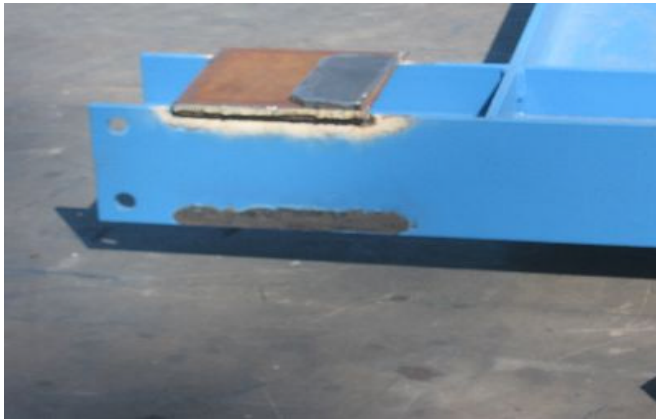

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 155

Date: 15-Aug-2011

Monday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 155

Date: 15-Aug-2011

Monday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 155

Date: 15-Aug-2011

Monday

