

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:31 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 157 Const Calendar Day: 708 Date: 17-Aug-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 2:00

Federal ID:

Location:

Reviewer: Boal, Brian

Approved Date:

10-Oct-13 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 4PM 60 - 70**Precipitation** None**Condition**Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" with some modification of the submittal. The framing system is stiffened longitudinally by welding new top steel channel section near the end saddles and a cross bracing with steel angle sections is added between the top and bottom members as shown in the pictures. Besides, a steel pipe section is welded between the front vertical steel members close to the front saddle surface as shown in the pictures. These modifications are being continued for both the East and West line saddle PWS framing system. By these modifications, the PWS framing system becomes very stiff longitudinally along the slope of the saddle.

ABF crews started installing the brackets holding the PWS beam hauling system. The difficulty of installing these brackets is not matching the bracket holes with the anchors driven into the W2 pier. As shown in the pictures forcing to fit the bracket causes bending of the anchor bolts.

NOTE: ABF Labor and Equipment list is not updated.

ABF crews involved in the PWS secondary hauling system

A) Installation crews:

- Jerry Kubala (FOR- Instalation)
- Im Bandal
- Rigovento Garcia
- Walter Hernandez
- Melgar Fleix
- Joseph Stone
- Henry Hernandez
- Kevin Alger (Crane Operator)

B) Welding Crews

- Ian Murphy
- Rick Clayman (FOR- Welding)
- Salvador Sandoval

C) Miscellaneous

- Jose Avila (Laborer)
- Jose Avalos (Laborer)



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Iranmanesh, Abbas Diary #: 157 Date: 17-Aug-2011 Wednesday

ABF Equipment:
Crane Terex RT160
Miller welding machine (ABF002242)
Lincoln Welding machine (ABF002082)
.

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	JOSE AVALOS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	JOSE AVILA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
		Im Bandoi	8.00	2.00	0.00	10.00		<input type="checkbox"/>
		Rick Clayman	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
2154	EQUIPMENT, CRANE, 60 TON	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
002242	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 157

Date: 17-Aug-2011

Wednesday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 157

Date: 17-Aug-2011

Wednesday

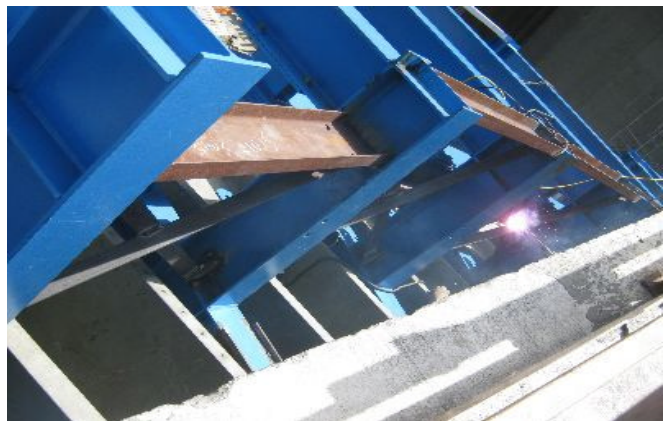

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 157

Date: 17-Aug-2011

Wednesday

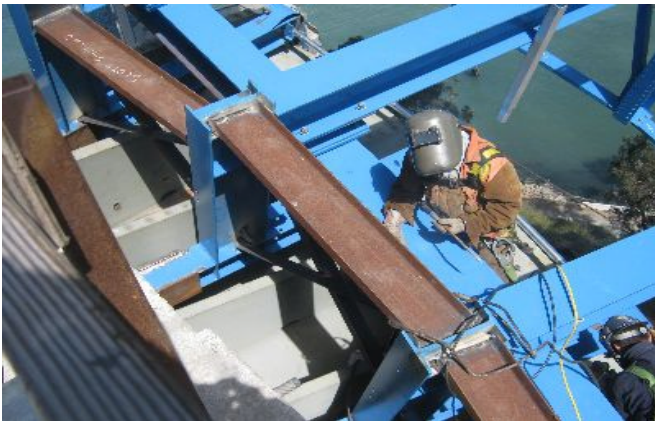

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 157

Date: 17-Aug-2011

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 157

Date: 17-Aug-2011

Wednesday

