

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:24 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 169 Const Calendar Day: 722 Date: 31-Aug-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 70**Precipitation** None**Condition** partly cloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and Primary PWS with respect to submittal ABF-2312R00, "Primary PWS Hauling System", as follows:

INSTALLATION:

- The winch was positioned based on the drawing No.DE431AB of the submittal ABF-SUB-2283R00.
- The leveling of the winch was a time consuming process, since the underneath pier 2 deck concrete surface was not level. The leveling was accomplished by positioning shims with variable thickness at different locations under the winch frame.
- After installing the frame, the winch with its chase was pulled out in order to grout underneath the frame as shown in the drawing No.DE431B of the submittal ABF-SUB--2283R00.
- The ABF crew continued tightening the bolts of the framing of the secondary hauling system and primary sheave brackets by the impact gun and adjusting pieces which had shop defects.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in Secondary hauling system

Installation crew:

- Jerry Kubala (FOR- Installation)
- Walter Hernandez
- Melgar Fleix
- Rigoverta Garcia
- Patrick Oleary
- Scott Ross (Crane Operator)
- Clinton Montgomery (Fork Lift Operaor)

ABF Equipments:

- Crane Terex RT160(Idle in the afternoon for maintainance)
- Fork Lift

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 169 **Date:** 31-Aug-2011 **Wednesday**

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	PATRICK OLEARY	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
000437	FORKLIFT, GRADALL 544D 10,000 LBS	1.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton	6.00	0.00	0.00	0.00		No	<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 169

Date: 31-Aug-2011

Wednesday

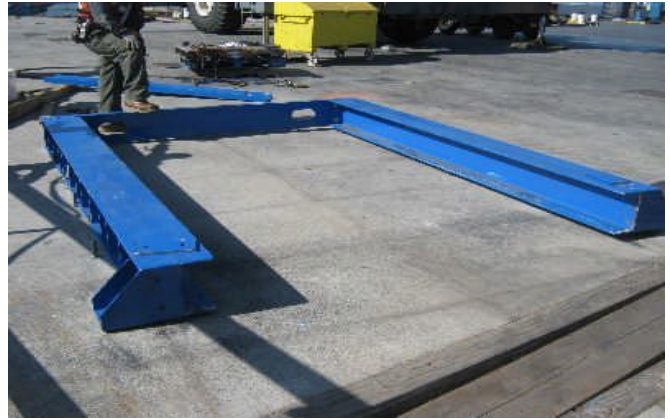

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 169

Date: 31-Aug-2011

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 169

Date: 31-Aug-2011

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 169

Date: 31-Aug-2011

Wednesday

