

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:16 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 178 Const Calendar Day: 736 Date: 14-Sep-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70
Precipitation None **Condition** Partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- ABF crews completed the installation of the UHMWP (Ultra High Molecular Weight Polyethylene) 6 mm thick Plates using ¼" countersunk screw on the North side of Pier W2 (W-Line saddle frames) and continuing the installation of the UHMWP plates on the frames between the two saddles. The Detail 20 on the drawing sheets No. DE419OT of the submittal ABF-SUB-2171R01.
- ABF crews completed installation of the side rollers on the framing system between the two saddles. Sheet drawing DE419PT, Sheet drawing DE419QT, Sections A, B & D, Sheet drawing DE419RT, Detail 24 & Section A of the submittal ABF-SUB-2171R01.
- The ABF crews continuing installation of the HSS 76x76 galvanized posts with respect to drawing sheet No.DE419PT of the submittal ABF-SUB-2171R01 by cutting the plywood deck of the falsework and welding the posts to the steel beam of the falsework. Due to existence of 2"x6" timber beams the end plate of the posts were cut to fit the post end plate to the existing condition. 20 HSS 76x76 galvanized posts have been installed two more posts are left to be completed.

SCAFFOLDING:

- ABF crews continuing the assembly of the scaffolding at the E-line saddle, at the South side of pier W2.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in Secondary hauling system

Installation crew:

- Jerry Kubala (FOR.- Installation)
- Walter Hernandez
- Melgar Fleix
- Rigoverto Garcia
- Ian Murphy



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 178 **Date:** 14-Sep-2011 **Wednesday**

- Rick Clayborn
-Victor Hernandez
-Clinton Montgomery (crane Operator)

ABF crew involved in the assembly of the scaffolding:

-Obra Paulk (FOR.)
-Michael Balwinski
-Ryan Nash
-Dusten Clayborn
-Barry Rothman
-pablo Ramirez
-Carlos Bustomante

Equipments

-Groove Crane (ABF002363)
- Miller welding machine (ABF-002303)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	IAN MURPHY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	OBRA PAULK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CARLOS BUSTAMANTE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	PABLO RAMIREZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DUSTEN CLAYBORN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RYAN NASH	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL BALWINSKI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	CLINTON MONTGOMERY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0210406	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			
*E0200406							No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday

04-0120F4



Bid Item: 060

X-W2C-JKS.060

E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment

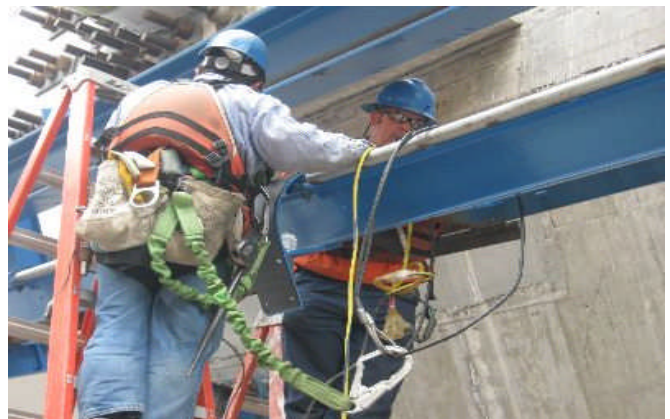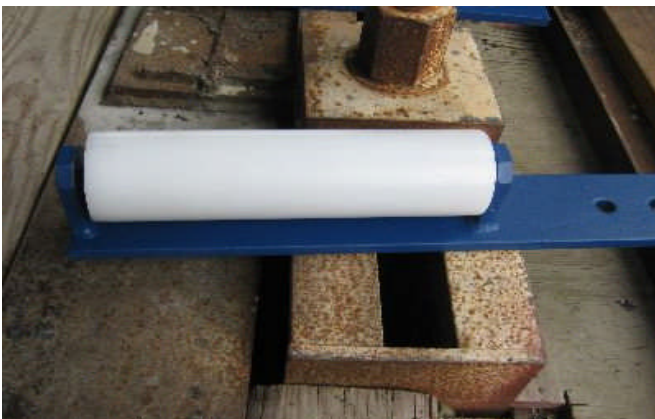

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday

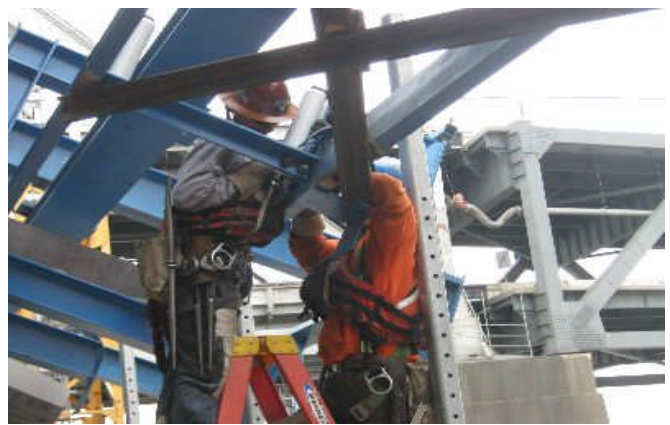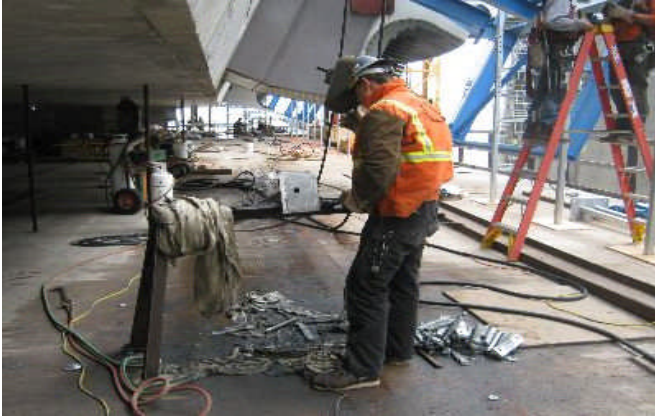

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday

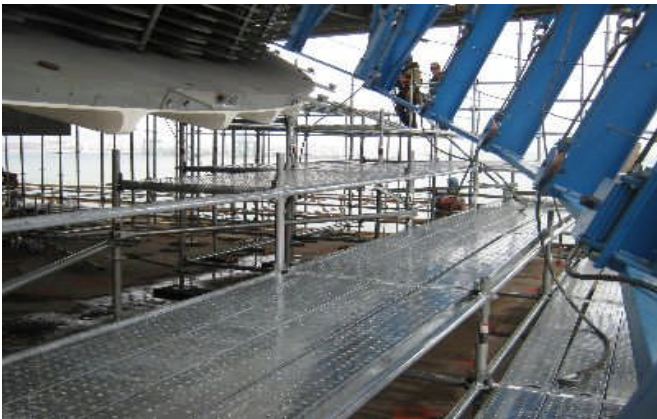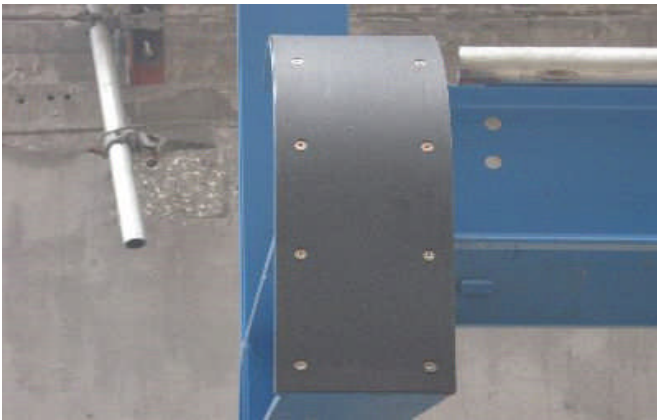

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 178

Date: 14-Sep-2011

Wednesday

